

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only (Revised 7-1-15) Zoning Official _____ Building Official _____
 AP# 13514 Date Received 12/4 By EW Permit # _____
 Flood Zone _____ Development Permit _____ Zoning _____ Land Use Plan Map Category _____
 Comments _____

FEMA Map# _____ Elevation _____ Finished Floor _____ River _____ In Floodway _____
☐ Recorded Deed or ☐ Property Appraiser PO ☐ Site Plan ☐ EH # _____ ☐ Well letter OR
☐ Existing well ☐ Land Owner Affidavit ☐ Installer Authorization ☐ FW Comp. letter ☐ App Fee Paid
☐ DOT Approval ☐ Parent Parcel # _____ ☐ STUP-MH _____ ☐ 911 App
☐ Ellisville Water Sys ☐ Assessment _____ ☐ Out County ☐ In County ☐ Sub VF Form


Property ID # 28-35-16-02376-000 Subdivision FIVEASH FOREST Lot# 35

- New Mobile Home ☒ Used Mobile Home _____ MH Size 28x66 Year 2024
- Applicant MARK S. GOODSON Phone # 386-303-2491
- Address 337 SW TOMPKINS ST LAKE CITY FL 32024
- Name of Property Owner FIVEASH FOREST LLC Phone# 386-752-7207
- 911 Address 396 NW TURNBERRY DR LAKE CITY FL 32055
- Circle the correct power company - FL Power & Light - Clay Electric
 (Circle One) - Suwannee Valley Electric - Duke Energy
- Name of Owner of Mobile Home BARBARA YANCEY Phone # 731-693-5382
 Address 396 NW TURNBERRY DR LAKE CITY FL 32055
- Relationship to Property Owner TENANT
- Current Number of Dwellings on Property 38
- Lot Size 75 X 150 Total Acreage 36
- Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
 (Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)
- Is this Mobile Home Replacing an Existing Mobile Home NO
- Driving Directions to the Property HWY 90 WEST. TURN RIGHT ON BROWN ROAD. GO TO NW TURNBERRY DR. ON RIGHT. FOLLOW TURNBERRY DR. TO LOT 35 ON RIGHT
- Email Address for Applicant: PGOODSON@COMCAST.NET
- Name of Licensed Dealer/Installer DALE HOUSTON Phone # 386-623-6522
- Installers Address 136 SW BARRS GLEN LAKE CITY FL 32024
- License Number IH 1133172 Installation Decal # 106418


Page 2, Site Plan for 9-1-1 Address Application From

1. A PLAT, PLAN, OR DRAWING SHOWING THE PROPERTY LINES OF THE PARCEL.
2. LOCATION OF PLANNED RESIDENT OR BUSINESS STRUCTURE ON THE PROPERTY WITH DISTANCES FROM AT LEAST TWO OF THE PROPERTY LINES TO THE STRUCTURE (SEE SAMPLE BELOW).
3. LOCATION OF THE ACCESS POINT (DRIVEWAY, ETC.) ON THE ROADWAY FROM WHICH LOCATION IS TO BE ADDRESSED WITH A DISTANCE FROM A PARALLEL PROPERTY LINE AND OR PROPERTY CORNER (SEE SAMPLE BELOW).
4. TRAVEL OF THE DRIVEWAY FROM THE ACCESS POINT TO THE STRUCTURE (SEE SAMPLE BELOW).

SAMPLE:

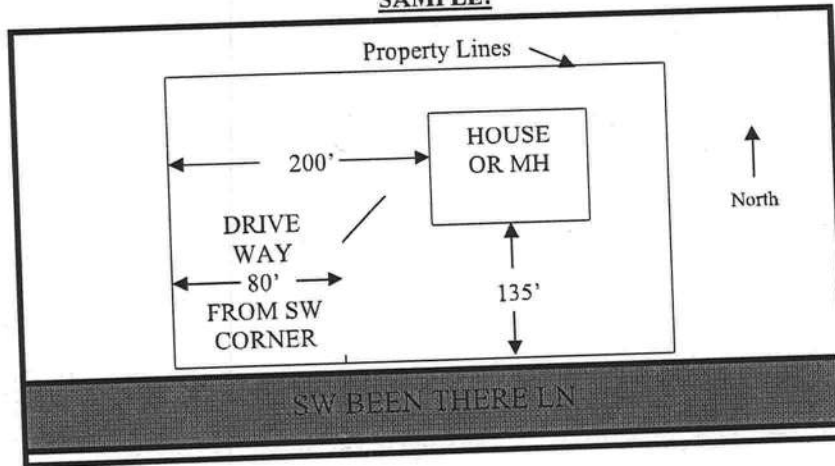

SITE PLAN BOX:

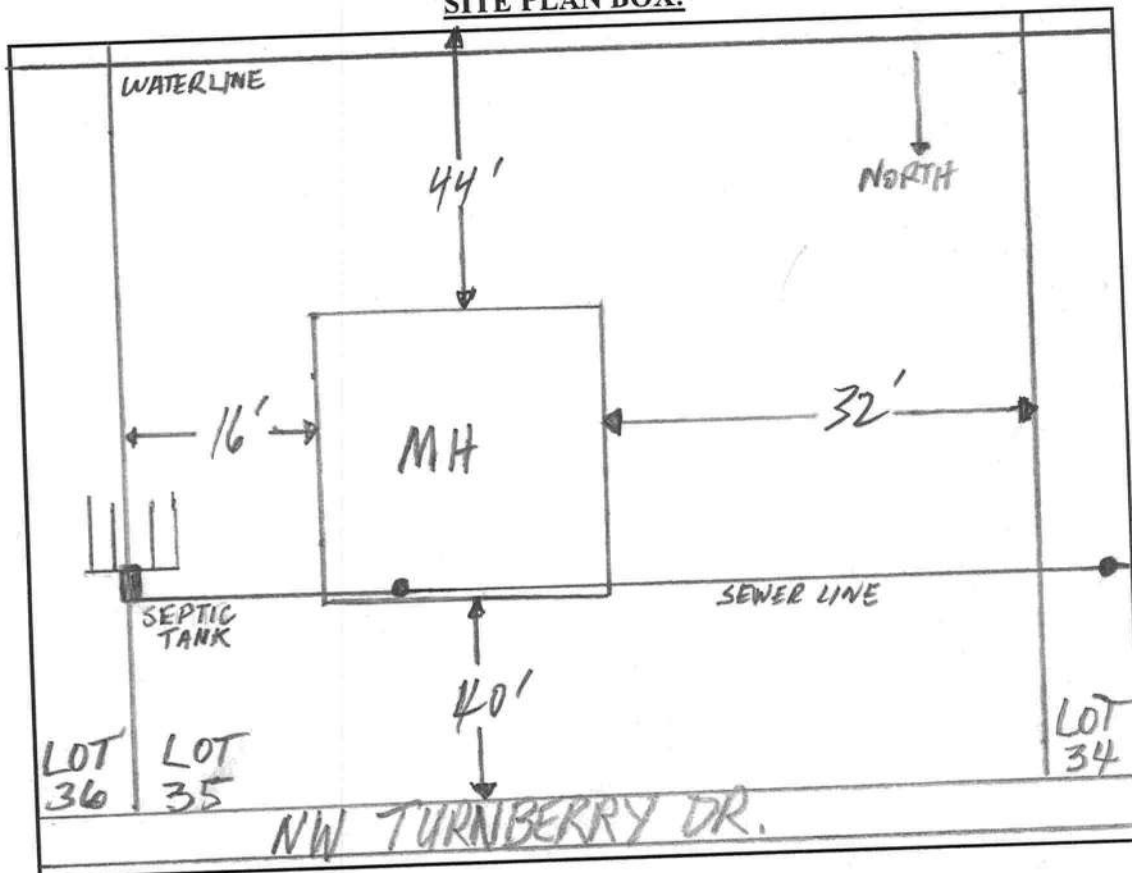



COLUMBIA COUNTY BUILDING DEPARTMENT
135 NE Hernando Ave, Suite B-21, Lake City, FL 32055
Phone: 386-758-1008 Fax: 386-758-2160

MOBILE HOME INSTALLERS LETTER OF AUTHORIZATION

I, DALE HOUSTON, give this authority for the job address show below
Installer License Holder Name

only, 396 NW TURNBERRY DR. LAKE CITY FL 32055, and I do certify that
Job Address

the below referenced person(s) listed on this form is/are under my direct supervision and control
and is/are authorized to purchase permits, call for inspections and sign on my behalf.

Printed Name of Authorized Person	Signature of Authorized Person	Authorized Person is... (Check one)
<u>PATTI H GOODSON</u>	<u>[Signature]</u>	☒ Agent ☐ Officer ☒ Property Owner
<u>MARK S GOODSON</u>	<u>[Signature]</u>	☒ Agent ☐ Officer ☒ Property Owner
		☐ Agent ☐ Officer ☐ Property Owner

I, the license holder, realize that I am responsible for all permits purchased, and all work done
under my license and I am fully responsible for compliance with all Florida Statutes, Codes, and
Local Ordinances.

I understand that the State Licensing Board has the power and authority to discipline a license
holder for violations committed by him/her or by his/her authorized person(s) through this
document and that I have full responsibility for compliance granted by issuance of such permits.


Dale Houston License Holders Signature (Notarized) TH 1183 292 License Number 12-4-23 Date

NOTARY INFORMATION:

STATE OF: Florida COUNTY OF: Columbia

The above license holder, whose name is Dale Houston,
personally appeared before me and is known by me or has produced identification
(type of I.D.) personally known on this 4 day of December, 2023.

[Signature]
NOTARY'S SIGNATURE



MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER _____ CONTRACTOR _____ PHONE _____

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL	Print Name <u>MARK S. GOODSON</u> License #: _____ Qualifier Form Attached ☐	Signature <u>Mark S. Goodson</u> Phone #: <u>386-303-2491</u>
MECHANICAL/ A/C _____	Print Name <u>MARK S. GOODSON</u> License #: _____ Qualifier Form Attached ☐	Signature <u>Mark S. Goodson</u> Phone #: <u>386-303-2491</u>

F. S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

Find address or place



generated on 12/1/2023 11:54:45 AM EST

Last Update: 12/1/2023 11:54:20 AM EST

Register for eBill

The information contained herein does not constitute a title search and should not be relied on as such.

Account Number		Tax Type		Tax Year	
R02376-000		REAL ESTATE		2023	
Mailing Address		Property Address			
FIVE ASH FOREST LLC		355 TURNBERRY LAKE CITY			
337 SW TOMPKINS ST					
LAKE CITY FL 32024		GEO Number			
		283S16-02376-000			
Exempt Amount		Taxable Value			
See Below		See Below			
Exemption Detail		Millage Code		Escrow Code	
NO EXEMPTIONS		002			
Legal Description (click for full description)					
28-3S-16 5028/502836.00 Acres COMM AT NW COR OF MAGNOLIA HILLS, RUN N 1122.85 FT, E 700 FT, N 200 FT, E 562.46 FT, S 1337.12 FT, W 1278.04 FT TO POB. 433-304, WD 1004-584, WD 1056-1951, WD 1070-49, DC 1453-2192,					
Ad Valorem Taxes					
Taxing Authority	Rate	Assessed Value	Exemption Amount	Taxable Value	Taxes Levied
BOARD OF COUNTY COMMISSIONERS	7.8150	408,590	0	\$408,590	\$3,193.13
COLUMBIA COUNTY SCHOOL BOARD					
DISCRETIONARY	0.7480	408,590	0	\$408,590	\$305.63
LOCAL	3.2170	408,590	0	\$408,590	\$1,314.43
CAPITAL OUTLAY	1.5000	408,590	0	\$408,590	\$612.88
SUWANNEE RIVER WATER MGT DIST	0.3113	408,590	0	\$408,590	\$127.19
LAKE SHORE HOSPITAL AUTHORITY	0.0001	408,590	0	\$408,590	\$0.04
Total Millage		13.5914	Total Taxes		\$5,553.30
Non-Ad Valorem Assessments					
Code	Levying Authority	Amount			
FFIR	FIRE ASSESSMENTS	\$9,726.51			
GGAR	SOLID WASTE - ANNUAL	\$0.00			
Total Assessments				\$9,726.51	
Taxes & Assessments				\$15,279.81	
If Paid By		Amount Due			
11/30/2023		\$14,668.62			
12/31/2023		\$14,821.42			
1/31/2024		\$14,974.21			
2/29/2024		\$15,127.01			

3/31/2024	\$15,279.81
-----------	-------------

Prior Years Payment History

Prior Year Taxes Due
NO DELINQUENT TAXES



[Click Here To Pay Now](#)

Mobile Home Permit Worksheet

Installer: Dade Housen License # 2H 1133271
 Address of home being installed: 396 NW Turnberry Dr
Lake City, FL 32055
 Manufacturer: Palm Harbor Length x width: 28 x 70

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home
 I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials: DH

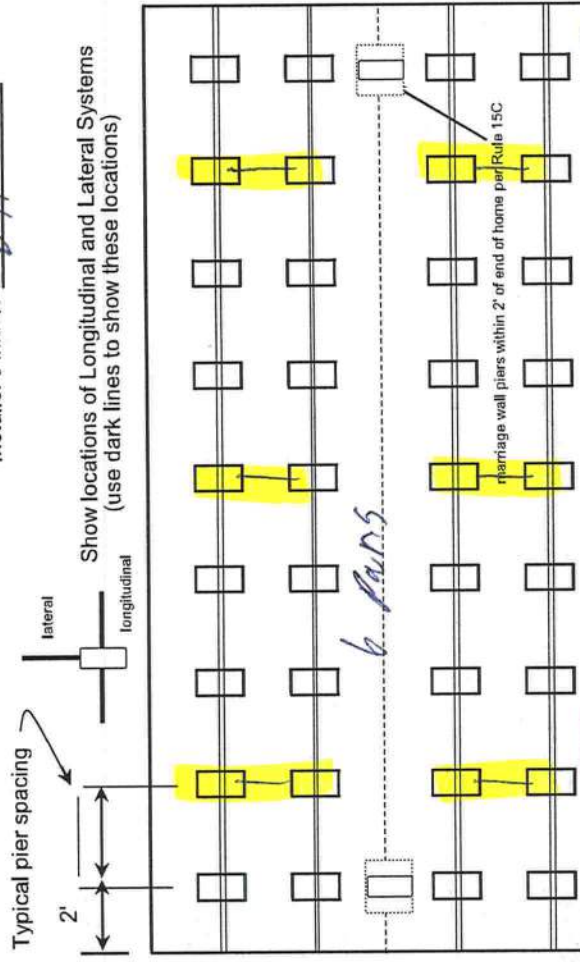

Application Number: _____

Date: 12-4-23

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 106718
 Triple/Quad ☐ Serial # DHH 340FL23-2376SAB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3"	4"	4"	5"	6"	7"	8"
1500 psf	4"	6"	6"	7"	8"	8"	8"
2000 psf	6"	8"	8"	8"	8"	8"	8"
2500 psf	7"	8"	8"	8"	8"	8"	8"
3000 psf	8"	8"	8"	8"	8"	8"	8"
3500 psf	8"	8"	8"	8"	8"	8"	8"

* interpolated from Rule 15C-1 pier spacing table.

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

PIER PAD SIZES 23 x 31

I-beam pier pad size 24 x 24

Perimeter pier pad size 17 x 23

Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening _____ Pier pad size 24 x 31

ANCHORS

4" ☒ 5" ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer _____

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer _____

OTHER TIES

Number

Sidewall

Longitudinal

Marriage wall

Shearwall

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

12-4-23

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil _____ without testing.

X _____ X _____ X _____

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

X _____ X _____ X _____

TORQUE PROBE TEST

The results of the torque probe test is 293 inch pounds or check here if you are declaring 5" anchors without testing _____. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

DH Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name Dale Houston

Date Tested 12/1/23

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed _____
Water drainage: Natural Swale Pad Other

Fastening multi wide units

Floor: _____
Walls: _____
Roof: _____
Type Fastener: lags Length: 6" Spacing: 18"
Type Fastener: _____ Length: _____ Spacing: _____
Type Fastener: _____ Length: _____ Spacing: _____
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials DH

Type gasket Foam
Pg. _____
Installed:
Between Floors Yes _____
Between Walls Yes _____
Bottom of ridgebeam Yes _____

Weatherproofing

The bottomboard will be repaired and/or taped. Yes _____ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____


Miscellaneous

Skirting to be installed. Yes _____ No _____
Dryer vent installed outside of skirting. Yes _____ N/A _____
Range downflow vent installed outside of skirting. Yes _____ N/A _____
Drain lines supported at 4 foot intervals. Yes _____
Electrical crossovers protected. Yes _____
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Dale Houston Date 12/1/23

Lifestyle Series

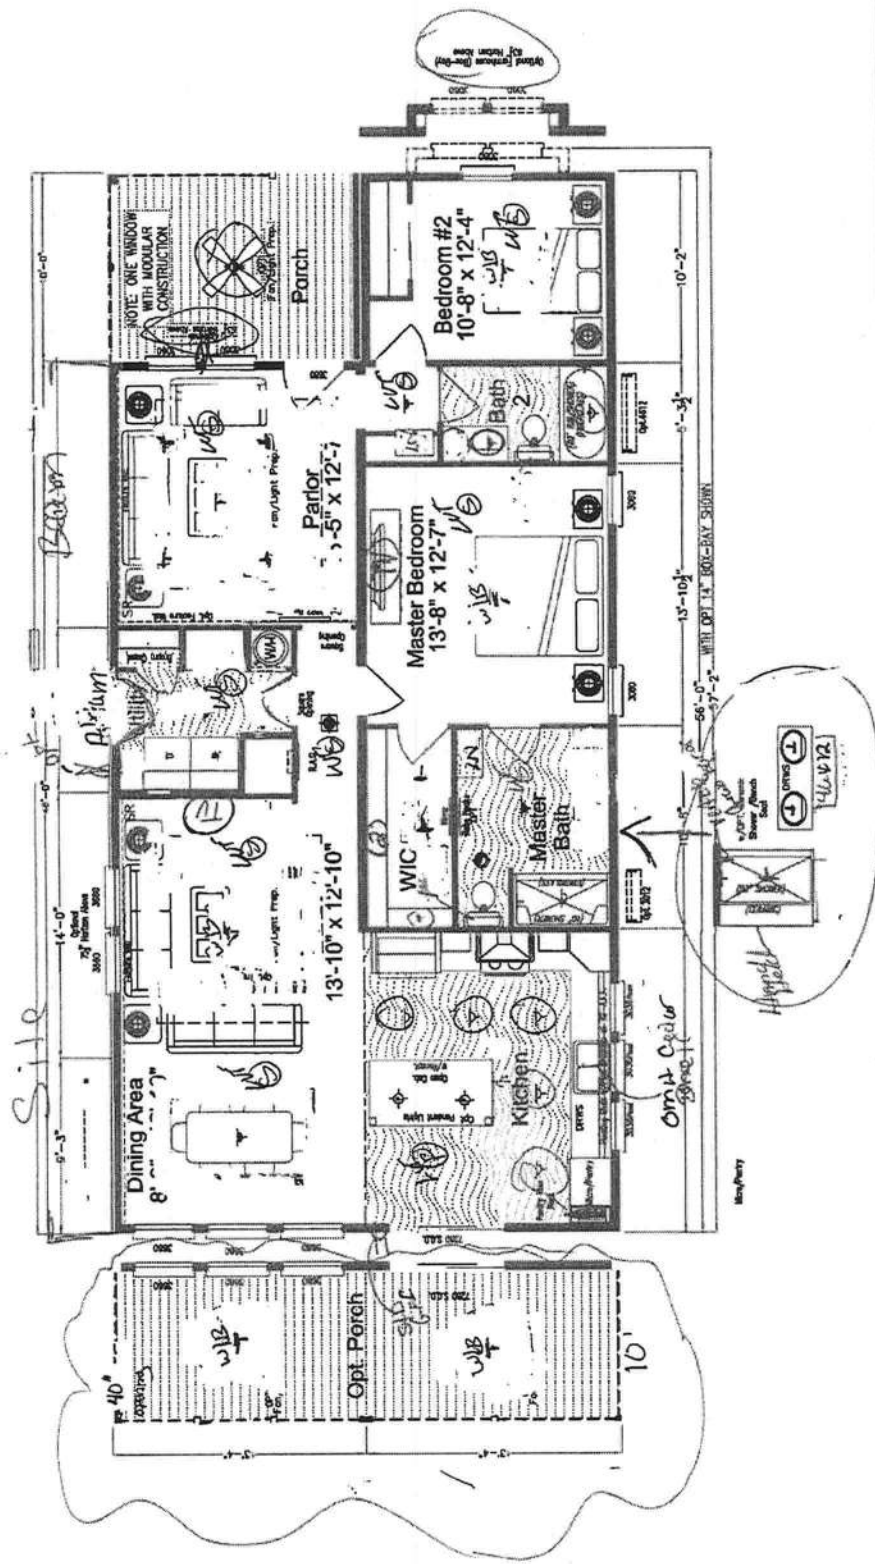

Carriage Farmhouse 26' 3" x 75'

Model 340LS28562K

Approx 1363 Sq Ft.

Bonus Utility Room

Opt. Full Porch

Large Master Suite w/ Walk-in Closet

Open Social Area

Triple Full View Windows in Kitchen

Lifestyle Front Porch w/ 120 sq. feet of Outdoor Living Area

Island Kitchen

Triple Full View Windows in Kitchen

Copyright © Palm Harbor Homes, Inc. Because Palm Harbor Homes has a continuous product updating and improvement process, prices, plans, dimensions, features, materials, specifications and availability are subject to change without notice or obligation. Please refer to our drawings for actual dimensions. Renderings and floor plans are artist depictions only and may vary from the completed home. Square footage calculations to 1/2 room times. All measurements are approximate and subject to industry standards.

Rev 05/13/20
