

Mobile Home Permit Worksheet

DW

 Installer: DAVID AIBRIGHT License # 1H-1129420


 Address of home
being installed _____

 Manufacturer LIVE OAK Length x width 26' x 32'

NOTE: If home is a single wide fill out one half of the blocking plan
If home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Typical pier spacing

 Installer's initials DA

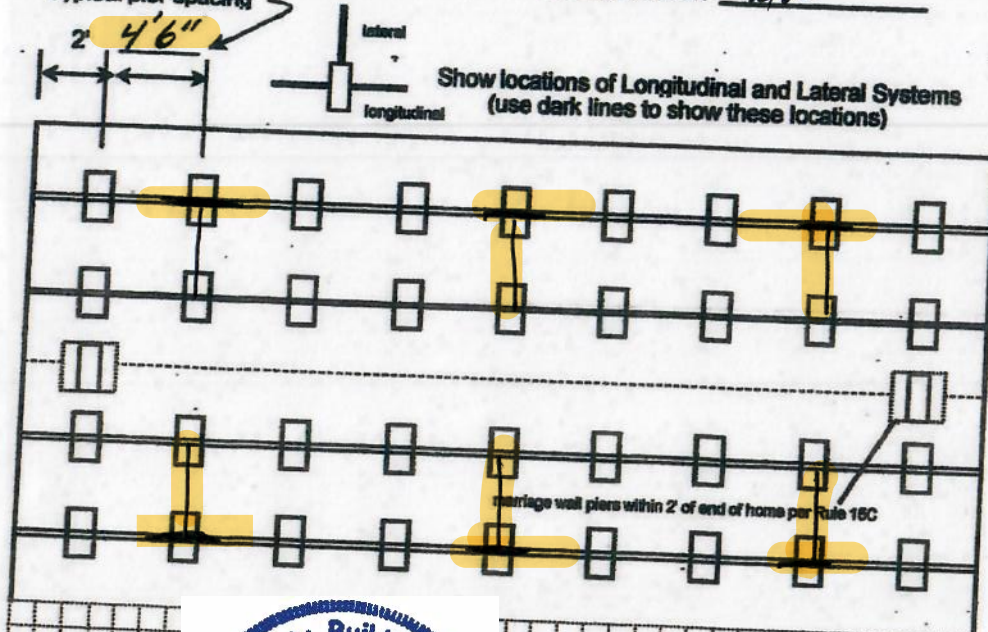 Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)


03-29-2023

Application Number: _____

Date: _____

 New Home ☒ Used Home ☐

 Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C ☒

 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

 Double wide ☒ Installation Decal # 98736

 Triple/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" X 24" (576)*	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'	
1500 psf	4' 6"	6'	7'	8'	9'	10'	
2000 psf	6'	8'	9'	10'	11'	12'	
2500 psf	7' 6"	9'	10'	11'	12'	13'	
3000 psf	9'	10'	11'	12'	13'	14'	
3500 psf	10'	11'	12'	13'	14'	15'	

* interpolated from Rule 15C-1 pier spacing table

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

 I-beam pier pad size 17x25

 Perimeter pier pad size 16x16

 Other pier pad sizes (required by the mfg.) 23x31

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

FACTORY DIAGRAM

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 28 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES

 within 2' of end of home
spaced at 5' 4" oc

OTHER TIES

	Number
Sidewall	<u>27</u>
Longitudinal	<u>6</u>
Marriage wall	<u>7-5' 6"-4'</u>
Shearwall	<u>4</u>

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer OLIVER TECHNOLOGIES
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer OLIVER TECHNOLOGIES

On

Date: _____

Site Preparation

X_____ **X**_____ **X**_____

- X** _____ **X** _____ **X** _____

Installer's initials**Date Tested**

Plumbing

~~Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 107~~

Installer Signature

Date _____

Page 2 of 2

Fastening multi wide units


Gasket (weatherproofing requirement)

Installed:
Between Floors Yes X
Between Walls Yes END WALLS
Bottom of ridgebeam Yes X

Miscellaneous

Skirting to be installed. Yes _____ No X
 Dryer vent installed outside of skirting. Yes _____ N/A X
 Range downflow vent installed outside of skirting. Yes _____ N/A X
 Drain lines supported at 4 foot intervals. Yes X
 Electrical crossovers protected. Yes X
 Other :

BLUE RIDGE

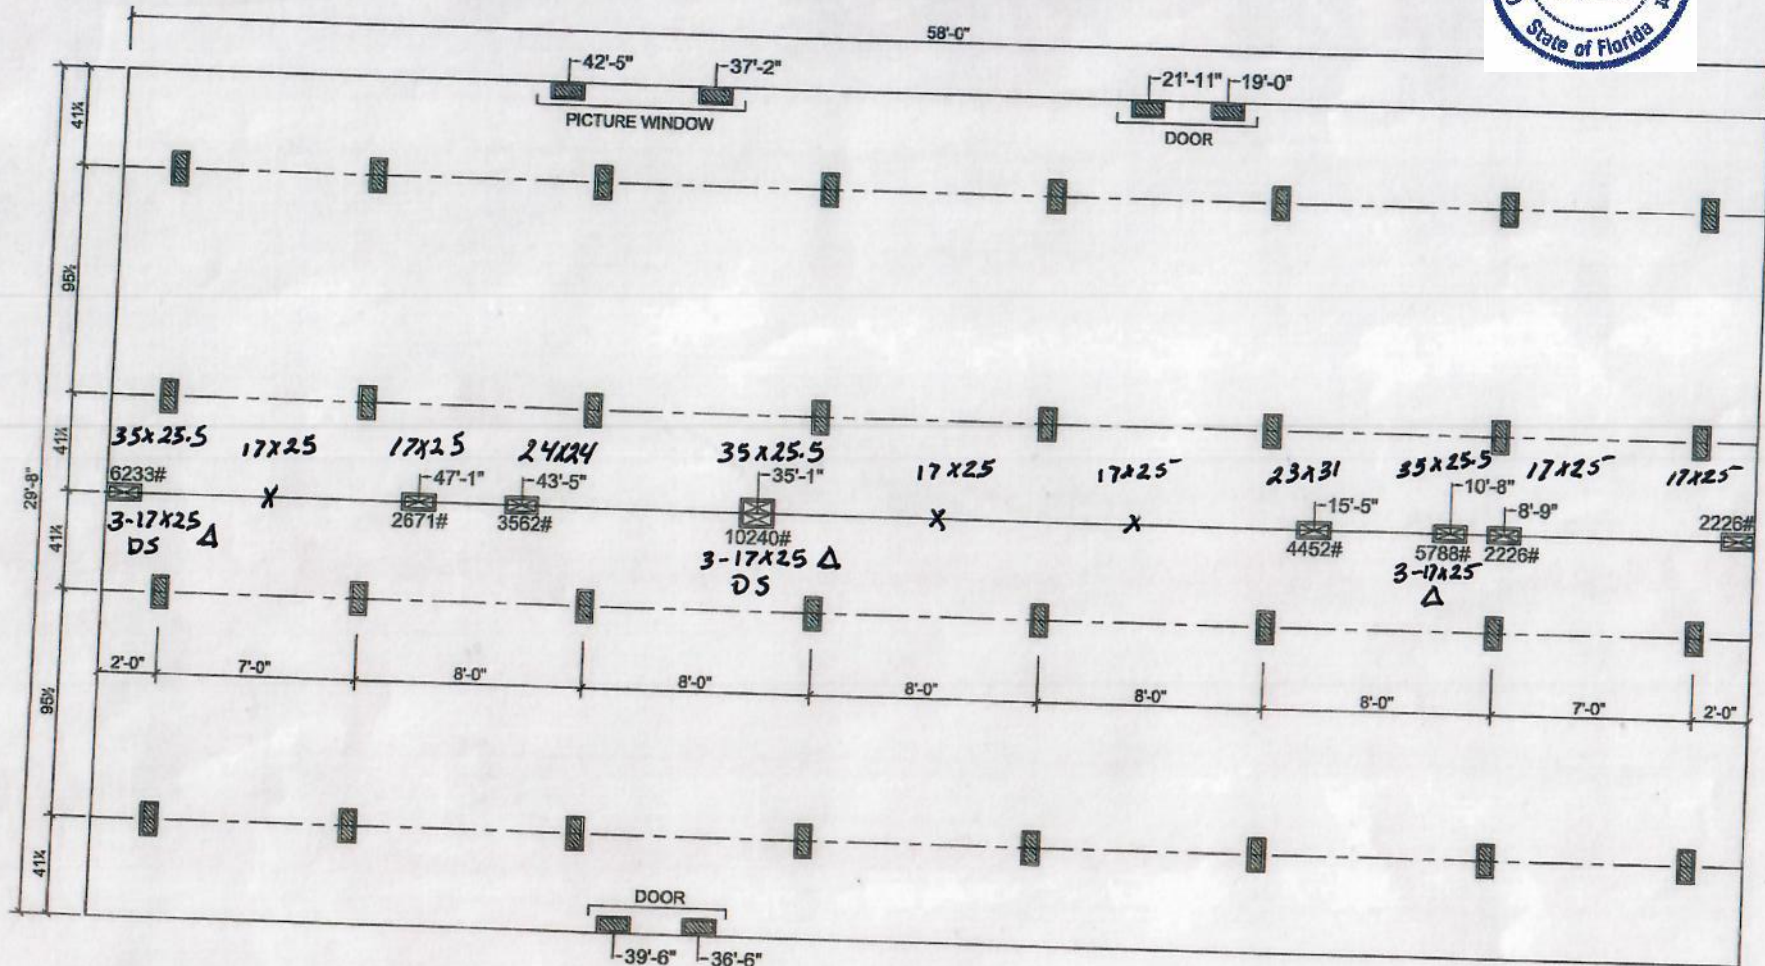

FOUNDATION NOTES:

REFERENCE HOME INSTALLATION MANUAL FOR OPTIONAL PIER SPACING AND LOADING (I.E. FIREPLACES, ETC.)
 SINGLE STACK PIERS MAX. 36" HIGH; DOUBLE STACK PIERS MAX. 80" HIGH.
 ALL DIMENSIONS ARE FROM REAR OF HOME UNLESS OTHERWISE NOTED.


02/19/20

LIVE OAK HOMES
MODEL: H-3583B-PS
3-BEDROOM / 2-BATH

H-3583B-PS



BLUE RIDGE

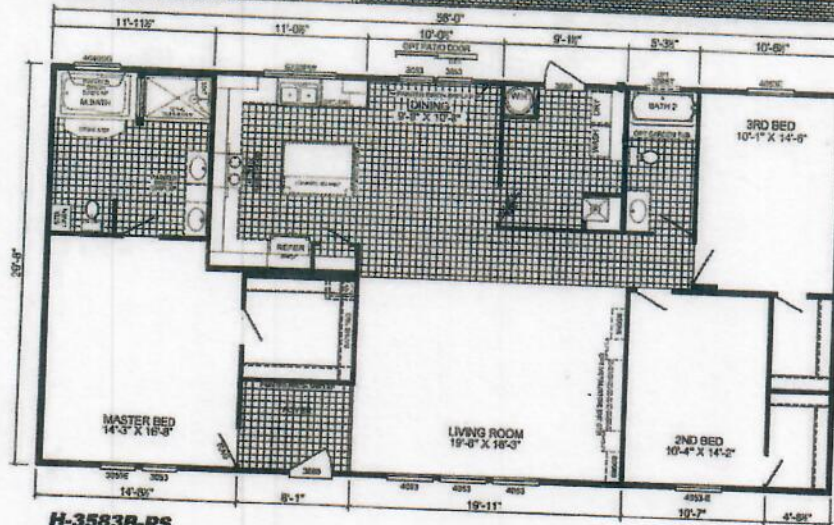

H-3583B-PS

3-BEDROOM / 2-BATH

32 x 62 - Approx. 1720 Sq. Ft.

Date: 04/09/20

* All room dimensions include closets and square footage figures are approximate.
* Live Oak Homes reserves the right to modify product offering at any time.

BLUE RIDGE
DELUXE DRYWALL SERIES

License Number: IH / 1129420 / 1 Name: DAVID E ALBRIGHT			
Order #: 5763	Label #: 98736	Manufacturer: LIVE OAK	(Check Size of Home)
Homeowner: HRAPSKI		Year Model: 2023	Single _____
Address:		Length & Width: 76' x 32'	Double X _____
City/State/Zip: LAKE CITY FL		Type Longitudinal System: 6 OTI	Triple _____
Phone #:		Type Lateral Arm System: 6 OTI	HUD Label #:
Date Installed:		New Home: X Used Home: _____	Soil Bearing / PSF:
Installed Wind Zone: II		Data Plate Wind Zone: II	Torque Probe / in-lbs:
Note:			Permit #:



**STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL**

98736

LABEL #	DATE OF INSTALLATION
DAVID E ALBRIGHT	
NAME	
IH / 1129420 / 1	5763
LICENSE #	ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
