

Mobile Home Permit Worksheet

Installer: Ernest S. Johnson License # TF 1075249

Address of home being installed: 19902 S. US Hwy 441


High Springs, FL 32643

Manufacturer: Revalley Length x Width: 66' x 32'

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home where the sidewall ties exceed 5 ft 4 in.

Installer's Initials: [Signature]

Typical pier spacing: 2' 6' x 6'
Show locations of Longitudinal and Lateral Systems (use dark lines to show these locations)

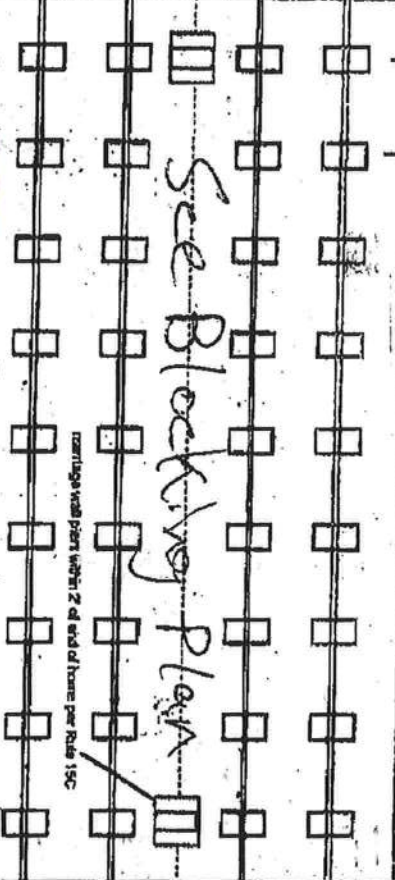

10-9-2020

Application Number: _____

Date: _____

Is my Home ☒ Used Home ☐ Home installed to the Manufacturer's Installation Manual. Home is installed in accordance with Rule 15C.

Single wide ☐ Wind Zone II ☐ Wind Zone III ☒
Double wide ☒ Installation Decal # 72783
Triple/Quad ☐ Serial # 9005413

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	16' x 16" (256)	18' 1/2" x 18" (324)	20' x 20" (400)	22' x 22" (484)	24' x 24" (576)	26' x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'
3500 psf	8'	9'	10'	11'	12'	13'

Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size: 23X31 1/2"
Fender pier pad size: 17.5 X 25.5"
Other pier pad sizes (required by the mfg.): _____

Draw the appropriate locations of marriage wall openings 4 foot or greater. Use this symbol to show the plans.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening _____ Pier pad size _____

See Blocking Plan

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer _____

Oliver 1101V

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc.

OTHER TIES

Side wall Longitudinal Marriage wall Shearwall 2

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

Slip Preparation

Debris and organic material removed
Water drainage: Natural Swale

Pad Other

Fastening multi-wide units

Type Fastener: 1095 Length: 7 Spacing: 20
Type Fastener: 1095 Length: 7 Spacing: 10
Type Fastener: 1095 Length: 7 Spacing: 10
For used homes: a 1/4" 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a slip of laps will not serve as a gasket.

Installer's Initials

Type gasket: PG-111

Installed:
Between Floors Yes
Between Walls Yes
Bottom of ridgebeam Yes

Weatherproofing

The bottomboard will be repaired and/or taped. Yes Pg. 1
Siding on units is installed to manufacturer's specifications. Yes
Fireplace chimney installed so as not to allow intrusion of rain water. Yes

Miscellaneous

Skirting to be installed. Yes No
Dryer vent installed outside of skirting. Yes N/A
Range downflow vent installed outside of skirting. Yes N/A
Drain lines supported at 4 foot intervals. Yes
Electrical crossovers protected. Yes
Other: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to
or check here to declare 1000 lb. soil without testing.

x 1000 x 1000 x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1000 x 1000 x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing. A test.

Note: A slate approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft. anchors are required at all centerline locations where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest S Johnson

Date Tested Assumed Oliver 10/12/05

Both 4x8 Elastics Foot Anchors

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg.

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Ernest S Johnson

Date


2020-08-25 15:38

C&G Mfg. Homes 3867552386 >> 3524814807

P 9/9



Zone EIT

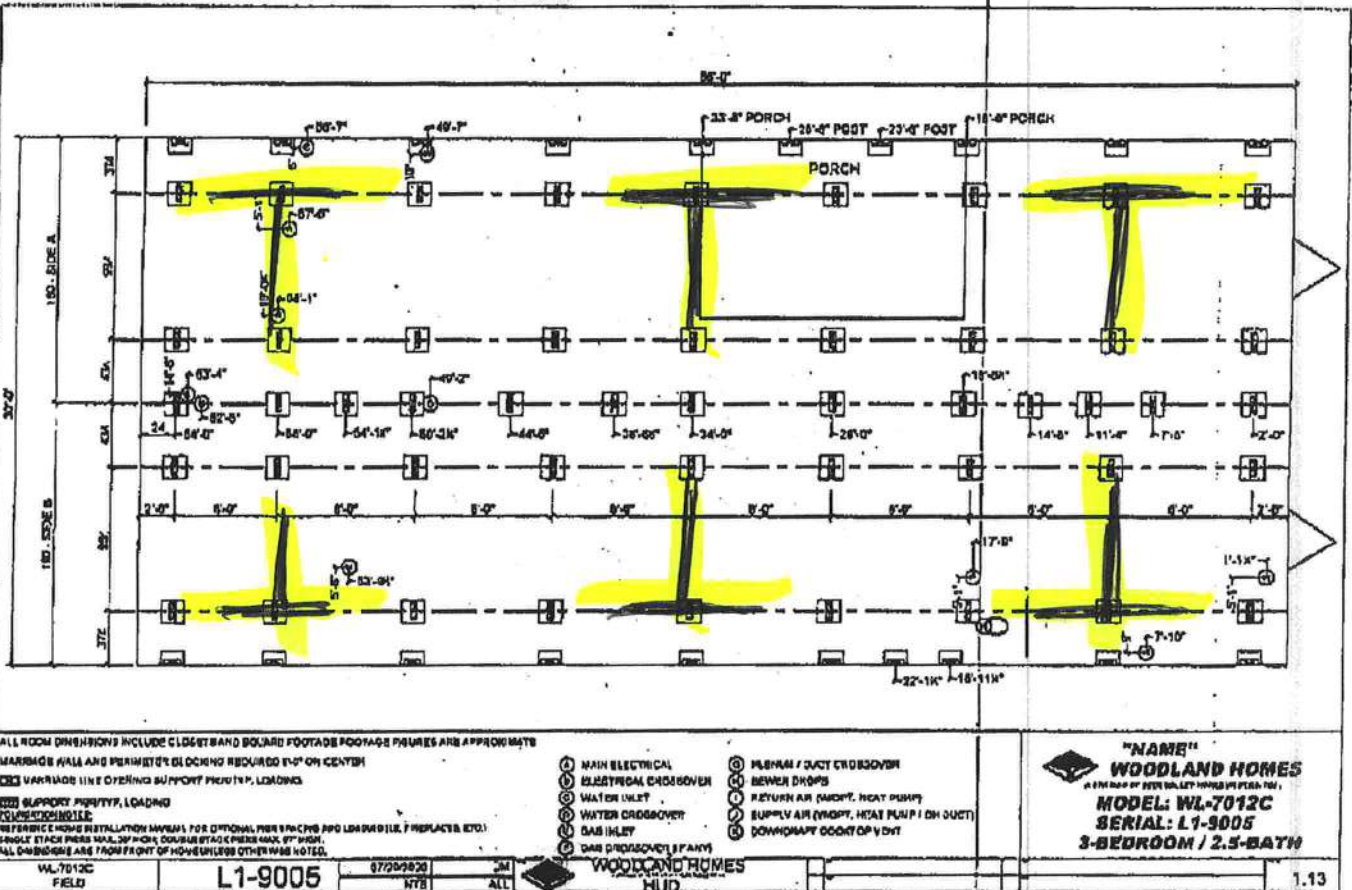


"NAME"
WOODLAND HOMES
A DIVISION OF BETH VALLEY HOMES (FL) LLC
MODEL: WL-7012C
SERIAL: L1-9005
3-BEDROOM / 2.5-BATH

McKnight

2020-08-25 15:38

C&G Mfg. Homes 3867552386 >> 3524814807

P 8/9

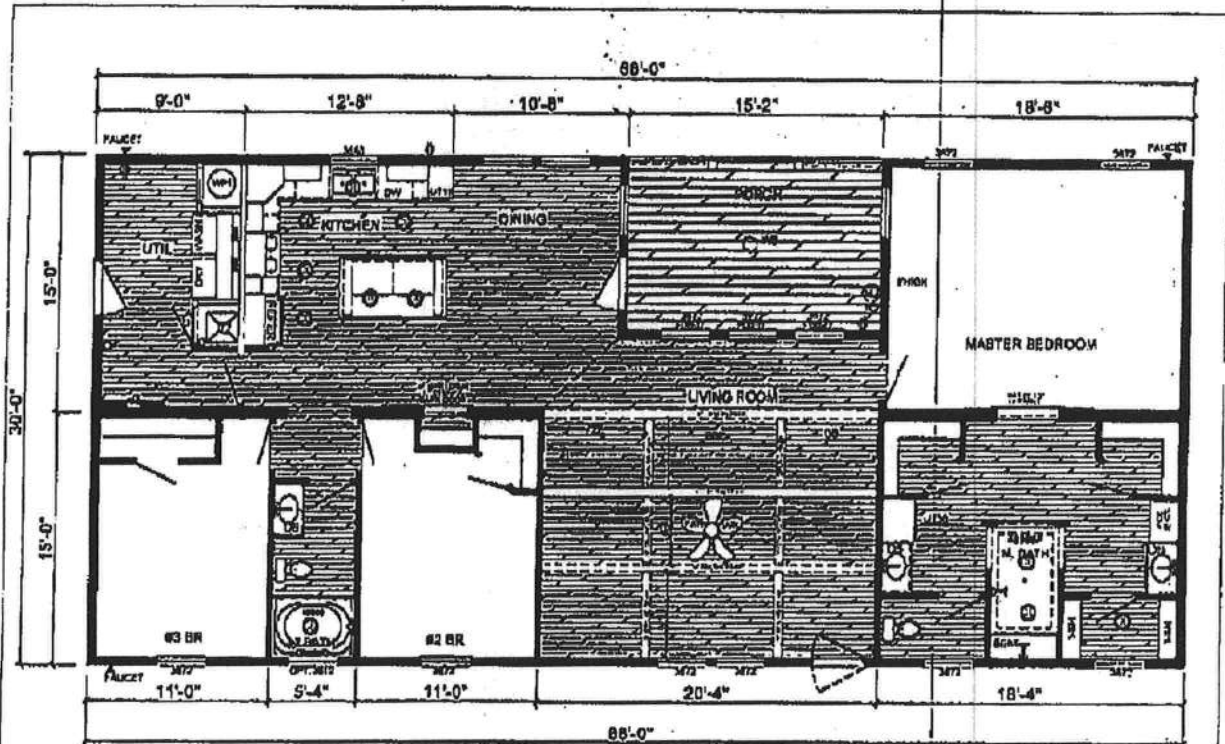

PAUL30(WL-7012C)
3-BEDROOM / 2-BATH
 32 x 70 - Approx. 1980 Sq. Ft.
 CUSTOMER:McKNIGHT



DEER VALLEY HOMEBUILDERS, INC.
 Woodland Homes Series

"AINON" (C)

For more information visit us at
www.deervalleyhomes.com

*All dimensions and square footages are approximate.
 *Drawing layout subject to change if
 required by engineering review.

DATE: 07-13-2020 07-14-2020 07-22-2020

BY: J.CROW

McKNIGHT
