

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

<i>For Office Use Only</i> (Revised 7-1-15)		Zoning Official _____	Building Official _____
AP# _____	Date Received _____	By _____	Permit # _____
Flood Zone _____	Development Permit _____	Zoning _____	Land Use Plan Map Category _____
Comments _____			
FEMA Map# _____	Elevation _____	Finished Floor _____	River _____ In Floodway _____
<input type="checkbox"/> Recorded Deed or <input type="checkbox"/> Property Appraiser PO <input type="checkbox"/> Site Plan <input type="checkbox"/> EH # _____ <input type="checkbox"/> Well letter OR <input type="checkbox"/> Existing well <input type="checkbox"/> Land Owner Affidavit <input type="checkbox"/> Installer Authorization <input type="checkbox"/> FW Comp. letter <input type="checkbox"/> App Fee Paid <input type="checkbox"/> DOT Approval <input type="checkbox"/> Parent Parcel # _____ <input type="checkbox"/> STUP-MH _____ <input type="checkbox"/> 911 App <input type="checkbox"/> Ellisville Water Sys <input type="checkbox"/> Assessment _____ <input type="checkbox"/> Out County <input type="checkbox"/> In County <input type="checkbox"/> Sub VF Form			

Property ID # 09-65-17-09630-006 Subdivision Heatherwood Lot# 6

- New Mobile Home X Used Mobile Home _____ MH Size _____ Year _____
- Applicant Brody Pack Phone # 503 689 6563
- Address 5683 153rd Rd Live Oak FL 32060
- Name of Property Owner Vasily Gusev Phone# 206 947 3371
- 911 Address 399 SW Manning Pl Lake City FL
- Circle the correct power company - FL Power & Light - Clay Electric
 (Circle One) - Suwannee Valley Electric - Duke Energy
- Name of Owner of Mobile Home Vasily Gusev Phone # 206 947 3371
 Address 399 SW Manning Pl Lake City FL
- Relationship to Property Owner Same
- Current Number of Dwellings on Property 0
- Lot Size _____ Total Acreage 5.07 acres
- Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
 (Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)
- Is this Mobile Home Replacing an Existing Mobile Home No
- Driving Directions to the Property South on SW Tustenuggee Ave,
Left on SW Herlong St, Right on SW marion
Mann Terr, Left on SW Manning Pl
- Name of Licensed Dealer/Installer Glenn Williams Phone # 386 344 3669
- Installers Address _____
- License Number IH/1054858 Installation Decal # 78819

Mobile Home Permit Worksheet



Installer: Glenn Williams License # IH/1051848

Address of home being installed 399 Manning Place
Lake City, FL 32024

Manufacturer Live Oak Length x width 28x40

NOTE: *if home is a single wide fill out one half of the blocking plan*
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall ties exceed 5 ft 4 in.

Installer's initials GW

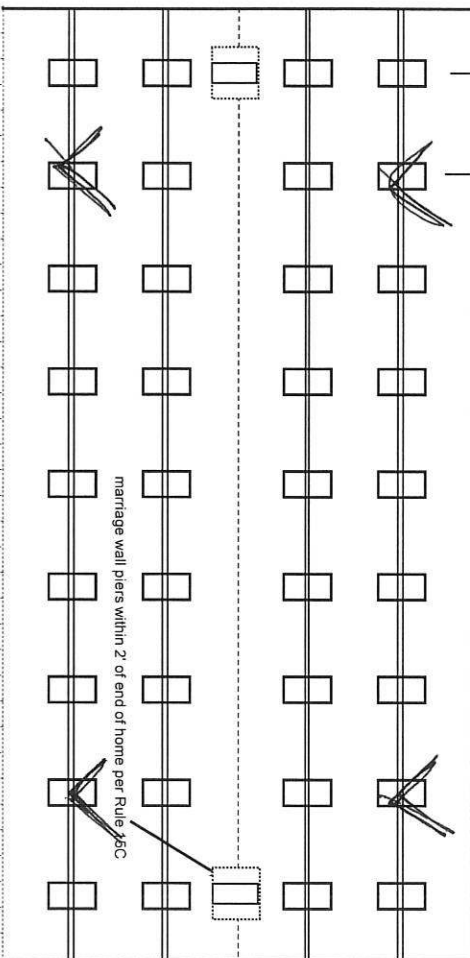

Frame ties

Application Number: _____

Date: _____

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Decal # 78819

Triple/Quad ☐ Serial # 1-2363C

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'	8'
1500 psf	4'6"	6'	7'	8'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7'6"	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 24 X 24
Perimeter pier pad size _____
Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft ☐

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Longitudinal Stabilizing Device (LSD)
Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer L

Sidewall _____
Longitudinal _____
Marriage wall _____
Shearwall _____
Number 28
4

Mobile Home Permit Worksheet

Application Number: _____

Date: _____

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil _____ without testing.

x 1500 x 1500 x 1500

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1500 x 1500 x 1500

TORQUE PROBE TEST

The results of the torque probe test is 280 inch pounds or check here if you are declaring 5' anchors without testing _____. A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. 1 understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Glenn Williams

Date Tested

4-12-21

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed _____ Swale ☒ Pad ☒ Other _____

Fastening multi wide units

Floor: Type Fastener: 1/4" Length: 6" Spacing: 2 ft
Walls: Type Fastener: 1/4" Length: 6" Spacing: 2 ft
Roof: Type Fastener: 1/4" Length: 6" Spacing: 2 ft
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials GW

Type gasket foam

Pg. 103

Installed:

Between Floors Yes _____

Between Walls Yes _____

Bottom of ridgebeam Yes _____

Weatherproofing

The bottomboard will be repaired and/or taped. Yes _____ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes _____
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes _____ N/A _____
Range downflow vent installed outside of skirting. Yes _____ N/A _____
Drain lines supported at 4 foot intervals. Yes _____
Electrical crossovers protected. Yes _____
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Glenn Williams Date 4-13-21



467 Swan Ave • Hohenwald, TN 38462 • (800) 284-7437 • www.olivertechnologies.com • Fax (931) 796-8811

Installation Instructions for 1100 "V" Series All Steel Foundation System Wind Zones I & II

SPECIAL CIRCUMSTANCES: If following conditions occur - STOP! Contact Oliver Technologies at 1-800-284-7437 for further instructions:

- a) Pier (system) height exceeds 48" b) Roof eaves exceed 16" c) Roof pitch greater than 7/12 d) Location is within 1500 feet of coastline
- e) Soil conditions less than 4B f) Thick and wide I Beam attachments are available.

INSTALLATION OF GROUND PAN FOR DIRT SET (IV)

- 1) Remove weeds and debris in an approximate three foot square to expose firm, level undisturbed soil or controlled fill for each ground pan. The 1100 V Pan is equivalent to a 21 x 21 footing. Top of ground pan (C) must be installed at ground level or per local jurisdiction.
- 2) Place center ground pan (C) directly below chassis I-beam. Press or drive pan completely into soil until flush with or below soil.

SPECIAL NOTE: The longitudinal "V" brace system serves as a pier under the home and should be loaded as any other pier. It is recommended that after leveling piers, and one-half inch (1/2") before home is lowered completely onto piers, complete items 3 through 7 below.


INSTALLATION OF LONGITUDINAL "V" BRACE SYSTEM

- 3) Select the correct square tube brace (E) length for set-up (pier) height at support location.

PIER HEIGHT 1.5"
(Approx. 40-60 degrees Max.) Tube Length

14" to 18"	20"
18" to 25"	28"
24" to 35"	39"
30" to 40"	44"
36" to 48"	54"

PIER HEIGHT = the dimension from the top of the pan
to the bottom of the I-Beam

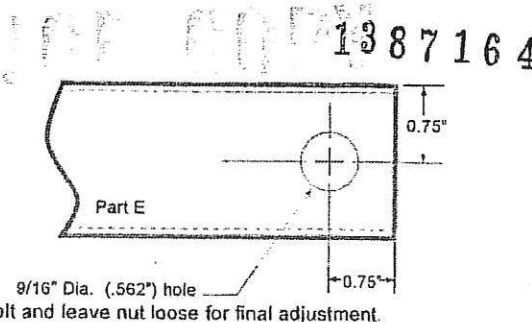

- 4) Install both of the 1.5" square tubes (E) into the "V" bracket (J), insert carriage bolt and leave nut loose for final adjustment.
- 5) Place I-beam connector (F) loosely on the bottom flange of the I-beam.
- 6) Attach the selected 1.5" tubes (E) to the I-beam connectors (F) and fasten loosely with bolts and nuts. NOTE: The ground pan must be level in both directions to ensure the angle markings on the center point connector are correct from the horizontal plane of the pan. The angle is not to exceed 60 degrees and not less than 40 degrees. The "V" bracket (J) is stamped with the angles to verify correct degree. Use proper length tube or cut and drill tube to achieve proper length. (The tube may be cut using any appropriate steel cutting method such as steel saw, cutting torch, etc. New holes must be drilled to the dimension and at the location as shown for part (E).
- 7) Using standard hand tools, tighten all nuts and bolts. When connecting the brace tube to the model 1100-10-P I-beam connector bracket, tighten at least one and a half to two full turns past hand tight.

INSTALLATION OF (LATERAL) TELESCOPING TRANSVERSE ARM SYSTEM (1100 ITV)

- 8) Select the correct transverse arm (H). The 60" sections are standard. The 72" sections are used on frame widths greater than 99.5"
- 9) Install the 1.5" transverse brace (H) to the ground pan connector (D) with the bolt and nut.
- 10) Slide 1.25" transverse brace into the 1.5" brace and attach to adjacent I-beam connector (I) with bolt and nut.
- 11) Secure 1.5" transverse arm to 1.25" transverse arm using four (4) 1/4" - 14 x 3/4" self-tapping screws in pre-drilled pilot holes.

INSTALLATION USING CONCRETE (ICV)

The concrete footer, runner or slab may be of any shape, that has a minimum of 2900 cu. in., with a minimum depth of 3.5" (dry set) or 6" (wet set), at each system location. The surface of the footing shall be large enough to support the pier load and allow at least 4" from the concrete bolt to the edge of the concrete (ie. 22"x22"x6" footer). The concrete shall be a minimum of 2500 psi mix (pre-blended sacked concrete mix is acceptable). Special inspection of footing is not required. If the 1100 ITC transverse system, (D (W or D) bracket only) is to be installed without the use of the 1100 ILC (V) longitudinal system (J (W or D) bracket), it MUST be installed within 18" of pier.

NOTE: The bottom of all footings, pads, slabs and runners must be per local jurisdiction.

LONGITUDINAL (V)



When using the 1100 wet set J(W) bracket, simply install the bracket in runner/footer OR when installing in cured concrete, use the 1100 dry set J(D) bracket. The 1100 dry set J(D) bracket is attached to the concrete using (2) 1/2" X 3" concrete wedge bolts. Place the bracket in desired location. Mark bolt hole locations, then using a 1/2" masonry bit, drill a hole to a minimum depth of 3". Be sure all dust is blown out of the holes. Place wedge bolts into drilled holes, then place 1100 J(D) bracket onto wedge bolts and start wedge bolt nuts. Take a hammer and lightly drive the wedge bolts down by hitting the nut (Do not hit the top of threads on bolt). Complete by tightening the nuts.

LATERAL (Transverse Arm)

For wet set installation set the transverse connector bracket D(W) into runner/footer at desired location. For dry set installations, the transverse connector bracket D(D) is attached to the concrete using (2) 1/2" X 3" concrete wedge bolts. Mark bolt hole locations, then using a 1/2" masonry bit, drill a hole to a minimum depth of 3". Be sure all dust is blown out of the holes. Place wedge bolts into drilled holes, then place transverse connector bracket J(D) bracket onto wedge bolts and start wedge bolt nuts. Take a hammer and lightly drive the wedge bolts down by hitting the nut (Do not hit the top of threads on bolt.) Complete by tightening the nuts.

**REQUIRED NUMBER AND LOCATION OF MODEL
1100 "V" SERIES BRACES FOR 4/12 & 5/12**

**REQUIRED NUMBER AND LOCATION OF MODEL
1100 "V" SERIES BRACES FOR 6/12 & 7/12**

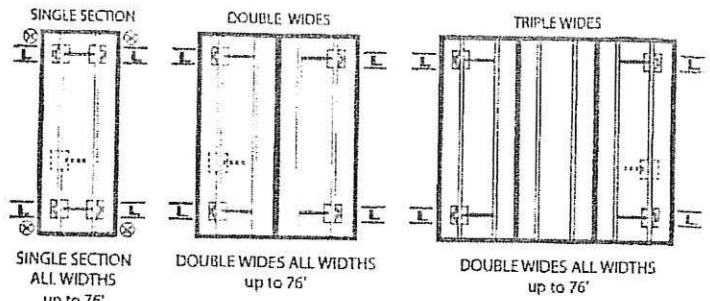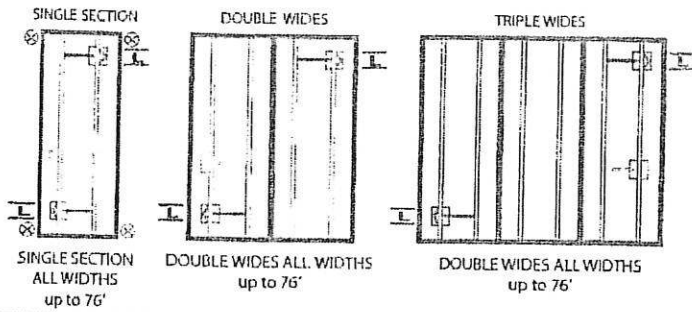

(Length of house is actual box size)

LEGEND:

1. - - Approximate location of the system (See note H)
2. - - Location of ASF Model 1100 "V" (Lateral and Longitudinal Bracing) or 1100 T (Lateral only)
3. - - Location of additional ASF Model 1100 T "V" System (Lateral only) for homes exceeding 76' in length or with roof pitch between 4.37/12 (20 degrees) and 5/12, the additional system is to be installed at approximately the midpoint of the house and may be installed at either exterior beam.
4. - - Installation of single wide homes require two (2) anchors per side located not more than ten (10) feet from each end (with a minimum of 3150 load rating)
5. - - Location of additional ASF Model 1100 T "V" System (Lateral only) for homes exceeding 76' in length, sidewall height exceeding 96' or with roof pitch between 6/12 & 7/12 the additional system is to be installed at approximately the midpoint of the house and may be installed at either exterior beam.

NOTE:

- a) Installation of the longitudinal system eliminates the need for the longitudinal anchors.
- b) Installation of the transverse system eliminates the need for all anchors, diagonal frame ties and stabilization plates except when noted. (Legend #5 & note C)
- c) All other home manufacturer's instructions for installation of stabilizing devices must be followed, including installation of vertical tie-down anchors, and mating line column, shear wall or center-line tie-down anchors. NOTE WIND ZONE II: ALL VERTICAL ANCHORS (NOT TO EXCEED 8' SPACING) MUST BE INSTALLED PER MANUFACTURER'S INSTALLATION INSTRUCTIONS!
- d) If the home manufacturer's installation instructions are not available, the home must be installed in accordance with any state promulgated rules or as required by the authority having jurisdiction.
- e) If bolts, nuts and tech screws are lost, they may be replaced as long as they meet or exceed the specs for OTI ASFS hardware.
- f) When the length of home exceeds 76', sidewall height exceeds 96' or the roof pitch is between 4.37/12 (20 degrees) and 5/12, add 1 transverse system (see location diagrams above) 6/12: a total of 4 Transverse & 3 Longitudinal systems are needed & 7/12: a total of 5 Transverse & 3 Longitudinal systems are needed. (Longitudinal portion only required when longitudinal bracing is required by home manufacturer).
- g) An alternative method using the 1100 CVD anchors (dry set) or 1100 CVW (wet set) may be used on a footing size of 16" diameter X 24" depth. These brackets are designed for lateral and longitudinal protection.
- h) It is recommended that the systems be installed at the 2nd pier in from each end of the house. However, they may be installed at any location at least 2 feet, but not more than 1/4 the house length, in from the ends of the home.

STATE OF MICHIGAN ONLY: As required by Section 1805.2 of the 200 Michigan Building Code, the depth of the footer shall be a minimum depth of 42 inches below grade, except that the authority having jurisdiction may approve a lesser depth based on known prevailing soil and weather conditions, or as provided by the exception under Section 1805.2.1 of the Code.

STATE OF ALABAMA ONLY: Maximum pier height is limited to 32" with pier defined in the Alabama Regulation as "that portion of the support system between the top of the footing and the bottom of the pier cap."


The State of Alabama limits the use of this system to H.U.D labeled homes.

STATE OF NORTH CAROLINA ONLY:

Tubing must be galvanized and, when the manufacturer's installation instructions are not available, vertical wall tie-downs must be installed not to exceed 8-feet on center. (Wind Zone II)

STATE OF IDAHO ONLY:


Concrete must be a minimum of 8" in depth.

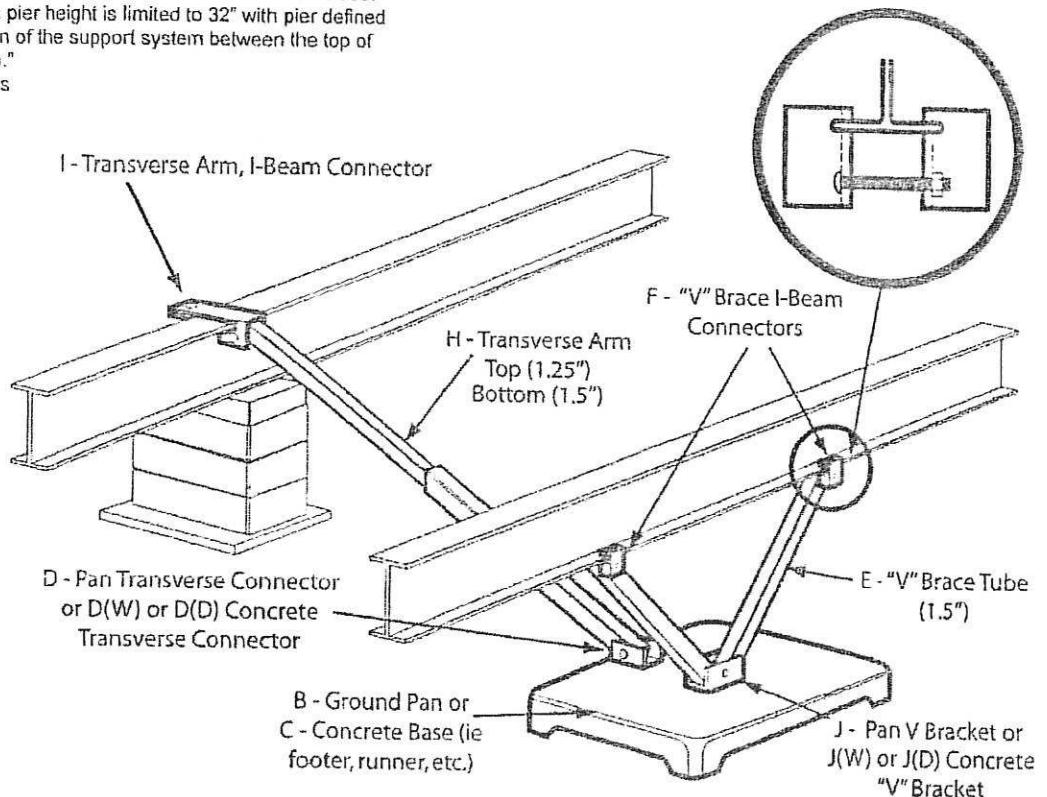

OLIVER
467 Swan Ave
Hohenwald, TN 38462
(800) 284-7437
www.olivertechnologies.com



467 Swan Ave • Hohenwald, TN 38462 • (800) 284-7437 • www.olivertechnologies.com • Fax (931) 796-8811



Installation Instructions for ABS Pads

**For use on all Mobile and Manufactured Homes, including
HUD approved Homes and Modular Building
Patent #5503500 and other patents pending**

GENERAL INSTRUCTIONS:

1. All pads are to be installed flat side down, ribbed side up.
2. The ground under the pads should be leveled as smooth as possible with all vegetation removed. Pads to be placed on fully compacted or undisturbed soil, at or below the frost-line or otherwise protected from the effects of frost. Refer to NCSBCS/ANSI A225.1
3. Pier & pad spacing will be determined by the manufactured homes' written set-up instructions or any local or state codes.
4. The open cells between the ribbing on the upper side of the pads may be filled with soil or sand after installation to prevent any accumulation of stagnant water in the pads.
5. A pocket penetrometer may be used to determine the actual soil bearing value. If no soil testing equipment is available – use an assumed soil value of 1000 lbs. / square foot.
6. All pad sizes shown are nominal dimensions and may vary up to 1/8".
7. The maximum deflection in a single pad is 5/8" measured from the highest point to the lowest point of the top face.
(NOTE: Actual test results were less than 5/8")
8. Pad loads are the same when using single stack or double stack blocks.
9. The maximum load at any intermediate soil value may be determined as the average of the next lower and next higher soil value given in the table below.
10. If the home manufacturer shows soil densities greater than 3000 lbs. When using ABS pads, do not exceed 3000 lbs. soil pier spacings per set up manual.

PAD SIZE	ID NO.	PAD AREA	1000 PSF SOIL	2000 PSF SOIL	3000 PSF SOIL
Oval 16" x 18.5"	1055-23/AIT-06-1000	288 sq. in.	2000 lbs.	4000 lbs.	6000 lbs.
Oval 17" x 22"	1055-16/AIT-06-1001	360 sq. in.	2500 lbs.	5000 lbs.	7500 lbs.
Oval 17.5" x 22.5"	1055-21	384 sq. in.	2667 lbs.	8000 lbs.	8000 lbs.
Oval 17.5" x 25.5"	1055-17/AIT-06-1002	432 sq. in.	3000 lbs.	6000 lbs.	9000 lbs. *
Oval 21" x 29"	1055-22/AIT-06-1003	576 sq. in.	4000 lbs.	8000 lbs. *	12000 lbs. *
Oval 23.25" x 31.25"	1055-20/AIT-06-1004	675 sq. in.	4694 lbs.	9388 lbs. *	9388 lbs. *


PAD SIZE	ID NO.	PAD AREA	1000 PSF SOIL	2000 PSF SOIL	3000 PSF SOIL
Square 16" x 16"	1055-14/AIT-06-1005	256 sq. in.	1785 lbs.	3560 lbs.	5333 lbs.
Square 18.5" x 18.5"	1055-9/AIT-06-1006	342 sq. in.	2375 lbs.	4750 lbs.	7100 lbs. *
Square 20" x 20"	1055-7/AIT-06-1007	400 sq. in.	2750 lbs.	5500 lbs.	8250 lbs. *
Square 24" x 24"	1055-13/AIT-06-1008	576 sq. in.	4000 lbs.	8000 lbs. *	8000 lbs. *


* Concrete blocks are required to be double blocked.

11. Any ABS pad configuration may be used to replace a home manufacturer's recommended concrete or wood base pad.
12. **ALABAMA ONLY:** The 23.25" x 31.25" ID#1055-20 may not be installed in the State of Alabama.
For the State of Alabama all ABS pads shall not have more than 3/8" deflection. See chart below for details on correct installation in Alabama.


EXAMPLE: 16' x 80' section (Alabama only)

PAD SIZE	1000 PSF	2000 PSF
Oval 16" x 18.5"	2'9"	5'6"
Oval 17" x 22"	3'0"	6'0"
Oval 17.5" x 22.5"	3'9"	7'6"
Oval 17.5" x 25.5"	4'0"	8'0"
Oval 21" x 29"	4'5"	8'0"
Oval 23.25" x 31.25"	6'0"	8'0"

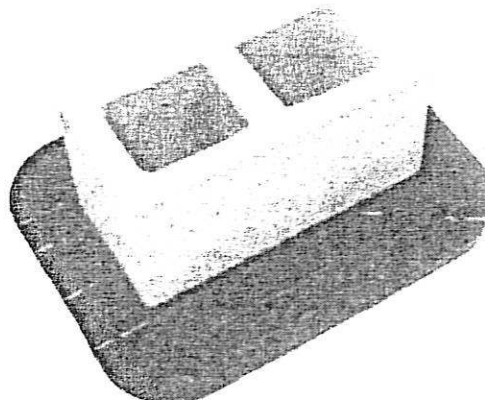



467 Swan Ave • Hohenwald, TN 38462 • (800) 284-7437 • www.olivertechnologies.com • Fax (931) 796-8811



13. TEXAS ONLY: 17.5" x 22.5" ID #1055-21 and 23.25" x 31.25" ID #1055-20 may not be installed in the State of Texas.
14. Steel Piers: All pads are tested with steel piers on 1000 PSF soil density unless otherwise noted. (See 15) If required, attach with (04) 2" #12 x 1/2" hex tech screws. Minimum Pier Base 7 1/4 inches. The Mult-Pad configuration 35" x 25.5" ID #AIT-06-1002 (03) requires minimum 9 1/4" pier base.
15. Available pads tested on 2000 PSF soil density using steel piers are: ID #1055-14, 1055-9, 1055-7 and 1055-13.
16. CALIFORNIA: Use an assumed value of 1000 lb/sq. ft. unless engineering and calculations are provided.




INSTRUCTIONS for Mult-Pad Configurations

MAXIMUM PIER LOAD IN POUNDS:

ABS Pad Types			8" Cell Block				Soil Bearing Value	Maximum Load
Oval 16" x 18.5" Pad	2.00 Square Feet	ID # 1055-23/AIT-06-1000	32" x 18.5" Pad Configuration	Single Stack	1000 lbs. / sq. ft.			4000 lbs.
Oval 32" x 18.5" Pad Configuration (03)	4.00 Square Feet			Double Stack	2000 lbs. / sq. ft.			8000 lbs. *
Oval 17" x 22" Pad	2.50 Square Feet	ID # 1055-16-AIT-06-1001	34" x 22" Pad Configuration	Single Stack	1000 lbs. / sq. ft.			5000 lbs.
Oval 34" x 22" Pad Configuration (03)	5.00 Square Feet			Double Stack	2000 lbs. / sq. ft.			10000 lbs. *
Oval 17.5" x 25.5" Pad	3.00 Square Feet	ID # 1055-17/AIT-06-1002	35" x 25.5" Pad Configuration	Single Stack	1000 lbs. / sq. ft.			6000 lbs.
Oval 35" x 25.5" Pad Configuration (03)	6.00 Square Feet			Double Stack	2000 lbs. / sq. ft.			12000 lbs. *

*Concrete blocks are only rated at 8000 pounds, 8001 pounds and higher must be double stacked.

PAD ASSEMBLY

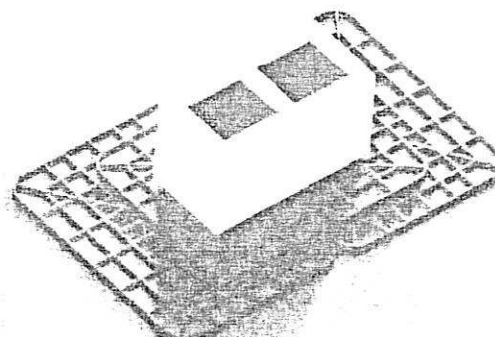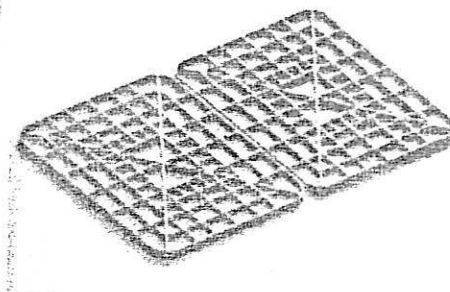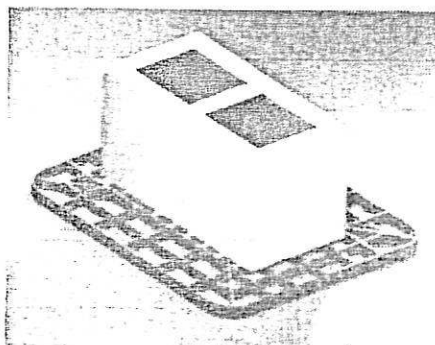


STEP 1 - 17" x 22" ABS Pad

(Note: Use 2 blocks side by side for soils rated at more than 1,000 lbs / sq. foot)

STEP 2 - (2) 17" x 22" ABS PADS (34" x 22" Configuration)

STEP 3 - Complete Assembly 34" x 22" Multi-pad Configuration

1. General instructions (on reverse) apply to all multi - pad configurations.
2. The 32" x 18.5" pad configuration is formed by using (3) 16" x 18.5" ABS Pads. Place (2) 16" x 18.5" side by side, and place (1) 16" x 18.5" on top, laid in the opposite direction to the bottom pads.
3. The 34" x 22" pad configuration is formed by using (3) 17" x 22" ABS Pads. Place (2) 17" x 22" pads side by side, and (1) 17" x 22" pad on top. The top pad is laid in the opposite direction to the bottom pads.
4. The 35" x 25.5" pad configuration is formed by using (3) 17.5" x 25.5" ABS Pads. Place (2) 17.5" x 25.5" pads side by side, and (1) 17.5" x 25.5" pad on top. The top pad is laid in the opposite direction to the bottom pads.

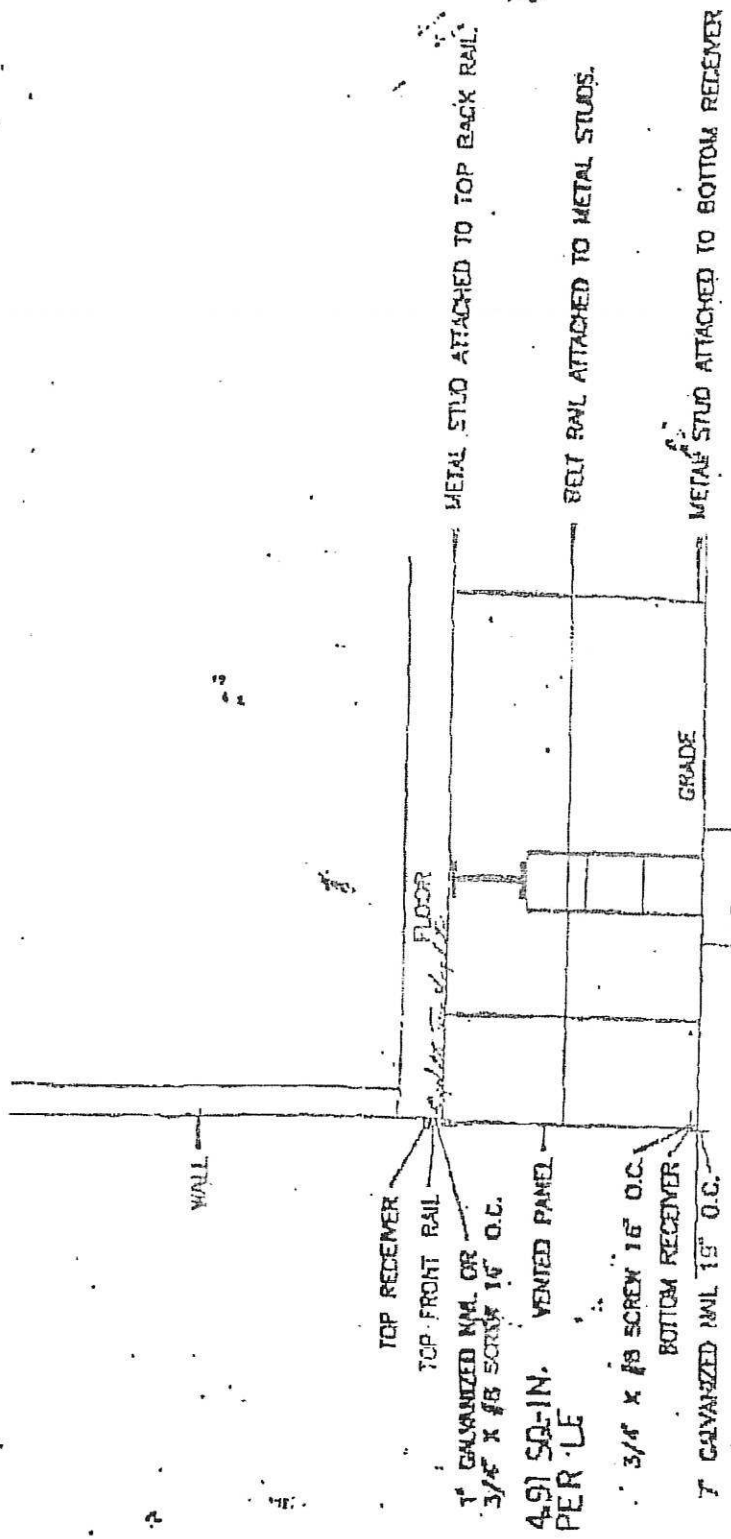


TYPICAL CRAWL SPACE WALL SECTION

SIZE AND LOCATION OF ACCESS DOOR TO BE PLACED TO COORDINATE WITH WATER CUT-OFFS. ACCESS TO BE 18" X 24" MINIMUM.

PER MARION COUNTY REQUEST, SCREWS TO BE INSTALLED AT TOP AND BOTTOM OF EACH PANEL

ANY HOME HAVING IN EXCESS OF 36" HEIGHT MUST HAVE VERTICAL STUDS EVERY 48" WITH BELT RAIL INSTALLED FOR BLOW OUT PROU

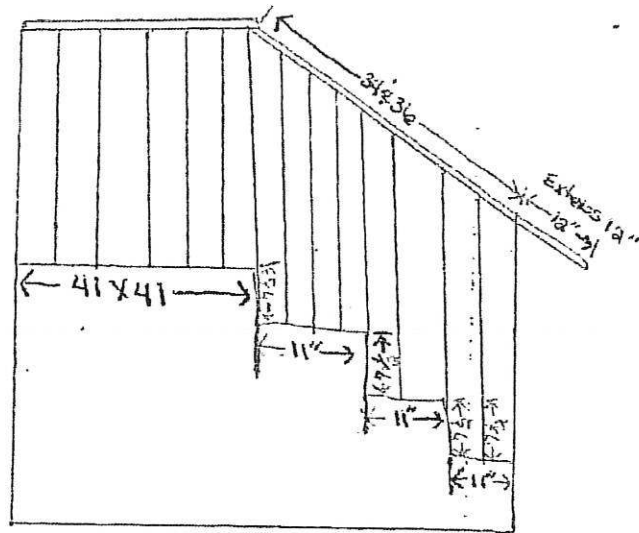

Platform 41x41
 Spindels 4" on center
 treads 11"
 risers $7\frac{1}{2}"$



MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER _____ CONTRACTOR Glenn Williams PHONE 386-344-3669

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL	<div>Print Name <u>Gusev Vasilily</u> Signature <u></u></div> <div>License #: <u>Homeowner</u> Phone #: _____</div> <div>Qualifier Form Attached <input type="checkbox"/></div>
MECHANICAL/ A/C _____	<div>Print Name <u>ACE A/C - Michael Boland</u> Signature <u></u></div> <div>License #: <u>CAC1817716</u> Phone #: _____</div> <div>Qualifier Form Attached <input type="checkbox"/></div>

F. S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

LIMITED POWER of ATTORNEY

Consents for County Permit Applications

I, Gusev Vasily, do hereby authorize Brody Pack to be my representative and act on my behalf in all aspects of applying for a Manufactured Home Permit to be placed on my property described as:

Sec. _____, Twp. _____ S, Rge. _____ E

Tax Parcel No. _____

Lot: _____, Block: _____, Subdivision: _____

Manufacturer: LIVE OAK HOMES, Model: _____, Year: _____

Length: _____ Width: _____ Serial # _____

I understand that this could result in an assessment for solid waste and fire protection services levied on this property.

Dated this 14th day of April, 2021
~~2016~~

Witness: _____

Owner: _____


Witness: [Signature]

Owner: _____

Sworn to and described before me this 14th day of April, 2021
~~2016~~

By: _____
Property Owner's Name

[Signature]
Notary's Name



LIMITED POWER OF ATTORNEY

License Holder: Michael A Boland

License #: CAC1817716

I hereby name & appoint Broderick Pack as an agent of Ace A/C of Ocala, LLC, to be my lawful attorney-in-fact to act for me to apply for, receipt for, sign for and do all things necessary to this appointment for Florida applying to:

☒ All permits and applications submitted by this contractor

☐ The permit and application for work located at: _____

Michael Boland


License Holder Signature

State of Florida

County of Marion

The foregoing instrument was acknowledged before me this 18 day of Jan, 2021,

By Michael Boland as identification and who did (did not) take an oath.



Jeffrey C. Willens
Signature of Notary

Jeffrey C. Willens
Print or type Notary name



COLUMBIA COUNTY BUILDING DEPARTMENT
135 NE Hernando Ave, Suite B-21, Lake City, FL 32055
Phone: 386-758-1008 Fax: 386-758-2160

MOBILE HOME INSTALLERS AGENT AUTHORIZATION

I, Glenn Williams Jr., give this authority and I do certify that the below
Installers Name
referenced person(s) listed on this form is/are under my direct supervision and control and
is/are authorized to purchase permits, call for inspections and sign on my behalf.

Printed Name of Authorized Person	Signature of Authorized Person	Agents Company Name
Brodence Pack		BKP Permitting

I, the license holder, realize that I am responsible for all permits purchased, and all work done
under my license and I am fully responsible for compliance with all Florida Statutes, Codes, and
Local Ordinances.

I understand that the State Licensing Board has the power and authority to discipline a license
holder for violations committed by him/her or by his/her authorized person(s) through this
document and that I have full responsibility for compliance granted by issuance of such permits.

License Holders Signature (Notarized)

1111054858 2-19-21
License Number Date


NOTARY INFORMATION:


STATE OF: Florida COUNTY OF: Alachua

The above license holder, whose name is Glenn Williams Jr.
personally appeared before me and is known by me or has produced identification
(type of I.D.) _____ on this 19th day of February, 2021

NOTARY'S SIGNATURE

(Seal/Stamp)





Prepared by and return to:

Daniel R. Monteau
Haile Title Company
4739-B NW 53rd Avenue
Gainesville, FL 32653
(352) 371-6264
File No HT-18-592

Parcel Identification No 09-6S-17-09630-006

[Space Above This Line For Recording Data]

WARRANTY DEED

(STATUTORY FORM – SECTION 689.02, F.S.)

This indenture made the 28th day of November, 2018 between Barbara Jandt, a married woman conveying her non-homestead property, whose post office address is 1010 Cherry Hills Drive, Sun City Center, FL 33573, of the County of Hillsborough, State of Florida, Grantor, to Vasiliy Gusev, a married man, whose post office address is PO Box 30406, Ft. Lauderdale, FL 33303, State of Florida, Grantee:

Witnesseth, that said Grantor, for and in consideration of the sum of TEN DOLLARS (U.S.\$10.00) and other good and valuable considerations to said Grantor in hand paid by said Grantee, the receipt whereof is hereby acknowledged, has granted, bargained, and sold to the said Grantee, and Grantee's heirs and assigns forever, the following described land, situate, lying and being in Columbia, Florida, to-wit:

Lot 6 Of "HEATHERWOOD", A Subdivision As Per Plat Thereof Recorded In Plat Book "5", Page 51 Of The Public Records Of Columbia County, Florida.

Together with all the tenements, hereditaments and appurtenances thereto belonging or in anywise appertaining.

Subject to taxes for 2019 and subsequent years, not yet due and payable; covenants, restrictions, easements, reservations and limitations of record, if any.

TO HAVE AND TO HOLD the same in fee simple forever.

And Grantor hereby covenants with the Grantee that the Grantor is lawfully seized of said land in fee simple, that Grantor has good right and lawful authority to sell and convey said land and that the Grantor hereby fully warrants the title to said land and will defend the same against the lawful claims of all persons whomsoever.

In Witness Whereof, Grantor has hereunto set Grantor's hand and seal the day and year first above written.

Signed, sealed and delivered in our presence:

1. Marilyn Baldelli

WITNESS print name Marilyn Baldelli

2. Binta

WITNESS print name BINTA KRAUTLER

Barbara Jandt
Barbara Jandt

STATE OF Florida

COUNTY OF Hillsborough

The foregoing instrument was acknowledged before me this 23 day of November, 2018, by Barbara Jandt.

Binta

Signature of Notary Public

Print, Type/Stamp Name of Notary

Personally Known: _____ OR Produced Identification: ☒

Type of Identification

Produced: FLDL JS30-070-46-725-0

