

12 Summers

PERMIT WORKSHEET

PERMIT NUMBER 46614

Installer Christopher Din License # MH0000153


Address of home being installed SW Highway 54

Manufacturer Jackson Length x width 32x52

NOTE: If home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in

Installer's initials CO

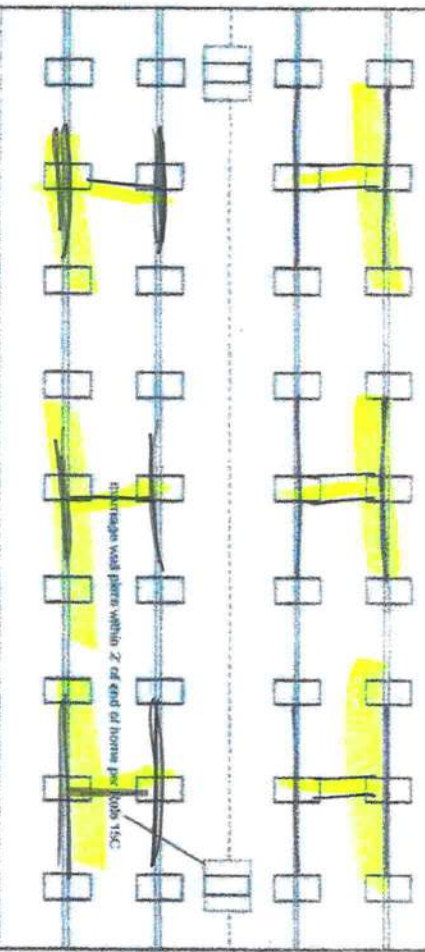

6/30/20

New Home ☒ Used Home ☐
Home installed to the Manufacturer's Installation Manual ☒
Home is installed in accordance with Rule 15-C ☐
Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
Double wide ☒ Installation Decal # ☐
Triple/Quad ☐ Serial # ☐

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	10' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'
3500 psf	8'	9'	10'	11'	12'	13'

PIER PAD SIZES

I-beam pier pad size 24x24
Perimeter pier pad size 20x20
Other pier pad sizes (required by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

POPULAR PAD SIZES

Pad Size	Sq ft
16 x 16	256
18 x 18	324
20 x 20	400
22 x 22	484
24 x 24	576
26 x 26	676

ANCHORS

4 ft 5 ft

FRAME TIES

within 2' of end of home, spaced at 5' 4" oc

OTHER TIES

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD) ☐
Manufacturer: Stabilizing Device w/ Lateral Arms ☐
Manufacturer: 1101 AS Systems ☐
Sidewall ☐
Longitudinal Marriage Wall ☐
Shearwall ☐
Number 26

PERMIT NUMBER

PERMIT WORKSHEET

Page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 100 psi or check here to declare 1000 lb soil ☒ without testing

X ☐ X ☐ X ☐

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb increments, take the lowest reading and round down to that increment.

X ☐ X ☐ X ☐

TORQUE PROBE TEST

The results of the torque probe test is Assumed with 110 ft-lb
here if you are declaring 5" anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewalk locations. I understand 5 ft. anchors are required at all centerline the points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb holding capacity.

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Christopher Dln

Date Tested

6-15-76

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg

Connect all potable water supply piping to an existing water meter, water tap or other independent water supply systems. Pg



Site Preparation

Debris and organic material removed ☐ Swale ☐ Pad ☒ Other ☐

Fastening multi-wide units

Type Fastener: 6" x 1/2" length Spacing: 18" hold
Type Fastener: Galv metal Spacing: every other
Type Fastener: Galv metal Spacing: every other
or used homes a min. 30 gauge, 8" wide, galvanized metal strip
roofing nails at 2" on center on both sides of the centerline

Gasket (weatherproofing requirement)

Understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

C.C.B.

Type gasket

foam

Installed: ☐
Between Floors: Yes ☐
Between Walls: Yes ☐
Bottom of ridgebeam: Yes ☐

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed: Yes ☒ No ☐
Drain vent installed outside of skirting: Yes ☐ N/A ☒
Range downflow vent installed outside of skirting: Yes ☐ N/A ☒
Drain lines supported at 4 foot intervals: Yes ☐
Electrical crossovers protected: Yes ☒
Other: ☐

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature

[Signature]

Date

6-25-76



www-jachomes.com

(727) 726-1138

COLUMN INFO. TABLE				COLUMN PAD - MIN. SIZES [eq. in.]					
COL. NO./IN.	SPAN	LOAD (PS PER SQ FT)	1000 psf SOIL	1500 psf SOIL	2000 psf SOIL	2500 psf SOIL	3000 psf SOIL	3500 psf SOIL	
1	19'-4"	45/5	659	439	329	264	264	264	
2	19'-4"	45/5	659	439	329	264	264	264	
3	0"	0	0	0	0	0	0	0	
4	0"	0	0	0	0	0	0	0	
5	0"	0	0	0	0	0	0	0	
6	0"	0	0	0	0	0	0	0	
7	0"	0	0	0	0	0	0	0	
8	0"	0	0	0	0	0	0	0	
9	0"	0	0	0	0	0	0	0	
10	0"	0	0	0	0	0	0	0	

REFER TO AD-TD-0250 THROUGH
AD-TD-0254 FOR COLUMN ANCHOR SIZES

[illegible]

N10 = SEE NOTE 10.
REFER TO SL-D1-0005 FOR
ADDITIONAL PIER REQUIREMENTS

WARNING:

INSTALLING A MANUFACTURED STRUCTURE/BUILDING CAN BE EXTREMELY DANGEROUS. ONLY QUALIFIED PERSONNEL SHOULD ATTEMPT TO INSTALL MANUFACTURED STRUCTURE/BUILDING. IMPROPER PROCEDURES AND/OR TECHNICAL INFORMATION COULD RESULT IN SERIOUS INJURY OR DEATH. IN ADDITION TO THE DANGER TO PERSONS, IMPROPER INSTALLATION COULD RESULT IN EXTENSIVE/COSTLY DAMAGE TO THE MANUFACTURED STRUCTURE. ANY ATTEMPT AT INSTALLATION BY YOU ARE NOT QUALIFIED AND/OR UNTRAINED PERSONS COULD HAVE PERSONAL AND/OR EQUIPMENT

CAUTIONS

[illegible]


NOTES:

1. REFER TO THE MODEL APPROVAL FOR PLAN-SPECIFIC INFORMATION.
2. REFER TO THE ACCORDION HOWER SETUP MANUAL AND ADDITIONAL FOR COMPLETE INSTALLATION INSTRUCTIONS. PIERRS CAN BE RELATED AND/OR SPANS IN/BE AND PER THE SETUP MANUAL.
3. REFER TO SCHEDULERS FOR ADDITIONAL PIR HUB MOUNTS.
4. REFER TO THE APPROVED DESIGN PLAN FOR SHEARWALL LOCATIONS AND LOADS.
5. REFER TO ASD-100 FOR SHEARWALL APPLICATIONS AND THE COMMENTS.
6. REFER TO THE APPROVED FLOOR PLAN FOR SPECTER COLUMN LOCATIONS. COLUMNS PIERRS SHALL BE LOCATED WITHIN 9" OF EITHER SIDE OF THE COLUMNS. ADDITIONAL PIERRS MAY BE REQUIRED ALONG THE SCHEDULING LINE. SEE THE SETUP MANUAL FOR SPECIFICS.
7. ALL IN-FLIGHT FLOOR SYSTEMS INCLUDING PERIMETER AND MAINING LINE BRACING.
8. ALL PER-FLOOR SYSTEMS WITH MORE THAN 1-4-2-2 REQUIRE PIERRS FOR MAINING LINE BRACING.
9. ANY ADDITIONAL AREA WITH A HIGHER BEAM OR A SPECTER/AL ATTACHMENT SHALL HAVE PIERRS AND ANCHORS SCHEDULED AND LOCATED THERE. 40" O.C. MAXIMUM. 1" SPACING WITHIN AREA'S MAY BE REQUIRED BEFORE INSTALLATION. REFER TO THE ACCORDION HOWER'S SETUP MANUAL FOR SPECIFIC SCHEDULING AND SCHEDULING WHEN THE ATTACHED STRUCTURE HAS FLOOR WALL CONSTRUCTION OR IS DESIGNATED AND CONSTRUCTED TO BE SELF-SUPPORTING. THESE ADDITIONAL PIERRS AND ANCHORS ARE NOT REQUIRED.
10. MAX. PIERR SPACING: 10' 0" H-SPAN IS 9' 0". MAX. PIERR SPACING: 10' 0" OR 10' 1" H-SPAN IS 10' 0". SEE NOTE 2 OF PIERRS SCHEDULING THROUGHOUT THE PROJECT.

REFER TO SL-01-0020, SL-01-0021, AND OTHER DETAILS IN THE SET-UP MANUAL FOR MAXIMUM HEIGHT
(THIS IS NOT DESIGNED, NOR INTENDED, TO BE A STILT FOUNDATION)

THIS BLOCKING DIAGRAM IS PROVIDED AS A COURTESY ONLY. THE LICENSED SET-UP CONTRACTOR SHALL REVIEW THIS DETAIL AND VERIFY COMPLIANCE. THE LICENSED SET-UP CONTRACTOR IS RESPONSIBLE AND LIABLE FOR ALL INSTALLATION.

*SPACING FOR HUNT PIER IS EQUAL TO
DOWNHUNT FOR ALLOWED PIER SPACING.
ON 1" HUNT PIER SPACING,
WHICH IS 15" LONG.

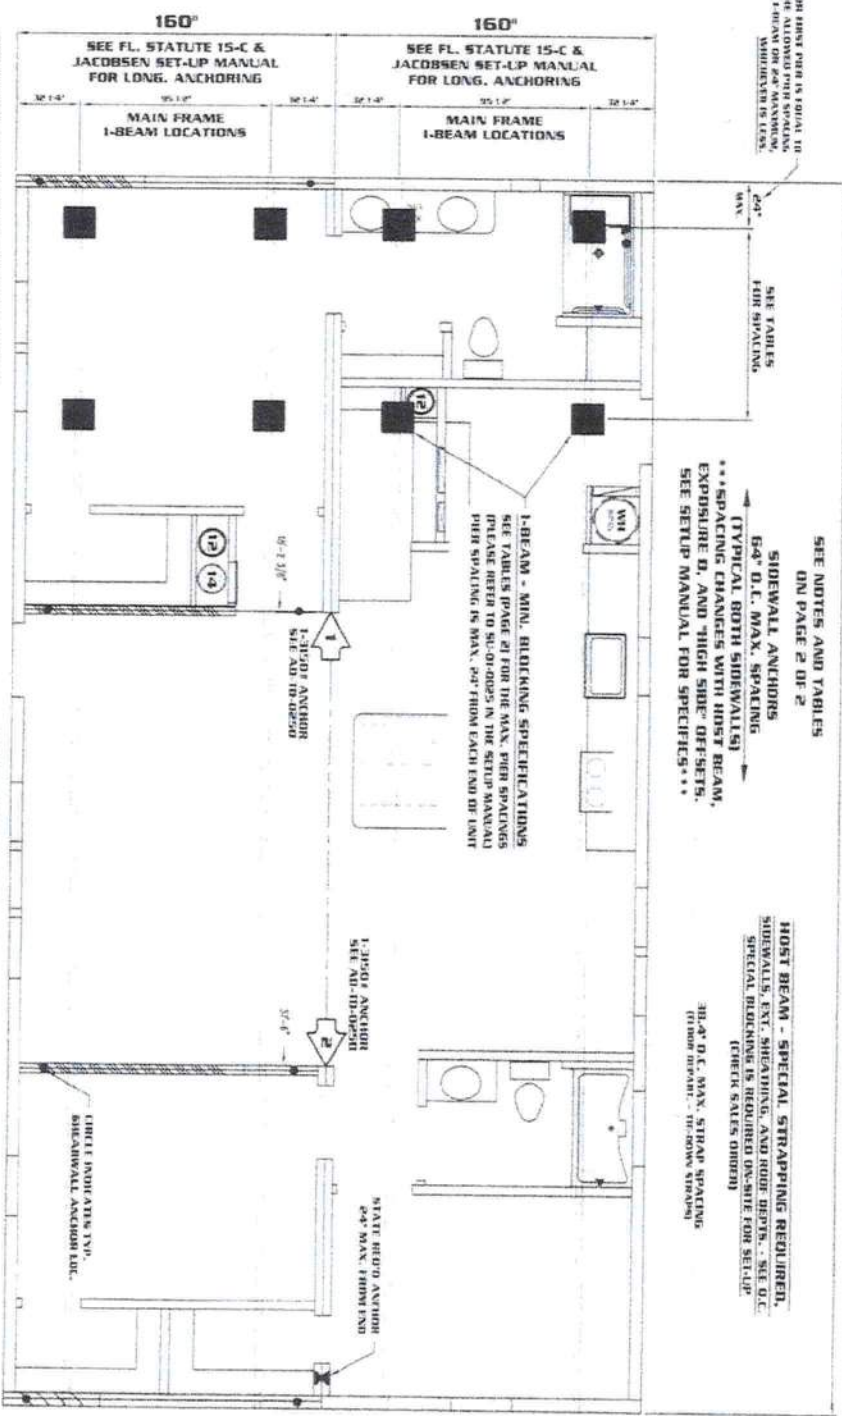


SEE NOTES AND TABLES
ON PAGE 2 OF 2

SHEARWALLS TIE-DOWN STRAPS ARE NOT INSTALLED AT THE FACTORY WHEN SHEARWALL IS LOCATED DIRECTLY OVER SOLID I-BEAM HEADER. SET-UP IS REQUIRED TO INSTALL THE SHEARWALL STRAPS OVER THE I-BEAM HEADER PER AD-TO-0050 (PAGE 48) IN THE SET-UP MANUAL ADDENDUM. STRAPS AND PIERS SHALL BE INSTALLED AT BOTH ENDS OF HEADER.



SEE NOTES AND TABLES ON PAGE 2 OF 2
SEE WARNINGS AND CAUTIONS ON PAGE 2

REFER TO SU-01-0005 FOR
ADD'L PIER REQUIREMENTS



JACOBSEN HOMES
PO BOX 368, 600 PARKWAY CT.
SAFETY HARBOR, FLORIDA 34695
727-726-1138
www.jacobshomes.com

REFER TO THE JACOBSEN HOMES SETUP MANUAL AND
ADDENDUM FOR COMPLETE INSTALLATION INSTRUCTIONS

HUD WIND ZONE - 2
HUD WIND EXPOSURE CATEGORY - C
36655 - PAGE 1 OF 2

REFER TO SU-01-0020, SU-01-0021, AND OTHER DETAILS IN THE SET-UP MANUAL FOR MAXIMUM HEIGHT
(THIS IS NOT DESIGNED, NOR INTENDED, TO BE A STILT FOUNDATION)

MODEL # IMP-45213B-655

JACOBSEN HOMES
IMP-36,655



THIS BLOCKING DIAGRAM IS PROVIDED AS A COURTESY ONLY. THE LICENSED SET-UP
CONTRACTOR SHALL REVIEW THIS DETAIL AND VERIFY COMPLIANCE. THE LICENSED
SET-UP CONTRACTOR IS RESPONSIBLE AND LIABLE FOR ALL INSTALLATION.
