

DATE 01/25/2010

Columbia County Building Permit
This Permit Must Be Prominently Posted on Premises During Construction

PERMIT
000028337

APPLICANT BO ROYALS PHONE 386.754.6737
ADDRESS 4068 US 90-W LAKE CITY FL 32055
OWNER THOMAS & REBECCA PASZKIEWICZ PHONE 954.649.0145
ADDRESS 310 SW HORSE WAY LAKE CITY FL 32055
CONTRACTOR WENDELL CREWS PHONE 352.351.6100
LOCATION OF PROPERTY 90-W TO SR 247-S, TL TO CYPRESS LAKE ROAD, TR TO HORSE WAY, TL
2ND PROPRTY ON R AFTER CURVE.
TYPE DEVELOPMENT M/H/UTILITY ESTIMATED COST OF CONSTRUCTION 0.00
HEATED FLOOR AREA TOTAL AREA HEIGHT STORIES
FOUNDATION WALLS ROOF PITCH FLOOR
LAND USE & ZONING A-3 MAX. HEIGHT
Minimum Set Back Requirments: STREET-FRONT 30.00 REAR 25.00 SIDE 25.00
NO. EX.D.U. 0 FLOOD ZONE X DEVELOPMENT PERMIT NO.

PARCEL ID 35-4S-15-00407-122 SUBDIVISION CYPRESS LAKE HILLS
LOT 22 BLOCK PHASE UNIT TOTAL ACRES 5.01

IH0000629
Culvert Permit No. Culvert Waiver Contractor's License Number Applicant/Owner/Contractor
EXISTING 10-0004 BLK WR Y
Driveway Connection Septic Tank Number LU & Zoning checked by Approved for Issuance New Resident
COMMENTS: 1 FOOT ABOVE ROAD.

Check # or Cash 30208

FOR BUILDING & ZONING DEPARTMENT ONLY

(footer/Slab)

Temporary Power Foundation Monolithic
 date/app. by date/app. by date/app. by
Under slab rough-in plumbing Slab Sheathing/Nailing
 date/app. by date/app. by date/app. by
Framing Insulation
 date/app. by date/app. by
Rough-in plumbing above slab and below wood floor Electrical rough-in
 date/app. by date/app. by
Heat & Air Duct Peri. beam (Lintel) Pool
 date/app. by date/app. by date/app. by
Permanent power C.O. Final Culvert
 date/app. by date/app. by date/app. by
Pump pole Utility Pole M/H tie downs, blocking, electricity and plumbing
 date/app. by date/app. by date/app. by
Reconnection RV Re-roof
 date/app. by date/app. by date/app. by

BUILDING PERMIT FEE \$ 0.00 CERTIFICATION FEE \$ 0.00 SURCHARGE FEE \$ 0.00
MISC. FEES \$ 300.00 ZONING CERT. FEE \$ 50.00 FIRE FEE \$ 57.78 WASTE FEE \$ 150.75
FLOOD DEVELOPMENT FEE \$ FLOOD ZONE FEE \$ 25.00 CULVERT FEE \$ **TOTAL FEE** 583.53
INSPECTORS OFFICE CLERKS OFFICE

NOTICE: IN ADDITION TO THE REQUIREMENTS OF THIS PERMIT, THERE MAY BE ADDITIONAL RESTRICTIONS APPLICABLE TO THIS PROPERTY THAT MAY BE FOUND IN THE PUBLIC RECORDS OF THIS COUNTY. AND THERE MAY BE ADDITIONAL PERMITS REQUIRED FROM OTHER GOVERNMENTAL ENTITIES SUCH AS WATER MANAGEMENT DISTRICTS, STATE AGENCIES, OR FEDERAL AGENCIES.

"WARNING TO OWNER: YOUR FAILURE TO RECORD A NOTICE OF COMMENCEMENT MAY RESULT IN YOUR PAYING TWICE FOR IMPROVEMENTS TO YOUR PROPERTY. IF YOU INTEND TO OBTAIN FINANCING, CONSULT WITH YOUR LENDER OR AN ATTORNEY BEFORE RECORDING YOUR NOTICE OF COMMENCEMENT."

EVERY PERMIT ISSUED SHALL BECOME INVALID UNLESS THE WORK AUTHORIZED BY SUCH PERMIT IS COMMENCED WITHIN 180 DAYS AFTER ITS ISSUANCE, OR IF THE WORK AUTHORIZED BY SUCH PERMIT IS SUSPENDED OR ABANDONED FOR A PERIOD OF 180 DAYS AFTER THE TIME THE WORK IS COMMENCED. A VALID PERMIT RECIEVES AN APPROVED INSPECTION EVERY 180 DAYS. WORK SHALL BE CONSIDERED NOT SUSPENDED, ABANDONED OR INVALID WHEN THE PERMIT HAS RECIEVED AN APPROVED INSPECTION WITHIN 180 DAYS OT THE PREVIOUS INSPECTION.

The Issuance of this Permit Does Not Waive Compliance by Permittee with Deed Restrictions.

PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only (Revised 1-10-08) Zoning Official B2K 10.01.00 Building Official WR 1-14-10
 AP# 1001-03 Date Received 1/5 By JW Permit # 28337
 Flood Zone X Development Permit N/A Zoning A-3 Land Use Plan Map Category A-3
 Comments _____
 FEMA Map# N/A Elevation N/A Finished Floor 2' above River River N/A In Floodway N/A
☒ Site Plan with Setbacks Shown ☒ EH # 10-0004 ☐ EH Release ☒ Well letter ☒ Existing well
☒ Recorded Deed or Affidavit from land owner ☒ Letter of Auth. from installer ☐ State Road Access
☐ Parent Parcel # _____ ☐ STUP-MH Parcel # _____ ☐ F W Comp. letter
 IMPACT FEES: EMS _____ Fire _____ Corr. FEES, EMS _____ Road/Code _____
 School _____ = TOTAL 2 Sussex School _____

Property ID # 35-45-15-00407-122 Subdivision Cypress Lake Hills - Lot 22

- New Mobile Home ☒ Used Mobile Home ☐ New Mobile Home MH Size 28x56 Year 2010
- Applicant William "Bo" Royals Phone # 754-6737
- Address 4068 W 90 West Lake City, FL 32055
- Name of Property Owner Thomas & Rebecca Paszkiewicz Phone # (954) 649-0145
- 911 Address 310 SW HORSEWAY, LAKE CITY, FL 32024
- Circle the correct power company - FL Power & Light Clay Electric
 (Circle One) - Suwannee Valley Electric - Progress Energy
- Name of Owner of Mobile Home Same as property owner Phone # _____
 Address "
- Relationship to Property Owner _____ Relationship to Property Owner _____
- Current Number of Dwellings on Property 0 Current Number of Dwellings on Property _____
- Lot Size 5.01 Total Acreage 5.01 acres
- Do you : Have Existing Drive or Private Drive or need Culvert Permit or Culvert Waiver (Circle one)
 (Currently using) (Blue Road Sign) (Putting in a Culvert) (Not existing but do not need a Culvert)
- Is this Mobile Home Replacing an Existing Mobile Home No (owe)
- Driving Directions to the Property 247 S TURN Rt. on Cypress Lake Rd.
Turn Left on Horseway and property on Right after curve
Lot # 22
- Name of Licensed Dealer/Installer Wendell Crews Phone # 352-351-6100
- Installers Address 4650 NE 35th Ocala, FL 34479
- License Number FH0000629 Installation Decal # 307263

30208

PERMIT WORKSHEET


Page 1 of 2

Installer Dentell Crews License # TH0000629
 Manufacturer Southern Energy Length x Width 28' x 56'
 Name of Owner of this Mobile Home Thomas & Rebecca Paszkiewicz
 Phone (954) 562-6700
 Address _____

NOTE: If home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials DC

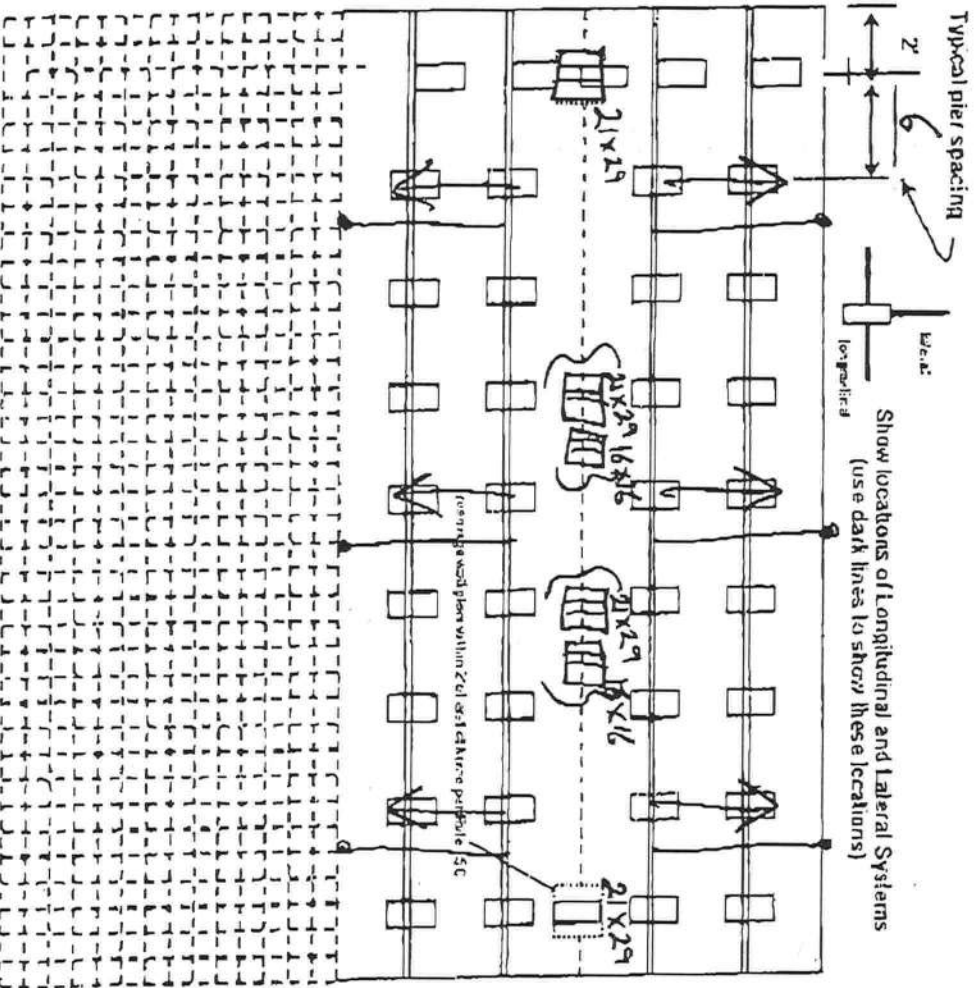

New Home ☒ Used Home ☐ Year 2006
 Home installed to the Manufacturer's installation Manual ☒
 Home is installed in accordance with Rule 15-C ☐
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Detail # 307263
 Triple Quad ☐ Serial # DSEAL1992948

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	18' x 18' (324)	18' x 18' (324)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'
3500 psf	8'	9'	10'	11'	12'	13'

* Interpolated from Rule 15C-1 for spacing table

PIER PAD SIZES

I-beam pier pad size 21' x 29'
 Perimeter pier pad size 16' x 16' Doors
 Other pier pad sizes (required by the mfg) 16' x 16' 8' x 8'

POPULAR PAD SIZES

Pad Size	Sq in
16' x 16'	256
16' x 18'	288
18.5' x 18.5'	342
16' x 22.5'	360
17' x 22'	374
13' 1/4' x 26' 1/4'	348
20' x 20'	400
17' 3/16' x 25' 3/16'	441
17' 1/2' x 25' 1/2'	448
24' x 24'	576
26' x 26'	676

Draw the approximate locations of mainline wall openings 4 foot or greater. Use this symbol to show the piers.

List all mainline wall openings greater than 4 foot and their pier pad sizes below

Opening 21' Pier pad size 21' x 29' 21' x 16'

ANCHORS

4 ft ☒ 5 ft ☐

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

OTHER TIES

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer OLIVER 11010

Manufacturer Wynbo

Longitudinal

Marriage wall

Manufacturer Oliver

PERMIT NUMBER

PERMIT WORKSHEET

Page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to psi or check here to declare 1000 lb soil without testing

X ☐ X ☐ X ☐

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations
2. Take the reading at the depth of the footer
3. Using 500 lb increments, take the lowest reading and round down to that increment

X ☐ X ☐ X ☐

TORQUE PROBE TEST

The results of the torque probe test is inch pounds or check here if you are declaring 5 anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A slate approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. 1 underslashed 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb lifting capacity

WC Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Glenn Cirus

Date Tested

1-4-10

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units Pg. 39

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. 39

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. 40

Site Preparation

Debris and organic material removed ☒
 Water drainage: Natural ☒ Swale ☒ Pad ☒ Other ☒

Fastening multi-wide units

Floor: Type Fastener: Lag Length: 3/8 x 5" Spacing: 16"
 Walls: Type Fastener: Screw Length: 1/8 x 4" Spacing: 16"
 Roof: Type Fastener: Metal Length: 5/8" Spacing: 24"
 For used homes a min 30-gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline

Gasket (weatherproofing integrity)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket

Installer's initials

WC

Type gasket

foam

Installed ☒
 Between Floors Yes ☒
 Between Walls Yes ☒
 Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped Yes ☒ Pg. 15
 Sliding on units is installed to manufacturer's specifications. Yes ☒
 Fireplace chimney installed so as not to allow intrusion of rain water Yes ☒


Miscellaneous

Skirting to be installed Yes ☒ No ☒
 Dryer vent installed outside of skirting Yes ☒ N/A
 Range downflow vent installed outside of skirting Yes ☒ N/A
 Drain lines supported at 4 foot intervals Yes ☒
 Electrical crossovers protected. Yes ☒

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature

Glenn Cirus Date 1-4-10

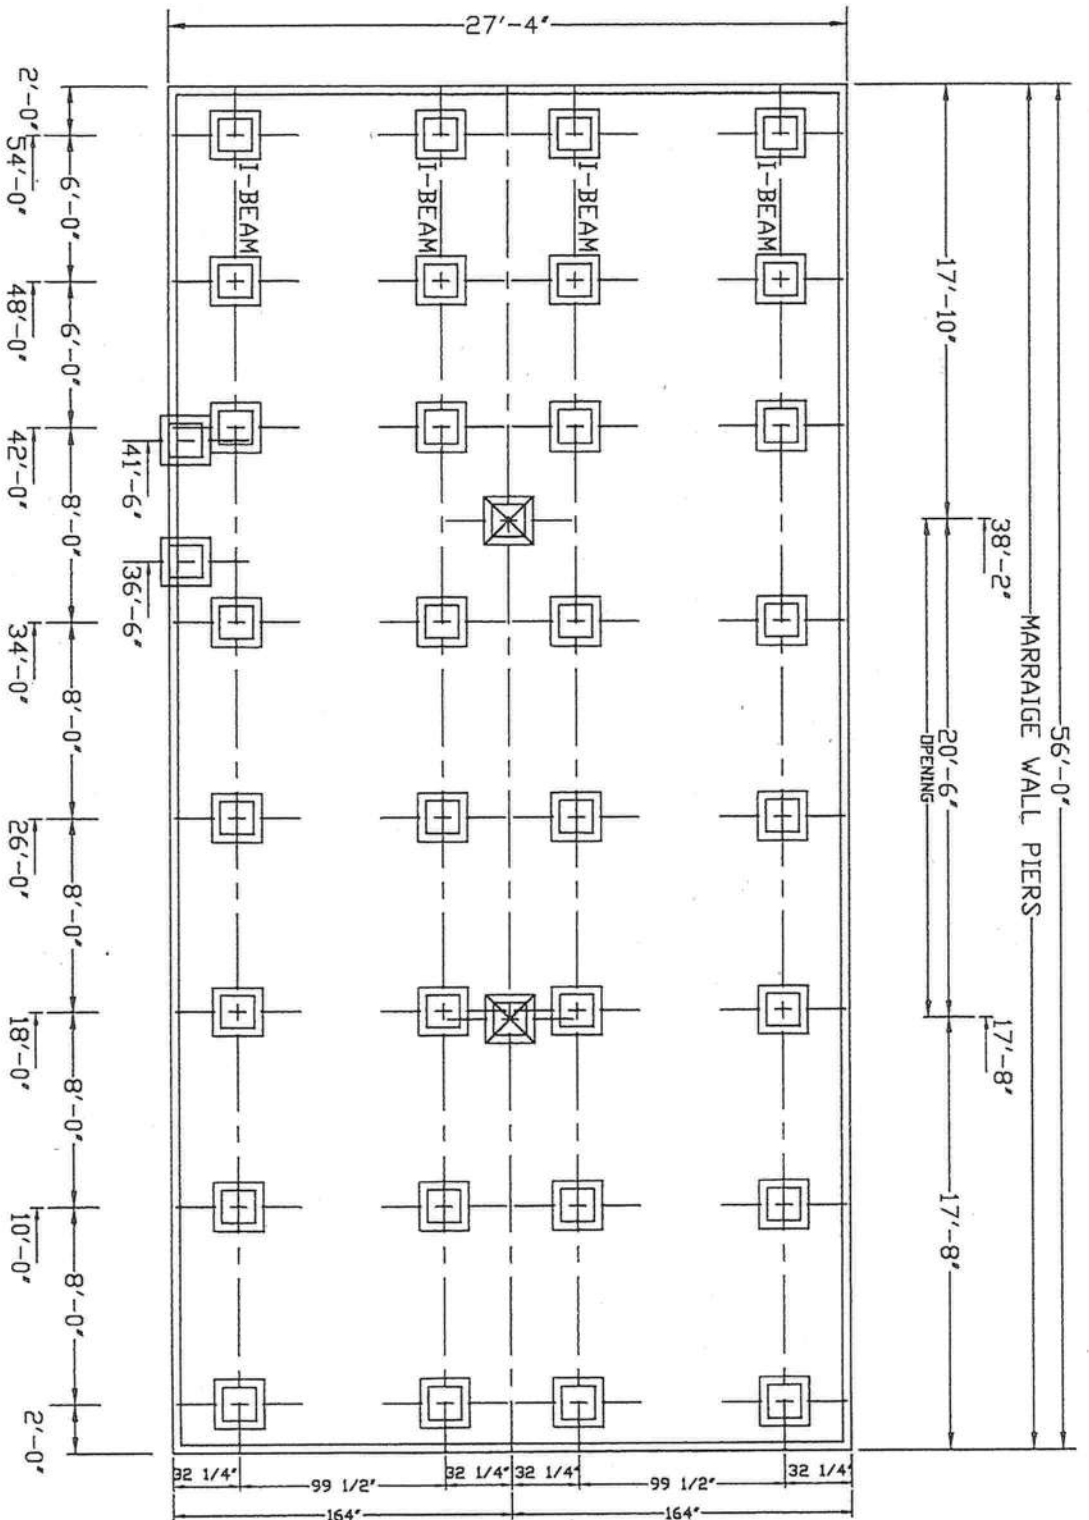

NOTES:

SEHOMES IS NOT RESPONSIBLE FOR THE FOUNDATION, THE WORK MUST CONFORM TO ALL STATE, LOCAL AND FHA REQUIREMENTS AND STANDARD CONSTRUCTION PRACTICES. SEHOMES IS NOT RESPONSIBLE FOR THE PIER LOCATIONS. THIS DRAWING IS ONLY A GUIDE. ALL PIER LOCATIONS MUST CONFORM TO SEHOMES INSTALLATION MANUAL.

THE REQUIRED PIER SPACING FOR ALL UNITS IS 2'-0" MAX. FROM EITHER END AND NOT OVER 8'-0" OC. THEREAFTER, SINCE THIS IS THE MIN. NUMBER OF PIERS REQUIRED BY THE MANUFACTURER, THEY MUST BE LOCATED UNDER THE MAIN BEAMS.

ADDITIONAL PIERS REQUIRED UNDER MARRIAGE WALLS AND EXTERIOR WALLS, UNDER TERMINAL STUDS AND OPENINGS GREATER THAN 4'-0", ALSO AT CORNERS OF THE FLOOR WHEN THE FLOOR OVERHANGS THE FRAME.

YOUR LIFE		SALESMAN:	
YOUR HOME		DATE: 6-23-09	
YOUR STYLE		DRAWN BY: S. PHILLIPS	
ENERGY HOMES		DEALER/CUSTOMER:	
a division of Eldorado, Inc.		STANDARD	

SEP 25-2007 09:26H FROM: OLIVER TECH

106: 138502

TO: 1385516100

F.1.1

FAX 352-401-0401



Installation Instructions for ABS Pads

For use on all Mobile and Manufactured Homes, including
HUD approved Homes and Modular Housing

part # 5503500 and other patents pending

GENERAL INSTRUCTIONS:

1. All pads are to be installed flat side down, ribbed side up.
2. The ground under the pads should be leveled as smooth as possible with all vegetation removed. Pads to be placed on fully compacted or undisturbed soil, at or below the frost-line, or per local jurisdiction.
3. Pier & pad spacing will be determined by the manufacturer's written set-up instructions or any local or state codes.
4. The open cells between the ribbing on the upper side of the pads may be filled with soil or sand after installation to prevent any accumulation of stagnant water in the pads.
5. A pocket penetrometer may be used to determine the actual soil bearing value. If soil-testing equipment is not available, use an assumed soil value of 1000 lbs. / square foot.
6. All pad sizes shown are nominal dimensions and may vary up to 1/8"
7. The maximum deflection in a single pad is 5/8" measured from the highest point to the lowest point of the top face. (NOTE: Actual test results were less than 5/8")
8. In frost areas, a 6" deep confined gravel base installed in well drained, non-frost susceptible soil is recommended.
9. Pad loads are the same when using single stack or double stack blocks.
10. The maximum load at any intermediate soil value may be determined as the average of the next lower and next higher soil value given in the table below.
11. Any configuration (see reverse side) may be used to replace a home manufacturer's recommended concrete or wood base pad.
12. If the home manufacturer shows soil densities greater than 3000 lb. when using ABS pads, do not exceed 3000 lb. soil pier spacings per set up manual.

Pad Size	ID No.	Pad Area	1000 PSF Soil	2000 PSF Soil	3000 PSF Soil
OVAL 16" x 18.5"	1055-23	288 sq. in.	2000 lbs.	4000 lbs.	6000 lbs.
OVAL 17" x 22"	1055-16	360 sq. in.	2500 lbs.	5000 lbs.	7500 lbs.
OVAL 17.5" x 22.5"	1055-21	384 sq. in.	2667 lbs.	5334 lbs.	8000 lbs. *
OVAL 17.5" x 25.5"	1055-17	432 sq. in.	3000 lbs.	6000 lbs.	9000 lbs. *
OVAL 21" x 29"	1055-22	576 sq. in.	4000 lbs.	8000 lbs.	12000 lbs.
OVAL 23.25" x 31.25"	1055-20	675 sq. in.	4694 lbs.	9388 lbs. *	14082 lbs. *

Pad Size	ID No.	Pad Area	1000 PSF Soil	2000 PSF Soil	3000 PSF Soil
16" x 16"	1055-14	256 sq. in.	1780 lbs.	3560 lbs.	5340 lbs.
18.5" x 18.5"	1055-9	342 sq. in.	2373 lbs.	4746 lbs.	7119 lbs.
20" x 20"	1055-7	400 sq. in.	2750 lbs.	5500 lbs.	8250 lbs.
24" x 24"	1055-13	576 sq. in.	4000 lbs.	8000 lbs.	12000 lbs.

* Concrete blocks are required to be double blocked.


13. ALABAMA ONLY: The 16" x 16" ID# 1055-14, 16" x 18.5" ID# 1055-23, 17" x 22" ID# 1055-16, 17.5" x 22.5" ID# 1055-21, 17.5" x 25.5" ID# 1055-17 are the only pads approved in the state of Alabama, and must not have more than 5/8" deflection.

See chart below for details on correct installation in Alabama.


14. TEXAS ONLY: 17.5" x 22.5" ID# 1055-21 and 23.25" x 31.25" ID# 1055-20 may not be installed in the State of Texas.
15. Steel Piers: All pads are tested with steel piers on 1000 PSF soil density unless otherwise noted. (#16)
16. Available pads tested on 2000 PSF soil density are: ID#s 1055-14, 1055-9, 1055-7 and 1055-13.

Example: 16" x 80" section

PAD SIZE	1000 Lb Psf	2000 Lb Psf
16" x 16" Pad	29"	5' 6"
16" x 18.5" Oval Pad	3' 0"	6' 0"
17" x 22" Oval Pad	3' 9"	7' 6"
17.5" x 22.5" Oval Pad	4' 0"	8' 0"
17.5" x 25.5" Oval Pad	4' 5"	8' 0"
21" x 29" Oval Pad	6' 0"	8' 0"



Revised 5/04



OLIVER TECHNOLOGIES, INC.
FLORIDA INSTALLATION INSTRUCTIONS FOR THE
MODEL 1101 "V" SERIES ALL STEEL FOUNDATION SYSTEM
MODEL 1101 "V" (STEPS 1-15)

LONGITUDINAL ONLY: FOLLOW STEPS 1-9
FOR ADDING LATERAL ARM: Follow Steps 10-15
FOR CONCRETE APPLICATIONS: Follow Steps 16-19

ENGINEERS STAMP

ENGINEERS STAMP

1. SPECIAL CIRCUMSTANCES: If the following conditions occur - STOP! Contact Oliver Technologies at 1-800-284-7437:
- a) Pier height exceeds 48" b) Length of home exceeds 76' c) Roof eaves exceed 16" d) Sidewall height exceed 96"
 - e) Location is within 1500 feet of coast

INSTALLATION OF GROUND PAN

2. Remove weeds and debris in an approximate two foot square to expose firm soil for each ground pan (C).
 3. Place ground pan (C) directly below chassis I-beam. Press or drive pan firmly into soil until flush with or below soil.
- SPECIAL NOTE:** The longitudinal "V" brace system serves as a pier under the home and should be loaded as any other pier. It is recommended that after leveling piers, and one-third inch (1/3") before home is lowered completely on to piers, complete steps 4 through 9 below then remove jacks.

INSTALLATION OF LONGITUDINAL "V" BRACE SYSTEM

NOTE: WHEN INSTALLING THE LONGITUDINAL SYSTEM ONLY, A MINIMUM OF 2 SYSTEMS PER FLOOR SECTION IS REQUIRED. SOIL TEST PROBE SHOULD BE USED TO DETERMINE CORRECT TYPE OF ANCHOR PER SOIL CLASSIFICATION. IF PROBE TEST READINGS ARE BETWEEN 175 & 275 A 5 FOOT ANCHOR MUST BE USED. IF PROBE TEST READINGS ARE BETWEEN 276 & 350 A 4 FOOT ANCHOR MAY BE USED. USE GROUND ANCHORS WITH DIAGONAL TIES AND STABILIZER PLATES EVERY 5'4". VERTICAL TIES ARE ALSO REQUIRED ON HOMES SUPPLIED WITH VERTICAL TIE CONNECTION POINTS (PER FLORIDA REG.).

4. Select the correct square tube brace (E) length for set-up (pier) height at support location. (The 18" tube is always used as the bottom part of the longitudinal arm). Note: Either tube can be used by itself, cut and drilled to length as long as a 40 to 45 degree angle is maintained.

PIER HEIGHT
(Approx. 45 degrees Max.)

1.25" ADJUSTABLE
Tube Length

1.50" ADJUSTABLE
Tube Length

7 3/4" to 25"	22"	18"
24 3/4" to 32 1/4"	32"	18"
33" to 41"	44"	18"
40" to 48"	54"	18"

5. Install (2) of the 1.50" square tubes (E {18" tube}) into the "U" bracket (J), insert carriage bolt and leave nut loose for final adjustment.
6. Place I-beam connector (F) loosely on the bottom flange of the I-beam.
7. Slide the selected 1.25" tube (E) into a 1.50" tube (E) and attach to I-beam connectors (F) and fasten loosely with bolt and nut.
8. Repeat steps 6 through 7 to create the "V" pattern of the square tubes loosely in place. The angle is not to exceed 45 degree and not below 40 degrees.
9. After all bolts are tightened, secure 1.25" and 1.50" tubes using four(4) 1/4"-14 x 3/4" self-tapping screws in pre-drilled holes.

INSTALLATION OF LATERAL TELESCOPING TRANSVERSE ARM SYSTEM

THE MODEL 1101 "V" (LONGITUDINAL & LATERAL PROTECTION) ELIMINATES THE NEED FOR MOST STABILIZER PLATES & FRAME TIES.

NOTE: THE USE OF THIS SYSTEM REQUIRES VERTICAL TIES SPACED AT 5'4".
 FOUR FOOT (4') GROUND ANCHOR MAY BE USED EXCEPT WHERE THE HOME MANUFACTURER SPECIFIES DIFFERENT.

10. Install remaining vertical tie-down straps and 4' ground anchors per home manufacturer's instructions. NOTE: Centerline anchors to be sized according to soil torque condition. Any manufacturer's specifications for sidewall anchor loads in excess of 4,000 lbs. require a 5' anchor per Florida Code.
11. NOTE: Each system is required to have a frame tie and stabilizer attached at each lateral arm stabilizing location. This frame tie & stabilizer plate needs to be located within 18" from of center ground pan.
12. Select the correct square tube brace (H) length for set-up lateral transverse at support location. The lengths come in either 60" or 72" lengths. (With the 1.50" tube as the bottom tube, and the 1.25" tube as the inserted tube.)
13. Install the 1.50 transverse brace (H) to the ground pan connector (D) with bolt and nut.
14. Slide 1.25" transverse brace into the 1.50" brace and attach to adjacent I-beam connector (I) with bolt and nut.
15. Secure 1.50" transverse arm to 1.25" transverse arm using four (4) 1/4" - 14 x 3/4" self-tapping screws in pre-drilled holes.



OLIVER TECHNOLOGIES, INC.
 1-800-284-7437

Telephone: 931-796-4555
 Fax: 931-796-8611
www.olivertechnologies.com

284

INSTALLATION USING CONCRETE RUNNER / FOOTER

16. A concrete runner, footer or slab may be used in place of the steel ground pan.

- The concrete shall be minimum 2500 psi mix
- A concrete runner may be either longitudinal or transverse, and must be a minimum of 8" deep with a minimum width of 16 inches longitudinally or 18 inches transverse to allow proper distance between the concrete bolt and the edge of the concrete (see below).
- Footers must have minimum surface area of 441 sq. in. (i.e. 21" square), and must be a minimum of 8" deep.
- If a full slab is used, the depth must be a 4" minimum.

Special inspection of the system bracket installation is not required. Footers must allow for at least 4" from the concrete bolt to the edge of the concrete.

NOTE: The bottom of all footings, pads, slabs and runners must be per local jurisdiction.

LONGITUDINAL: (Model 1101 LC "V")

17. When using Part # 1101-W-CPCA (wetset), simply install the bracket in runner/footer OR When installing in cured concrete use Part # 101-D-CPCA (dryset). The 1101 (dryset) CA bracket is attached to the concrete using (2) 5/8"x3" concrete wedge bolts (Simpson part # S162300H 5/8" X 3" or Powers equivalent). Place the CA bracket in desired location. Mark bolt hole locations, then using a 5/8" diameter masonry bit, drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the holes. Place wedge bolts into drilled holes, then place 1101 (dry set) CA bracket onto wedge bolts and start wedge bolt nuts. Take a hammer and lightly drive the wedge bolts down by hitting the nut (making sure not to hit the top of threads on bolt). The sleeve of concrete wedge bolt needs to be at or below the top of concrete. Complete by tightening nuts.

LATERAL: (Model 1101 TC "V")


18. For wet set (part # 1101-W-TACA) installation simply install the anchor bolt into runner/footer. For dry set installation (part # 1101-D-TACA) mark bolt hole locations, then using a 5/8" diam. masonry bit, drill a hole to a minimum depth of 3". Make sure all dust and concrete is blown out of the hole. Place wedge bolts (Simpson part #S162300H 5/8" X 3" or Powers equivalent) into (D) concrete dry transverse connector and into drilled hole. If needed, take a hammer and lightly drive the wedge bolts down by hitting the nut (making sure not to hit the top of threads on bolt), then remove the nut. The sleeve of concrete wedge bolt needs to be at or below the top of concrete.

19. When using part # 1101 CVW (wetset) or 1101 CVD (dryset), install per steps 17 & 18.

Notes:

- LENGTH OF HOUSE IS THE ACTUAL BOX SIZE
- = STABILIZER PLATE AND FRAME TIE LOCATION (needs to be located within 18 inches of center of ground pan or concrete)
- ☐ = LOCATION OF LONGITUDINAL BRACING ONLY
- ☐ = TRANSVERSE & LONGITUDINAL LOCATIONS


REQUIRED NUMBER AND LOCATION OF MODEL 1101 "V" OR 1101 C "V"
BRACES FOR UP TO 4/12 ROOF PITCH

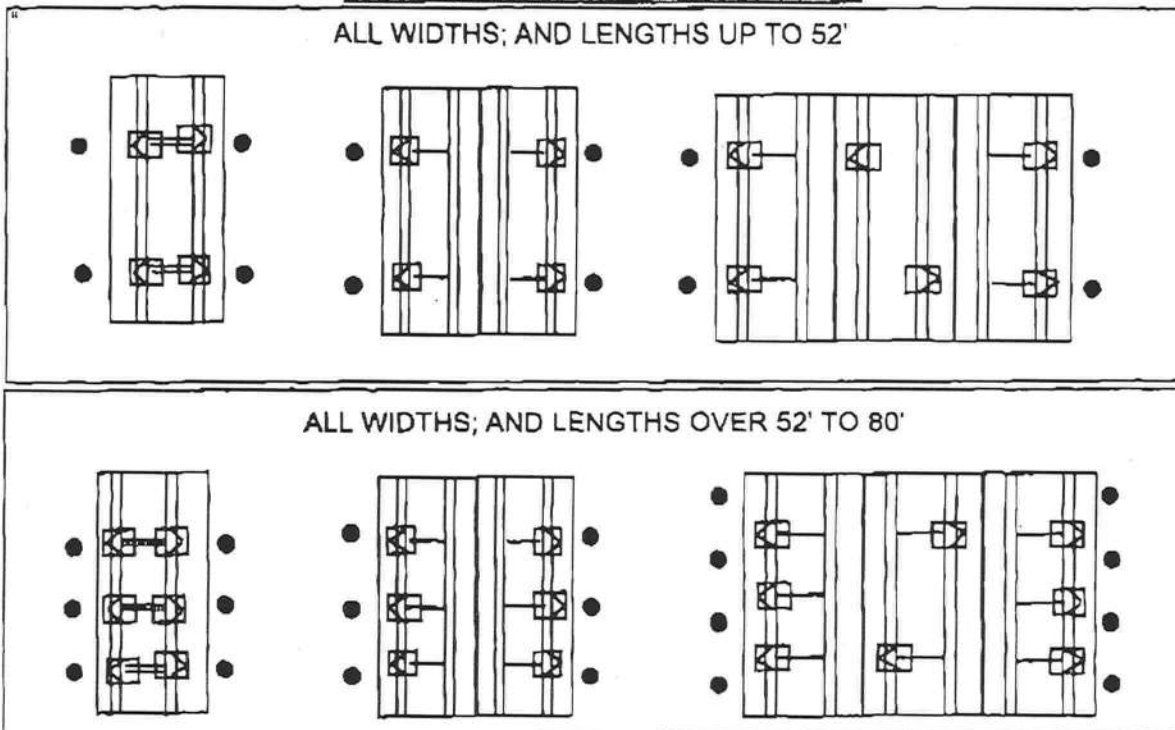

HOMES WITH 5/12 ROOF PITCH REQUIRE: PER FLORIDA REGULATIONS



6 systems for home lengths up to 52' and 8 systems for homes over 52' and up to 80'. One stabilizer plate and frame tie required at each lateral bracing system.

3-08-4

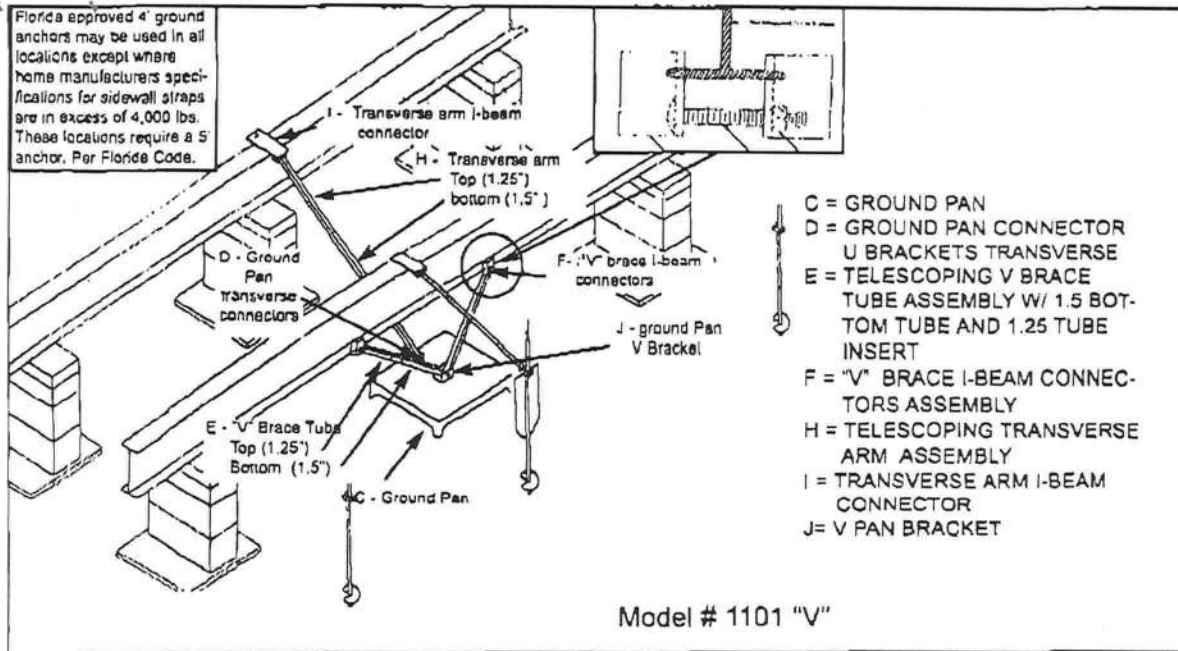



Longitude dry concrete bracket part # 1101 D-CPCA

Wet bracket part # 1101 W-CPCA not shown

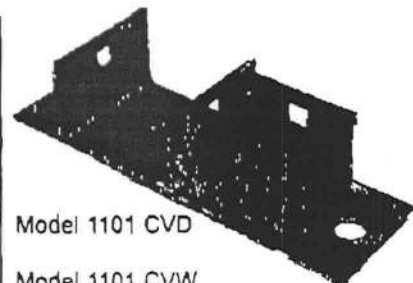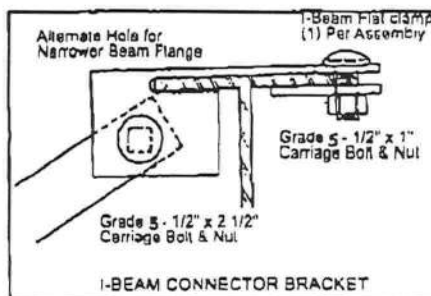

Model 1101 CVD

Model 1101 CVW not shown

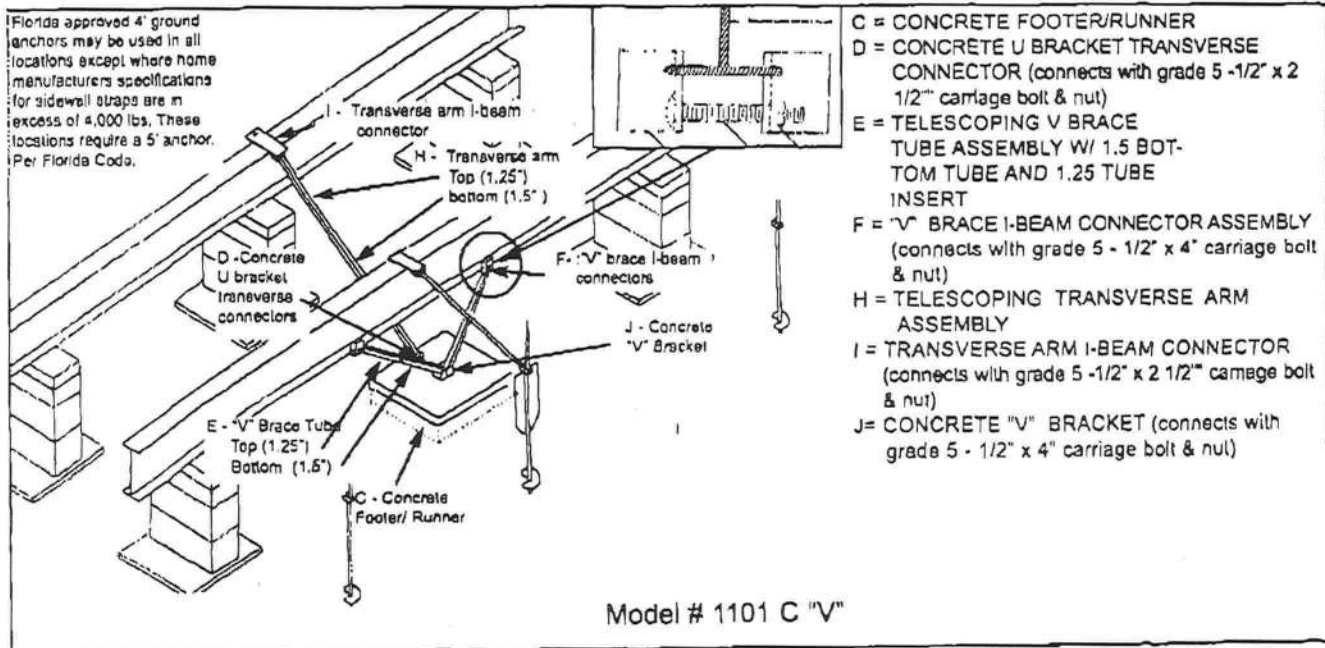

OLIVER TECHNOLOGIES, INC.
1-800-284-7437


Telephone: 931-796-4555
Fax: 931-796-8811
www.olivertechnologies.com


404

4. CLOSURE EXCEEDS 1 : 10,000.

5. SCALE AND GRAPHIC LOCATION OF FENCES AND UTILITY POLES, IF ANY, MAY BE EXAGGERATED FOR CLARITY.

6. PRM DENOTES -- PERMANENT REFERENCE MONUMENT.

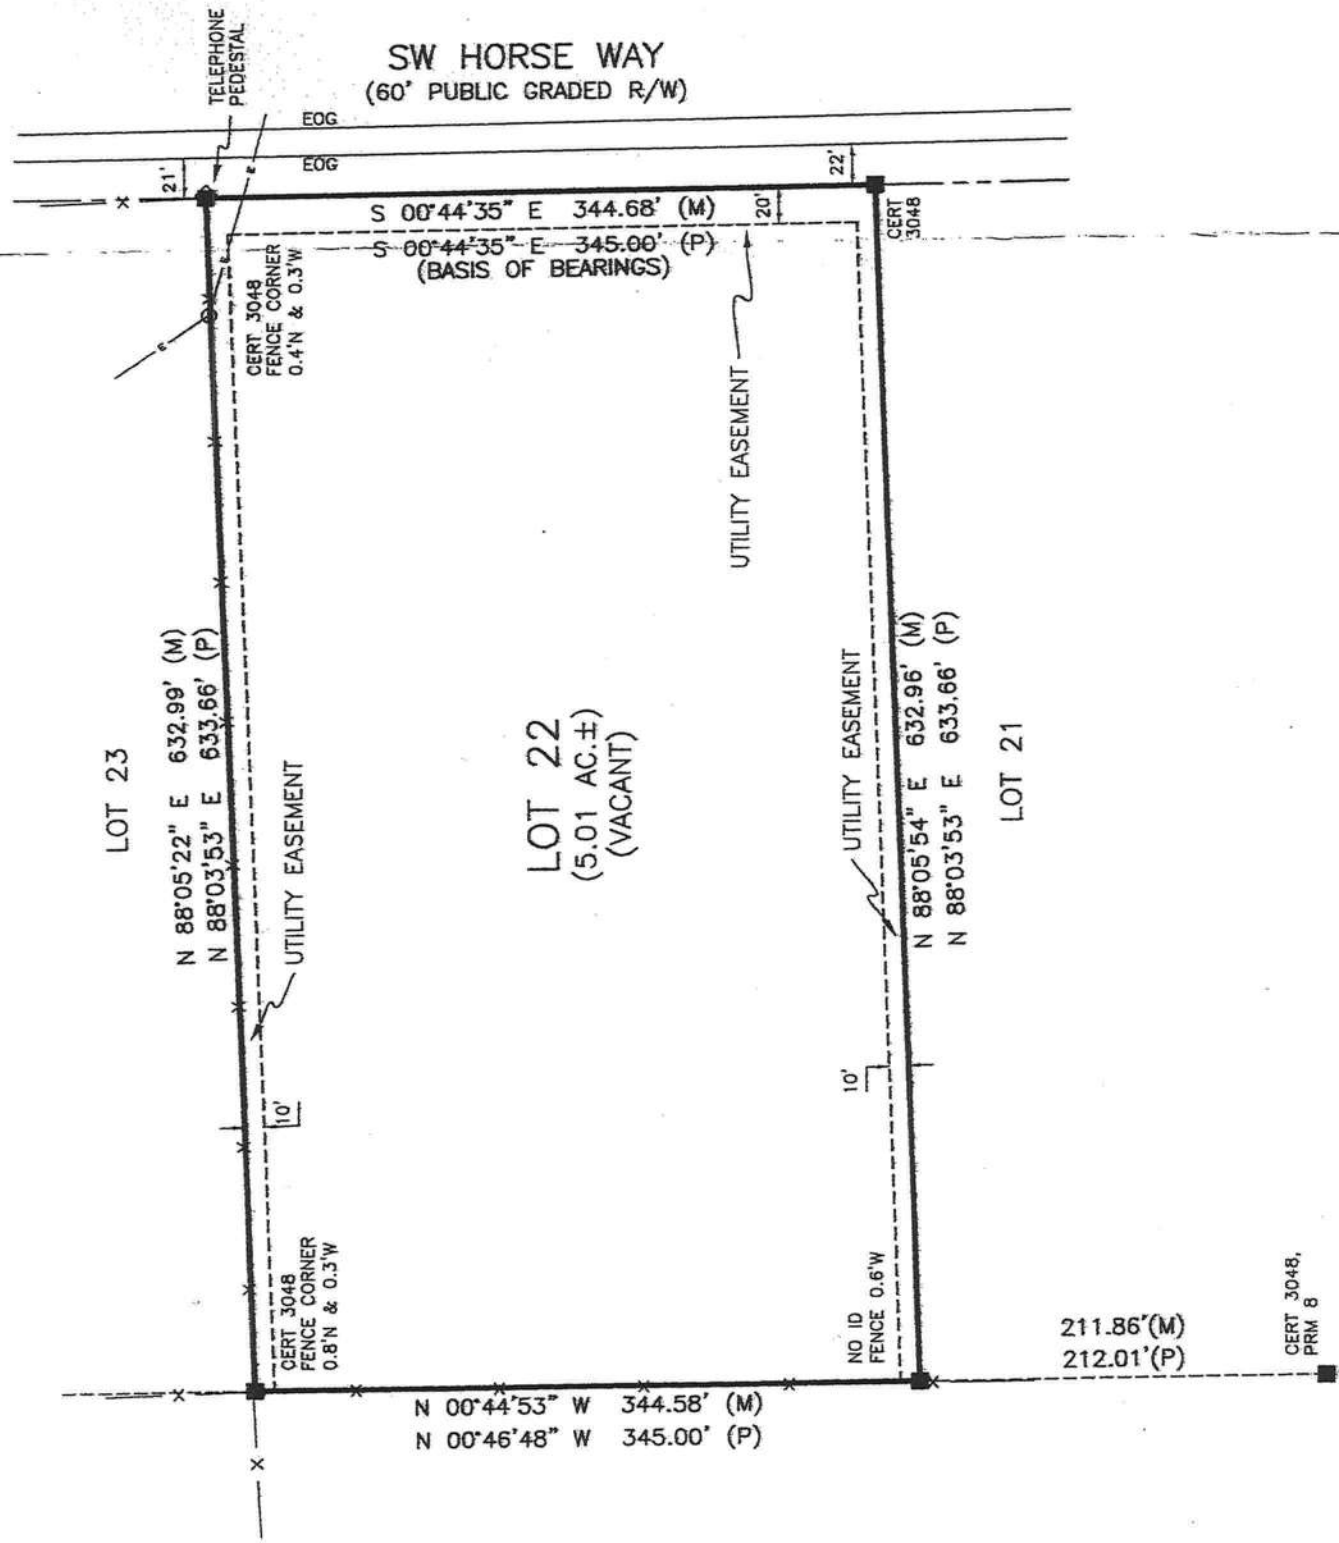

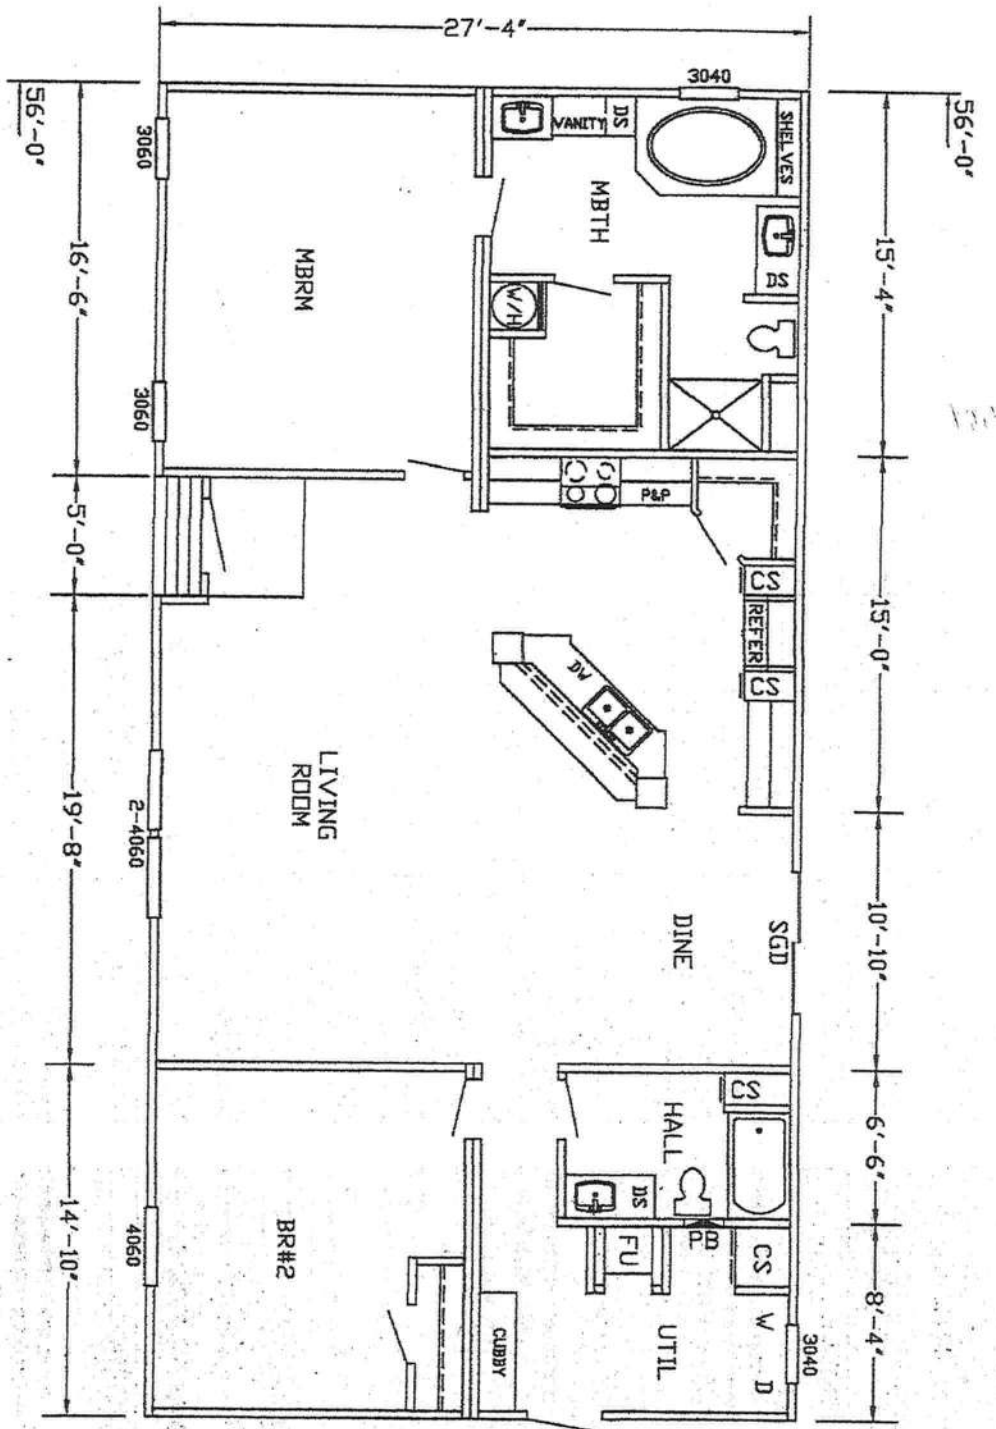



STATE OF FLORIDA
DEPARTMENT OF HEALTH
APPLICATION FOR ONSITE SEWAGE DISPOSAL SYSTEM CONSTRUCTION PERMIT

Permit Application Number _____

ASZKIEWICZ

PART II - SITEPLAN

Scale: 1 inch = 50 feet.

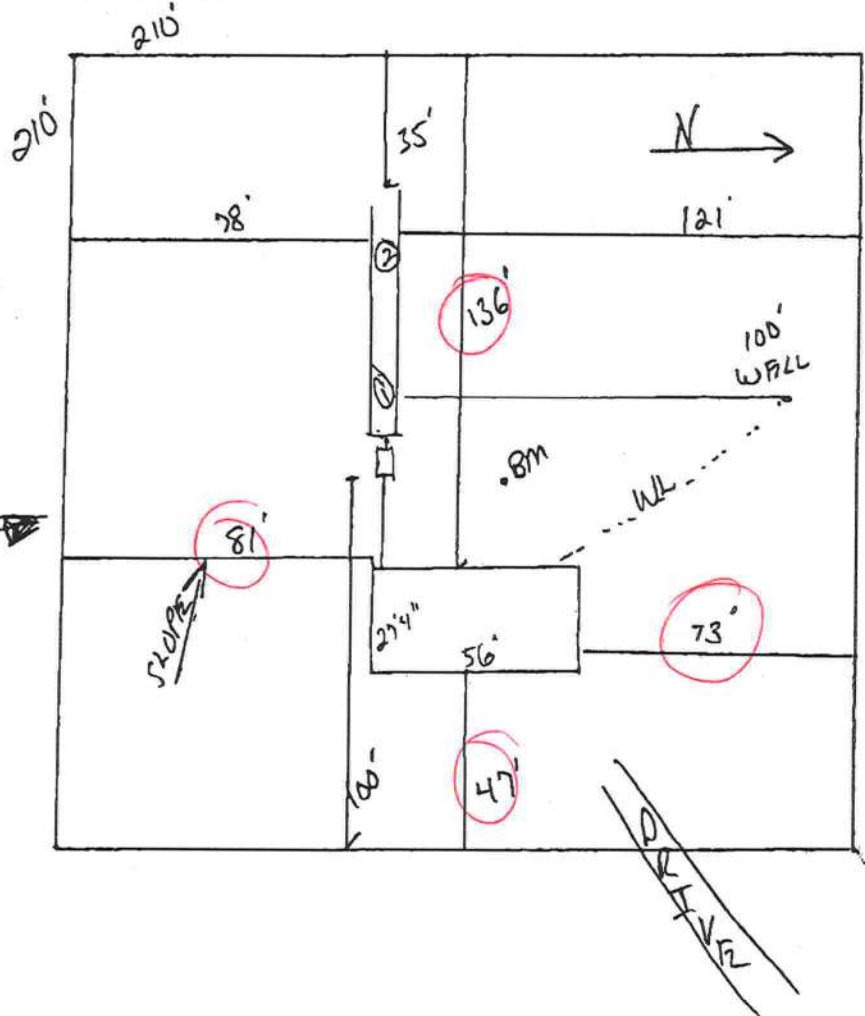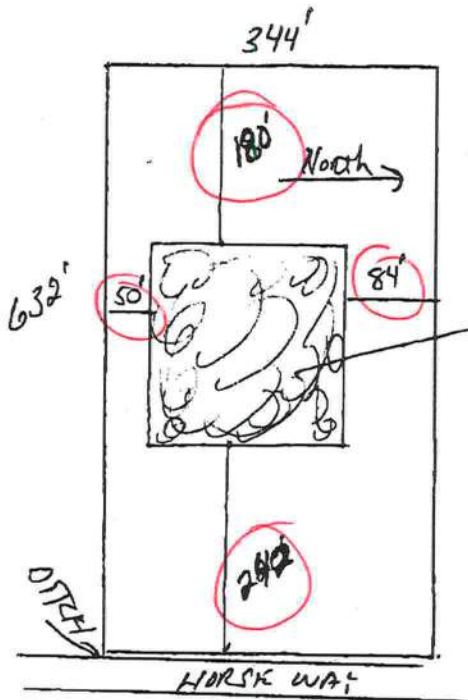

Notes: 1 of 5.01 Acres

Site Plan submitted by: Rock D F

MASTER CONTRACTOR

Plan Approved _____ Not Approved _____

Date _____

By _____ County Health Department

ALL CHANGES MUST BE APPROVED BY THE COUNTY HEALTH DEPARTMENT

Prepared by & Return to:
Matthew D. Rocco
Sierra Title, LLC
619 SW Baya Drive, Suite 102
Lake City, Florida 32025

File Number: 09-0226

Inst: 200912004250 Date: 3/16/2009 Time: 4:16 PM
Doc Stamp-Deed: 304.50
DC, P. DeWitt Cason, Columbia County Page 1 of 1 B.1159 P.744

General Warranty Deed

Made this March 7, 2009 A.D. By David M. Myers and Jo Ann B. Myers, husband and wife whose post office address is: 5006 County Route 24, Canton, NY 13617, hereinafter called the grantor, to Thomas Paszkiewicz and his wife, Rebecca Paszkiewicz, whose post office address is: 1501 NW 114 Avenue, Pembroke Pines, FL 33026, hereinafter called the grantee:

(Whenever used herein the term "grantor" and "grantee" include all the parties to this instrument and the heirs, legal representatives and assigns of individuals, and the successors and assigns of corporations)

Witnesseth, that the grantor, for and in consideration of the sum of Ten Dollars, (\$10.00) and other valuable considerations, receipt whereof is hereby acknowledged, hereby grants, bargains, sells, aliens, remises, releases, conveys and confirms unto the grantee, all that certain land situate in Columbia County, Florida, viz:

Lot 22, Cypress Lake Hills, according to the plat thereof, as recorded in Plat Book 5, Page 82, of the Public Records of Columbia County, Florida.

Parcel ID Number: R00407-122

Together with all the tenements, hereditaments and appurtenances thereto belonging or in anywise appertaining.

To Have and to Hold, the same in fee simple forever.

And the grantor hereby covenants with said grantee that the grantor is lawfully seized of said land in fee simple; that the grantor has good right and lawful authority to sell and convey said land; that the grantor hereby fully warrants the title to said land and will defend the same against the lawful claims of all persons whomsoever; and that said land is free of all encumbrances except taxes accruing subsequent to December 31, 2008.

In Witness Whereof, the said grantor has signed and sealed these presents the day and year first above written.

Signed, sealed and delivered in our presence:

Arian M. Maury
Witness Printed Name: Arian M. Maury

Nicole Hitt
Witness Printed Name: Nicole Hitt

State of New York
County of St. Lawrence

David M. Myers (Seal)
David M. Myers
Address: 5006 County Route 24, Canton, NY 13617

Jo Ann B. Myers (Seal)
Jo Ann B. Myers
Address:

The foregoing instrument was acknowledged before me this 7th day of March, 2009, by David M. Myers and his wife, Jo Ann B. Myers, who is/are personally known to me or who has produced NYSOL as identification.

Shaun H. Kimball
Notary Public
Print Name: Shaun H. Kimball
My Commission Expires: 9/25/10

\$39,800 1000 DP

H



Columbia County Property Appraiser
J. Doyle Crews, CFA - Lake City, Florida - 386-758-1083

0 0.06 0.12 0.18 mi

PARCEL: 35-4S-15-00407-122 - VACANT (000000)

Name: MYERS DAVID M & JO ANN B	LandVal	\$50,100.00
Site: CYPRESS LAKE HILLS	BldgVal	\$0.00
Mail: 5006 CR 24	ApprVal	\$50,100.00
CANTON, NY 13617	JustVal	\$50,100.00
	Assd	\$50,100.00
	Exmpt	\$0.00
	Taxable	\$50,100.00
9/1/1986 \$142,130.00 / V		
Sales U		
Info V		
1/1/1987 \$10,500.00 / Q		



This information, GIS Map Updated: 4/15/2008, was derived from data which was compiled by the Columbia County Property Appraiser Office solely for the governmental purpose of property assessment. This information should not be relied upon by anyone as a determination of the ownership of property or market value. No warranties, expressed or implied, are provided for the accuracy of the data herein, it's use, or it's interpretation. Although it is

A & B Well Drilling, Inc.
5673 NW Lake Jeffery Road
Lake City, FL, 32055
(O) 386-758-3409
(F) 386-758-3410
(C) 386-623-3151

12/31/2009

To: Columbia County Building Department

Description of well to be installed for Customer: PASEKIEWICZ
Located at Address: HORSE WAY

1 hp 15 GPM Submersible Pump, 1 1/4" drop pipe, 86 gallon captive tank and back flow prevention, With SRWMD permit.

Bruce Park
Sincerely
Bruce Park
President

COLUMBIA COUNTY 9-1-1 ADDRESSING

P. O. Box 1787, Lake City, FL 32056-1787

PHONE: (386) 758-1125 * FAX: (386) 758-1365 * Email: ron_croft@columbiacountyfla.com

Addressing Maintenance

To maintain the Countywide Addressing Policy you must make application for a 9-1-1 Address at the time you apply for a building permit. The established standards for assigning and posting numbers to all principal buildings, dwellings, businesses and industries are contained in Columbia County Ordinance 2001-9. The addressing system is to enable Emergency Service Agencies to locate you in an emergency, and to assist the United States Postal Service and the public in the timely and efficient provision of services to residents and businesses of Columbia County.

DATE REQUESTED: 1/4/2010 DATE ISSUED: 1/5/2010

ENHANCED 9-1-1 ADDRESS:

310 SW HORSE WAY

LAKE CITY FL 32024

PROPERTY APPRAISER PARCEL NUMBER:

35-4S-15-00407-122

Remarks:

LOT 22 CYPRESS LAKE HILLS S/D

Address Issued By: 

Columbia County 9-1-1 Addressing / GIS Department

NOTICE: THIS ADDRESS WAS ISSUED BASED ON LOCATION INFORMATION RECEIVED FROM THE REQUESTER. SHOULD, AT A LATER DATE, THE LOCATION INFORMATION BE FOUND TO BE IN ERROR, THIS ADDRESS IS SUBJECT TO CHANGE.

Handwritten: JHN: WEEGIE

Columbia County Building Department Culvert Waiver

Handwritten: "RUSH"

Culvert Waiver No. 000001790

DATE: 01/28/2010

BUILDING PERMIT NO. 28337

APPLICANT BO ROYALS

PHONE 386.754.6737

ADDRESS 4068 US 90-W

LAKE CITY

FL 3055

OWNER THOMAS & REBECCA PASCZKIEWICZ

PHONE 954.649.0145

ADDRESS 310 SW HORSE WAY

LAKE CITY

FL 32024

CONTRACTOR WENDELL CREWS

PHONE 352.351.6100

LOCATION OF PROPERTY 90-W TO SR.247-S, TL TO CYPRESS LAKE ROAD, TR TO HORSE WAY, TL AND IT'S
THE 2ND PROPERTY ON R AFTER CURVE.

SUBDIVISION/LOT/BLOCK/PHASE/UNIT CYPRESS LAKE HILLS

22

PARCEL ID # 35-4S-15-00407-122

I HEREBY CERTIFY THAT I UNDERSTAND AND WILL FULLY COMPLY WITH THE DECISION OF THE COLUMBIA
COUNTY PUBLIC WORKS DEPARTMENT IN CONNECTION WITH THE HEREIN PROPOSED APPLICATION.

SIGNATURE: *[Signature]*

A SEPARATE CHECK IS REQUIRED
MAKE CHECKS PAYABLE TO BCC

Amount Paid 50.00

PUBLIC WORKS DEPARTMENT USE ONLY

I HEREBY CERTIFY THAT I HAVE EXAMINED THIS APPLICATION AND DETERMINED THAT THE
CULVERT WAIVER IS:

APPROVED

NOT APPROVED - NEEDS A CULVERT PERMIT

COMMENTS: _____

SIGNED: *James Thomas*

DATE: 1-29-10

ANY QUESTIONS PLEASE CONTACT THE PUBLIC WORKS DEPARTMENT AT 386-752-5955.

135 NE Hernando Ave., Suite B-21
Lake City, FL 32055
Phone: 386-758-1008 Fax: 386-758-2160



COLUMBIA COUNTY
ON
CALVINY

M/H OCCUPANCY

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 35-4S-15-00407-122


Building permit No. 000028337

Permit Holder WENDELL CREWS

Owner of Building THOMAS & REBECCA PASZKIEWICZ

Location: 310 SW HORSE WAY

Date: 01/28/2010



Building Inspector



POST IN A CONSPICUOUS PLACE
(Business Places Only)
