


Installer RODNEY FEAGLES License # TH1025288
 Manufacturer TOWNHOME Length x Width 28 x 76
 Name of Owner of this Mobile Home BRENTON KOONTZ
 Phone 318-0879
 Address 184. RT. WHITE, FL.

NOTE: If home is a single wide fill out one half of the blocking plan
 If home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials RF

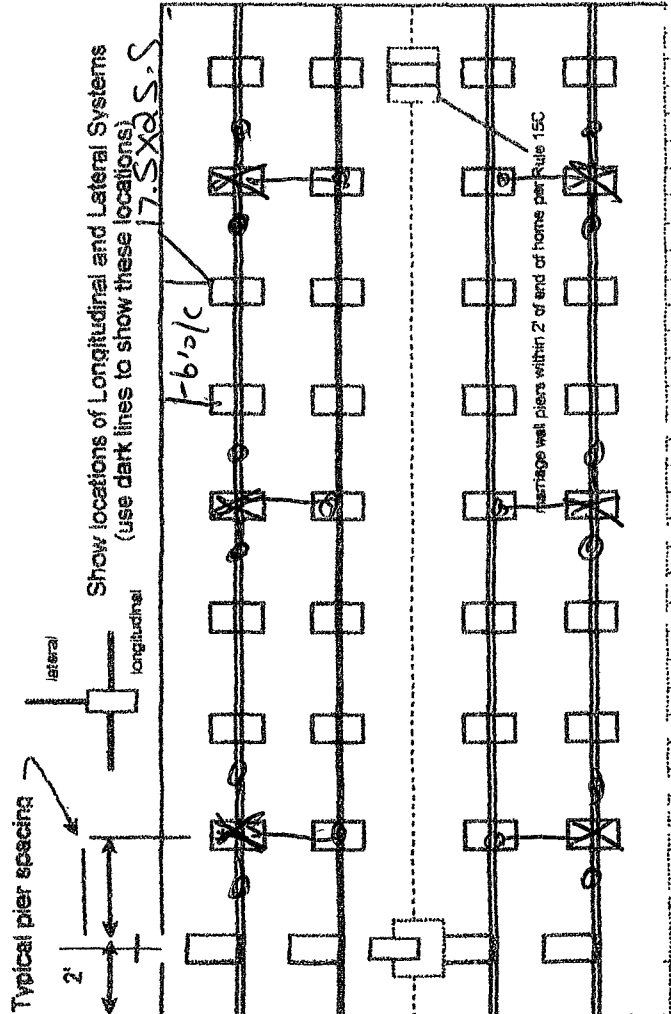

New Home ☒ Used Home ☐ Year 2014
 Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C ☐
 Single wide ☐ Wind Zone II ☒ Wind Zone III ☐
 Double wide ☒ Installation Decal # 20428
 Triple/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)"	24" x 24" (576)"	26" x 26" (676)
1000 dsf	3'	3'	4'	5'	6'	7'	8'
1500 dsf	4'	4'	5'	6'	7'	8'	8'
2000 dsf	6'	6'	8'	8'	8'	8'	8'
2500 dsf	7'	7'	8'	8'	8'	8'	8'
3000 dsf	8'	8'	8'	8'	8'	8'	8'
3500 dsf	8'	8'	8'	8'	8'	8'	8'

* interpolated from Rule 15C-1 pier spacing table

PIER PAD SIZES

I-beam pier pad size 17.5 x 25.5
 Perimeter pier pad size 16 x 16
 Other pier pad sizes (required by the mfg) 16 x 16

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening Pier pad size

SEE DIAGRAM

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer Oliver Tech.

OTHER TIES

Number _____
 Sidewall _____
 Longitudinal _____
 Marriage wall _____
 Shearwall _____

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

ANCHORS

4 ft 5 ft

POPULAR PAD SIZES

Pad Size	Sq in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	445
24 x 24	576
25 x 26	676

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb soil without testing.

x 1500 x 1500 x 1500

POCKET PENETROMETER TESTING METHOD

- 1 Test the penmeter of the home at 6 locations
- 2 Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment

x 1500 x 1500 x 1500

TORQUE PROBE TEST

The results of the torque probe test is 285 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity

RF Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source This includes the bonding wire between multi-wide units Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg

Connect all potable water supply piping to an existing water meter, water tap, or other

Site Preparation

Debris and organic material removed ☒ Swale ☐ Pad ☒ Other ☐

Fastening multi wide units

Floor: Type Fastener 3/8" Length 6" Spacing 18"
Walls: Type Fastener 3/8" Length 6" Spacing 24"
Roof: Type Fastener 3/8" Length 6" Spacing 24"
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled manmade walls are a result of a poorly installed or no gasket being installed I understand a strip of tape will not serve as a gasket.

Installer's initials RF

Type gasket FOAM Pg. 16

Installed: Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. 10
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Skirting to be installed Yes ☒ No ☐
Dryer vent installed outside of skirting. Yes ☒ N/A ☐
Range downflow vent installed outside of skirting. Yes ☒ N/A ☐
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒
Other


Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature

Date

2-28-14

INSTALL A PERIMETER BLOCK PIER BELOW THE EDGE JOIST AT SHEAR WALLS WHEN THE SHEAR WALL EXTENDS OVER THE FLOOR CANTILEVER OR ADD A PIER BELOW THE EDGE JOIST WHEN THE SHEAR WALL EXTENDS OVER THE FLOOR CANTILEVER - TYP BELOW THE SIDEWALLS AND MAR. WALLS (THE PIER MAY BE MOVED ALONG THE EDGE JOIST UP TO 6" FROM THE SHEAR WALL TO PERMIT THE INSTALLATION OF REQUIRED SHEAR WALL ANCHORS)

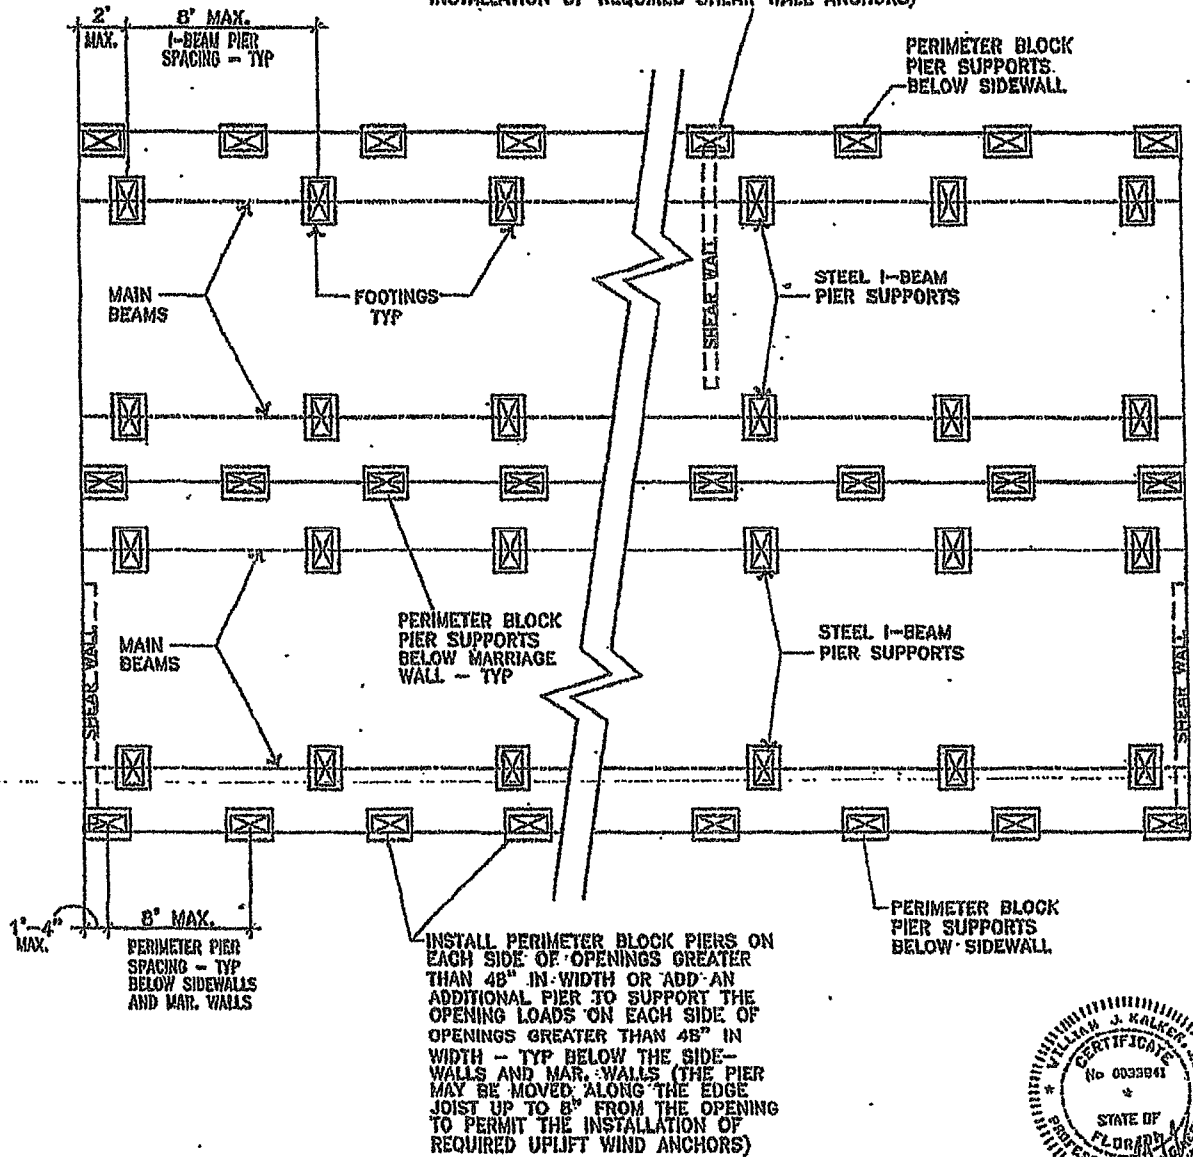

TYPICAL DOUBLE WIDE PERIMETER BLOCKING LAYOUT

NOTES:

- PIERS SHALL BE LOCATED AT EACH SIDE OF ALL SIDEWALL AND MARRIAGE WALL OPENINGS GREATER THAN 4'-0" IN WIDTH (BAY WINDOWS, PORCHES, RECESSED ENTRIES, ETC.). DOORS AND OPENINGS ON ENDWALLS DO NOT REQUIRE PIERS.

REFER TO OTHER MANUAL PAGES FOR FOOTING TABLES AND PIER CONSTRUCTION DETAILS

APPROVED

JAN 10 2005

Federal Manufactured

APPROVED

SU-17

TOWN HOMES

DATE: 1/8/05	REVISIONS:
CODES: AHCSS	
LABELS: HUD	
SCALE: NTS	

PERIMETER PIER LAYOUT
DOUBLE WIDE HOMES
