


28'-0 X 56'-0 ~ 1493 SQ. FT.

Jazz backup



NOTE: SEE I-3.2
INSTALLATION MANUAL

4. ARE PANS MAY BE COMBINED TO COVER A LARGER AREA, IN THIS CASE THE MAX. ALLOWABLE LOADS MAYBE COMBINED AS WELL.

5. IF THE REQUIREMENTS OF DESIGN NO. INSTALLATION MANUAL, CONFLICT WITH THE REQUIREMENTS OF THE OLIVER TECHNOLOGIES INSTALLATIONS THE MORE STRINGENT REG. SHALL BE USED.

Destiny
Industries, LLC

REVISU
—1000 LBS ABSPAD FOUNDATION PLAN^{mtf}

Sheet

PERMIT NUMBER

Installer

Stephan Weeks License # 141025306

Owner Name & Address of home being installed

5014 SW Ickestuck Ave
Ft White, TX 72038

Manufacturer

Clayton

Length x width

28x48

NOTE:

If home is a single wide fill out one half of the blocking plan
If home is a triple or quad sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials

[Signature]

PERMIT WORKSHEET

New Home

☒ Used Home

☐ Year Model

Home installed to the Manufacturer's Installation Manual

Home is installed in accordance with Rule 15-C

Single wide

☐ Wind Zone II

☒ Wind Zone III

Double wide

☒ Installation Detail #

Triple/Quad

Serial #

1052909a23-131066

page 1 of 2

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq ft)	14' x 16' (224)	16' x 16' (256)	18' x 16' (288)	20' x 16' (320)	22' x 16' (352)	24' x 16' (384)	26' x 16' (416)
1000 psf	3'	4'	4'	5'	5'	6'	6'
1500 psf	4'	5'	5'	6'	6'	7'	7'
2000 psf	5'	6'	6'	7'	7'	8'	8'
2500 psf	6'	7'	7'	8'	8'	9'	9'
3000 psf	7'	8'	8'	9'	9'	10'	10'
3500 psf	8'	9'	9'	10'	10'	11'	11'

Interpolated from Rule 16C-1 pier spacing table

PIER PAD SIZES

14' x 16' pad size 23x31
16' x 16' pad size 23x31 or 17.5x25.5

Other pier pad sizes (required by the mfg.)

Draw the approximate locations of openings, wall openings 4 foot or greater. Use this symbol to show the piers.

List all marlage wall openings greater than 4 foot and their pier pad sizes below.

Opening

Pier pad size

See

Back of

Blocking Plan

TRIPOD COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer Stabilizing Device w/ Lateral Arms
Manufacturer

OLIVER INDIV

Pad Size	Sq. ft.
14' x 16'	224
16' x 16'	256
18' x 16'	288
20' x 16'	320
22' x 16'	352
24' x 16'	384
26' x 16'	416
28' x 16'	448
30' x 16'	480
32' x 16'	512
34' x 16'	544
36' x 16'	576
38' x 16'	608
40' x 16'	640

ANCHORS

FRAME TIES

within 2' of end of home spaced at 5' 4" oc


OTHER TIES

Number

Sidewall
Longitudinal
Marlage wall
Shearwall

PERMIT WORKSHEET

page 2 of 2

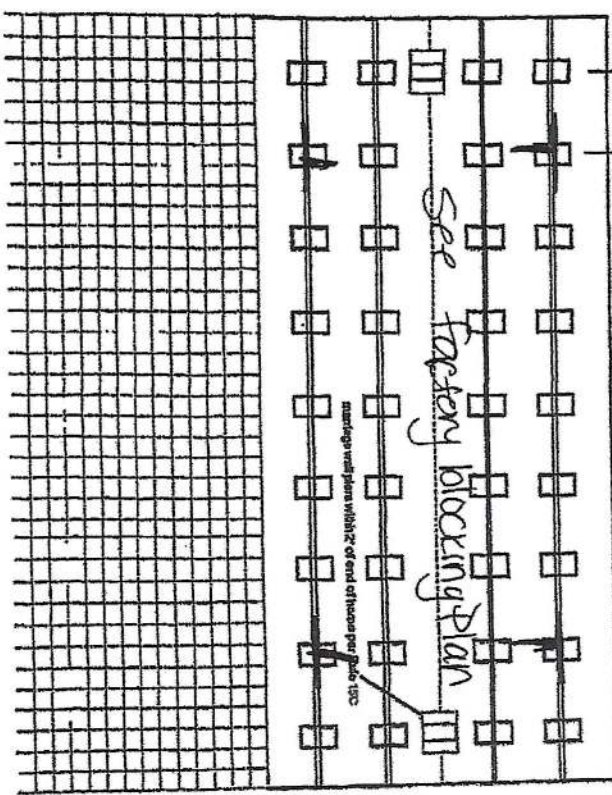

PERMIT NUMBER _____

Page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ without testing. _____

x100

x100

x100

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 5 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x100

x100

x100

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. Understand 5 ft. anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 _____

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name _____

Date Tested _____

Stephen Weeks
Assigned diver 1101V
USGS 4's 1 Anchors

Electrical

Connect electrical conductors between multi-wide units, buried to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed _____ Swale _____

Fastening multi wide units

Other

Floor: _____

Walls: _____

Roof: _____

Type Fastener: 1445 Length: 3 Spacing: 20
Type Fastener: 1445 Length: 6 Spacing: 20
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galy. roofing nails at 2' on center on both sides of the centerline.

Garage (smaller than required)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly fastened or no gasketing installed. I understand a strip of tape will not serve as a gasket.

Installer's initials

SW

Type gasket

Pg. P11

Installed: Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or replaced. Yes ☒ Pg. _____
Sliding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Miscellaneous

Shading to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes ☒ N/A
Range downflow vent installed outside of skirting. Yes ☒ N/A
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossover protected. Yes ☒
Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the _____

Installer Signature: *Stephen Weeks* Date: *5/4/2003*
All information on this worksheet must be filled out completely to be accepted.
