

438.53 Called by Message
PERMIT APPLICATION / MANUFACTURED HOME INSTALLATION APPLICATION

For Office Use Only

Zoning Official BLK 30.12.05

Building Official DK JH 12-29-05

AP# 051265

Date Received 12-28-05

By GT

Permit # 24037

Flood Zone X

Development Permit MA

Zoning A-3

Land Use Plan Map Category A-3

Comments _____

FEMA Map # _____ Elevation _____ Finished Floor _____ River _____ In Floodway _____

☒ Site Plan with Setbacks shown ☒ Environmental Health Signed Site Plan ☐ Env. Health Release

☐ Well letter provided ☒ Existing Well

Revised 9-23-04

Property ID 04-78-17-09891-0045 Must have a copy of the property deed

New Mobile Home ☒ Used Mobile Home _____ Year 2006

Subdivision Information _____

Applicant Mary Ann Hamilton Phone # (386) 758-6755

Address 513 SW Deputy J. Davis Lane Lake City, FL 32024

Name of Property Owner Tammy R. Sealey Phone # (352) 281-7678

911 Address 2231 SW Old L.C. Terr. High Spring 32643

Circle the correct power company - FL Power & Light - Clay Electric
 (Circle One) - Suwannee Valley Electric - Progressive Energy

Name of Owner of Mobile Home Tammy R. Sealey Phone # (352) 281-7678

Address 23464 3rd NW Newberry, FL 32669

Relationship to Property Owner AGENT

Current Number of Dwellings on Property 0

Lot Size _____ Total Acreage 5. acres (owe)

Do you : Have an Existing Drive or need a Culvert Permit or a Culvert Waiver Permit

Driving Directions 41 South 1 mile past Olena State Park. Turn R on Barney. Turn Right on Old Lake City. 2nd driveway on Right.

Is this Mobile Home Replacing an Existing Mobile Home No

Name of Licensed Dealer/Installer Bruce L. Goodson Phone # 755-1783

Installers Address 1505 SW CR252B Lake City, FL 32024

License Number JH0000702 Installation Decal # 254158

Prepared by
Deborah Bissell, an employee of
First American Title Insurance Company
23335 NW County Road 236, Suite 10
High Springs, Florida 32643
(386)454-2727

Return to: Grantee

File No.: 1095-1040060

Inst:2005031256 Date:12/19/2005 Time:11:33
Doc Stamp-Deed : 385.00
DC, P. DeWitt Cason, Columbia County B:1068 P:1438

WARRANTY DEED

This indenture made on **December 15, 2005 A.D.**, by

Tony L. Parrish and Linda L. Parrish, husband and wife

whose address is: **2139 SW Old Lake City Terrace, High Springs, FL 32643**
hereinafter called the "grantor", to

Tammy R. Sealey

whose address is: **P.O. Box 2414, High Springs, FL 32655**
hereinafter called the "grantee":

(Which terms "Grantor" and "Grantee" shall include singular or plural, corporation or individual, and either sex, and shall include heirs, legal representatives, successors and assigns of the same)

Witnesseth, that the grantor, for and in consideration of the sum of Ten Dollars, (\$10.00) and other valuable considerations, receipt whereof is hereby acknowledged, hereby grants, bargains, sells, allens, remises, releases, conveys and confirms unto the grantee, all that certain land situate in **Columbia County, Florida**, to-wit:

See Exhibit "A" attached hereto

Parcel Identification Number: **R09891-004 (part of)**

Subject to all reservations, covenants, conditions, restrictions and easements of record and to all applicable zoning ordinances and/or restrictions imposed by governmental authorities, if any.

Together with all the tenements, hereditaments and appurtenances thereto belonging or in any way appertaining.

To Have and to Hold, the same in fee simple forever.

1095 - 1040060

And the grantor hereby covenants with said grantee that the grantor is lawfully seized of said land in fee simple; that the grantor has good right and lawful authority to sell and convey said land; that the grantor hereby fully warrants the title to said land and will defend the same against the lawful claims of all persons whomsoever; and that said land is free of all encumbrances except taxes accruing subsequent to December 31st of 2004.

In Witness Whereof, the grantor has hereunto set their hand(s) and seal(s) the day and year first above written.

✓ Tony L. Parrish
Tony L. Parrish

✓ Linda L. Parrish
Linda L. Parrish

Signed, sealed and delivered in our presence:

Deborah L. Bissell
Witness Signature

Print Name: DEBORAH BISSELL

Beverly H. Magee
Witness Signature

Print Name: _____

State of FL


County of Alachua

The Foregoing Instrument Was Acknowledged before me on **December 15, 2005**, by **Tony L. Parrish and Linda L. Parrish, husband and wife** who is/are personally known to me or who has/have produced a valid driver's license as identification.

NOTARY PUBLIC

Deborah L. Bissell
Notary Print Name

My Commission Expires: _____



Inst: 2005031256 Date: 12/19/2005 Time: 11:33

Doc Stamp-Deed : 385.00

DC, P. DeWitt Cason, Columbia County B: 1068 P: 1439

Exhibit "A"

COMMENCE AT THE SOUTHWEST CORNER OF THE SOUTHEAST 1/4 OF SECTION 4, TOWNSHIP 7 SOUTH, RANGE 17 EAST, COLUMBIA COUNTY, FLORIDA, AND RUN THENCE NORTH 00 DEG. 40 MIN. 00 SEC. WEST, 715.08 FEET TO THE POINT OF BEGINNING; THENCE CONTINUE NORTH 00 DEG. 40 MIN. 00 SEC. WEST, 253.75 FEET; THENCE NORTH 89 DEG. 30 MIN. 00 SEC. EAST, 700.00 FEET; THENCE SOUTH 00 DEG. 40 MIN. 00 SEC. EAST, 368.29 FEET; THENCE NORTH 81 DEG. 12 MIN. 41 SEC. WEST, 709.64 FEET TO THE POINT OF BEGINNING.


Inst:2005031256 Date:12/19/2005 Time:11:33

Doc Stamp-Deed : 385.00

_____, P. DeWitt Cason, Columbia County B:1068 P:1440

72P
LHP

1095 - 1040060

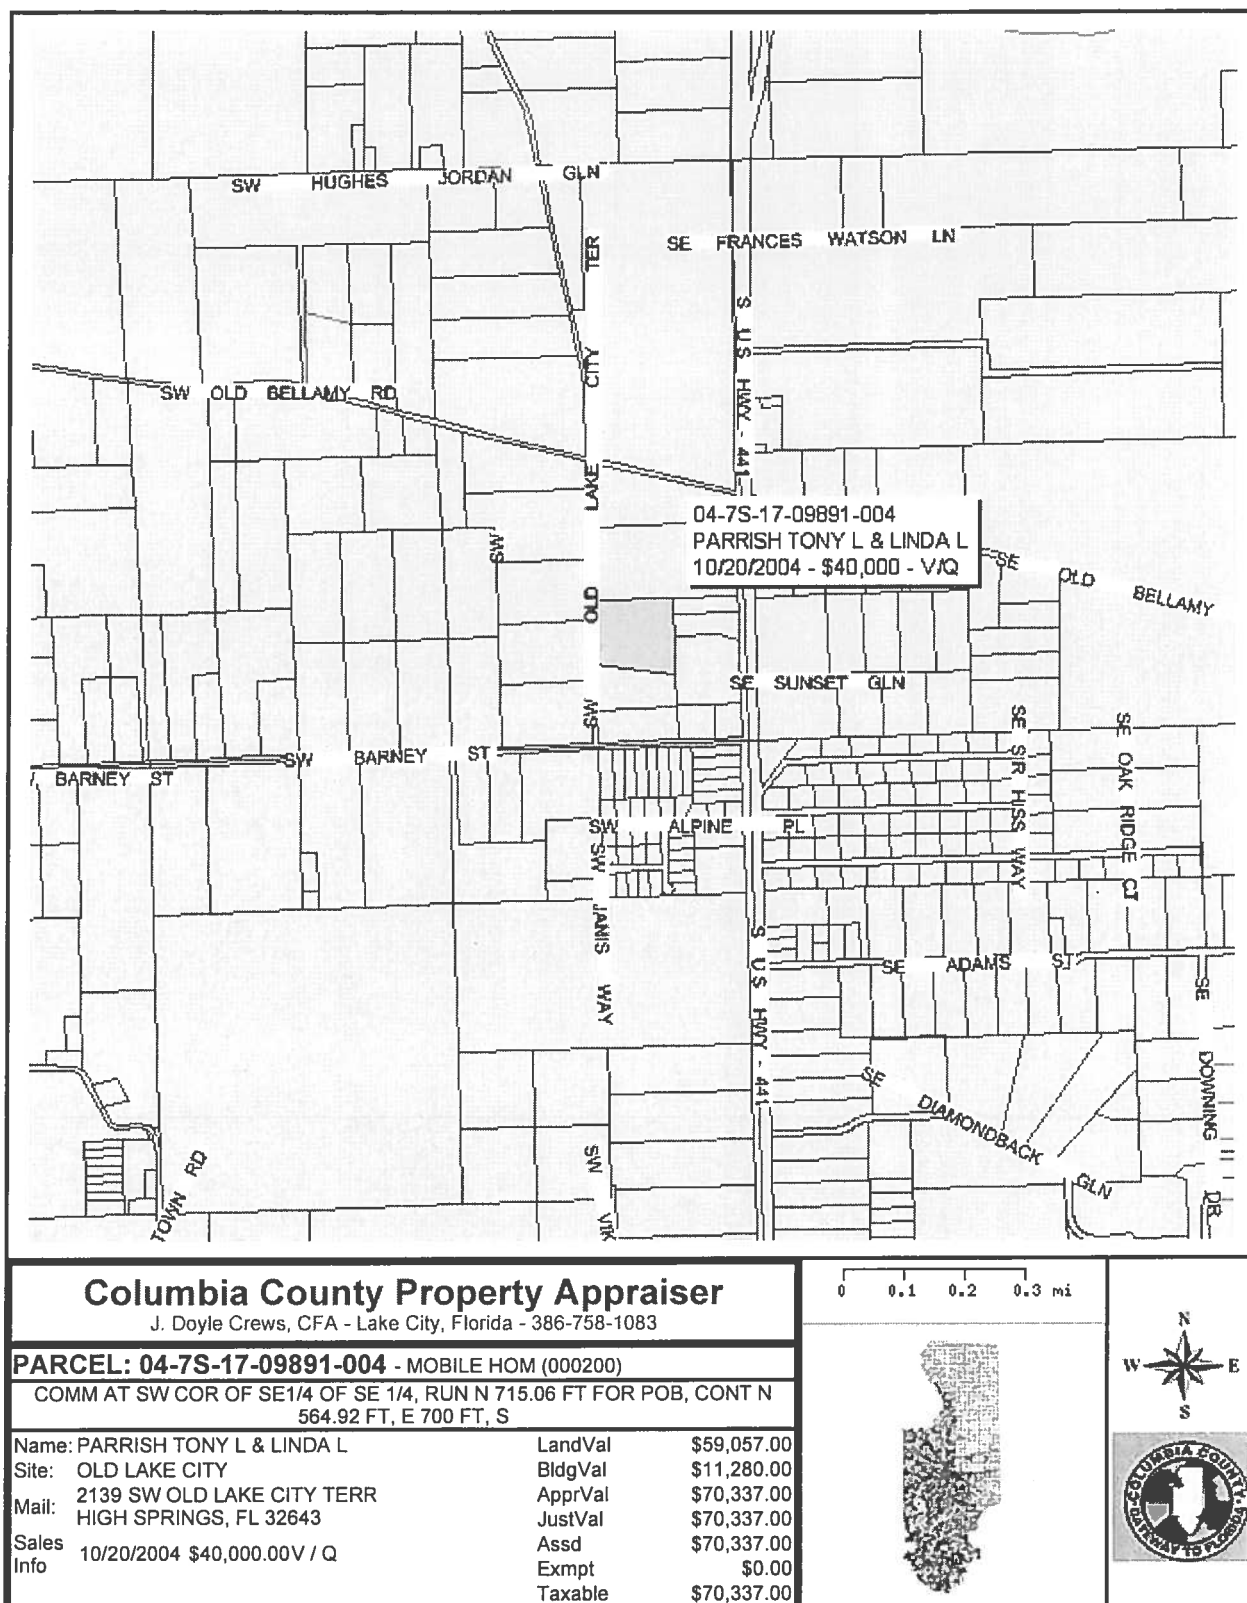

This information, GIS Map Updated: 8/3/2005, was derived from data which was compiled by the Columbia County Property Appraiser Office solely for the governmental purpose of property assessment. This information should not be relied upon by anyone as a determination of the ownership of property or market value. No warranties, expressed or implied, are provided for the accuracy of the data herein, it's use, or it's interpretation. Although it is periodically updated, this information may not reflect the data currently on file in the Property Appraiser's office. The assessed values are NOT certified values and therefore are subject to change before being finalized for ad valorem assessment purposes.

@ CAM112M01	CamaUSA Appraisal System		Columbia County
12/29/2005 9:44	Legal Description Maintenance	37500	Land 001
Year T Property	Sel		AG 000
2006 R 04-7S-17-09891-005	...		Bldg 000
			Xfea 000
SEALEY TAMMY R		37500	TOTAL B

1	COMM AT SW COR OF SE1/4, RUN N	715.08 FT FOR POB, CONT N	2
3	253.75 FT, E 700 FT, S 368.29	FT, N 81 DG W 709.64 FT TO POB	4
5	ORB 1068-1438		6
7			8
9			10
11			12
13			14
15			16
17			18
19			20
21			22
23			24
25			26
27			28

Mnt 12/28/2005 WANDA

F1=Task F3=Exit F4=Prompt F10=GoTo PgUp/PgDn F24=More


@ CAM110M01 S CamasUSA Appraisal System Columbia County
 12/28/2005 16:32 **Property Maintenance** 59057 Land 002
 Year T Property Sel AG 000
 2006 R 04-7S-17-09891-004 * 10474 Bldg 001
 Owner PARRISH TONY L & LINDA L Conf Xfea 000
 Addr 2139 SW OLD LAKE CITY TERR 69531 TOTAL B*
 10.010 Total Acres
 Retain Cap? Renewal Notice
 City, St HIGH SPRINGS FL Zip 32643 N
 Country (PUD1) (PUD2) (PUD3) MKTA02
 Appr By JS Date 9/29/2005 AppCode UseCd 000200 MOBILE HOME
 TxDist Nbhd MktA ExCode Exemption/% TxCode Units Tp
 003 4717.00 02
DIST 3
 House# 2139 Street OLD LAKE CITY MD TERR Dir SW #
 - City HIGH SPRINGS
 Subd N/A Condo .00 N/A
 Sect 4 Twn 7S Rnge 17E Subd Blk Lot
 Legals COMM AT SW COR OF SE1/4 OF SE 1/4, RUN N 715.06 FT FOR POB,
 CONT N 564.92 FT, E 700 FT, S 679.46 FT, W 709.64 FT TO POB, +
 Map# Mnt 10/18/2005 PINKY
F1=Task F2=ExTx F3=Exit F4=Prompt F11=Docs F10=GoTo PgUp/PgDn F24=More

Split # 09891-005


Sealey, Tammy R.

[illegible]

SITE PLAN EXAMPLE / WORKSHEET

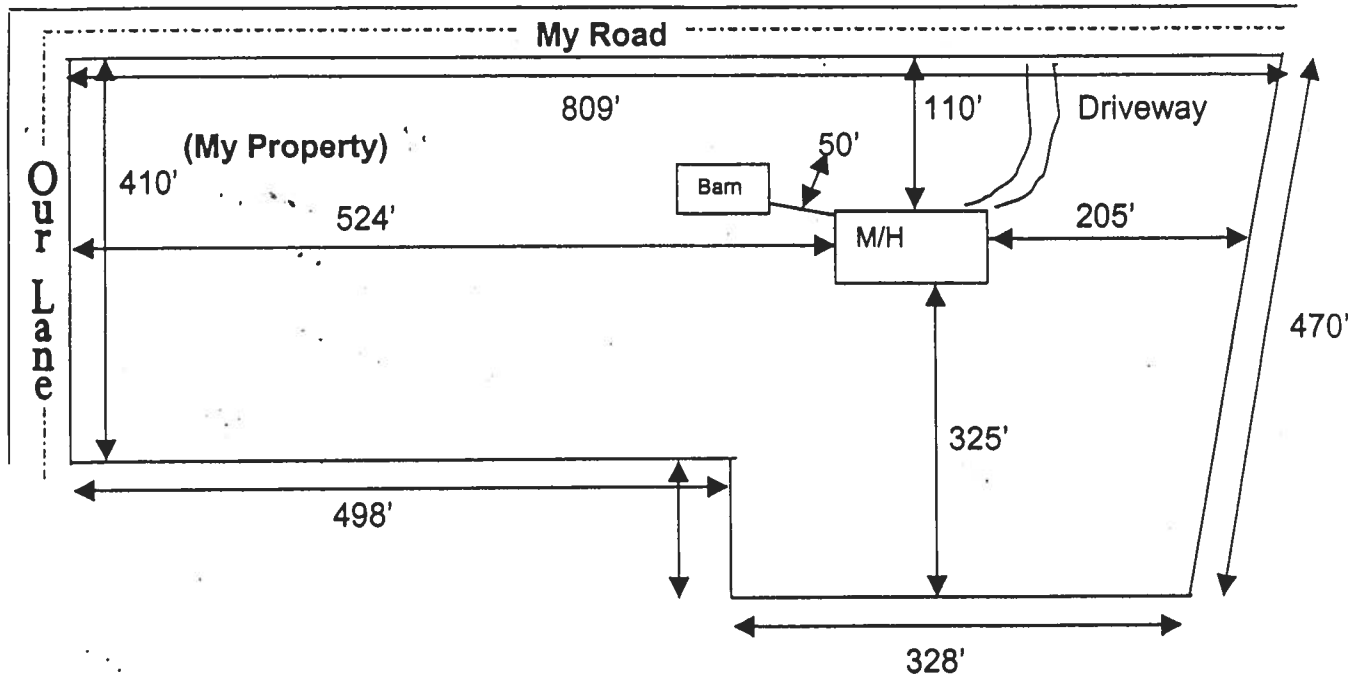

Use this example to draw your own site plan. Show all existing buildings and any other homes on this property and show the distances between them. Also show where the road or roads are around your property.

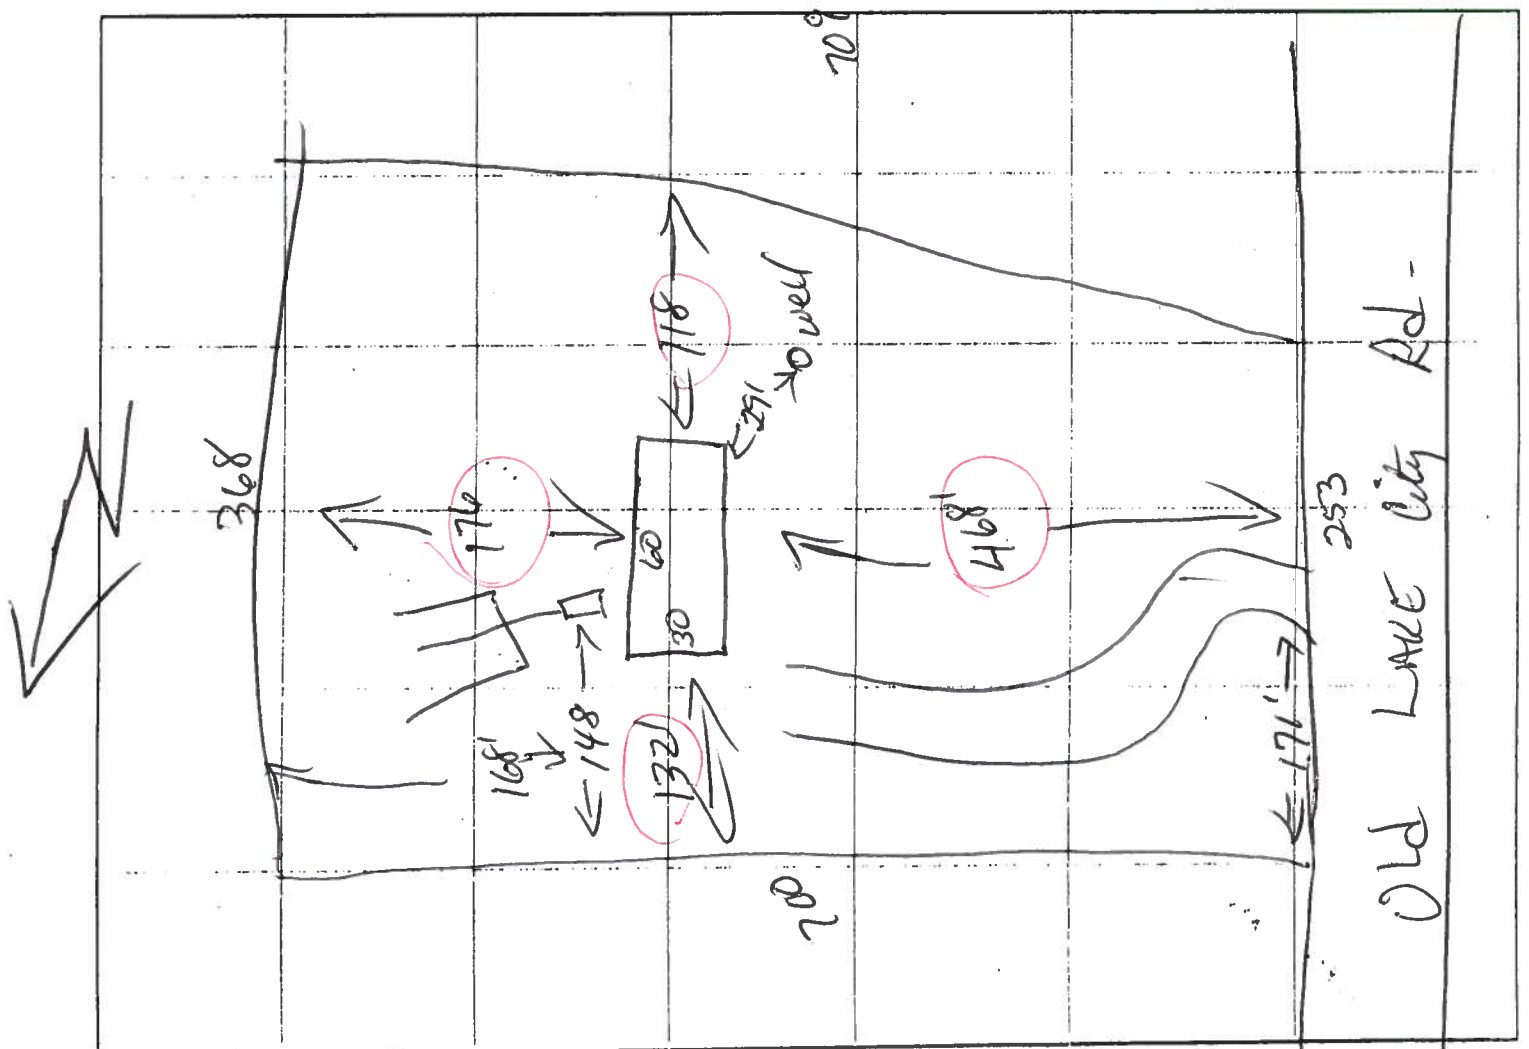

PERMIT NUMBER

Installer Bruce B. Goodson License # IAH0000702


Address of home being installed Sw Old Lake City Terr

Manufacturer High Springs, FL 32643 Length x width 64 (60) x 32

NOTE: if home is a single wide fill out one half of the blocking plan if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used) where the sidewall ties exceed 5 ft 4 in.

Installer's initials

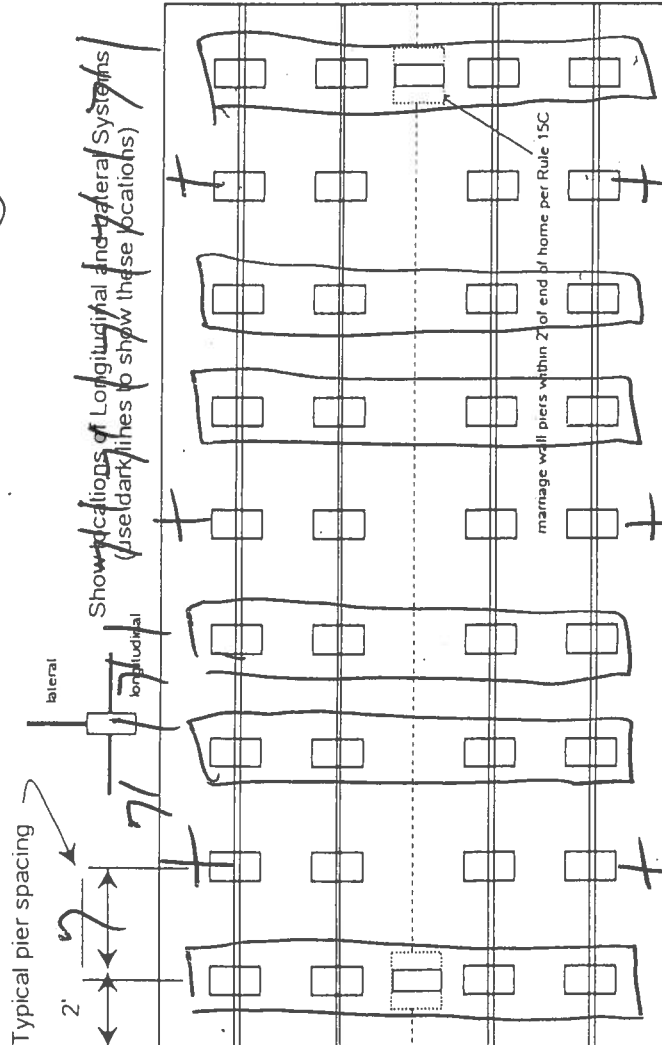

Found Concrete 16" x 20" with 4" x 8" deep
 continuous of 2 #5 Bars
 ABS PDS close where 17x22
 Paul voni zeal Anchors 5444 OLC
 or less
 6) Oliver 1101 V's -

New Home



Used Home



Home installed to the Manufacturer's Installation Manual



Home is installed in accordance with Rule 15-C



Single wide



Wind Zone II



Wind Zone III



Double wide



Installation Decal #

254158

Triple/Quad



Serial #

DIAL-10600994 AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psf	3'	4'	4'	5'	6'	7'	8'
1500 psf	4'	6'	6'	7'	8'	8'	8'
2000 psf	6'	8'	8'	8'	8'	8'	8'
2500 psf	7'	8'	8'	8'	8'	8'	8'
3000 psf	8'	8'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size

17 1/2 x 22 1/2

Perimeter pier pad size

16 x 16

Other pier pad sizes

Panel 8" deep
2 #5 Bars continuous

Draw the approximate locations of marriage wall openings 4 foot or greater Use this symbol to show the piers



List all marriage wall openings greater than 4 foot and their pier pad sizes below

Opening

20'

Pier pad size

22 x 17

4 ft

6 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer OLIVER (3)

OTHER TIES

Number

Sidewall

Longitudinal

Marriage wall

Shearwall

per manual

per manual

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb soil without testing

x 1800

x 1600

x 1600

POCKET PENETROMETER TESTING METHOD

- 1 Test the perimeter of the home at 6 locations
- 2 Take the reading at the depth of the footer
- 3 Using 500 lb increments, take the lowest reading and round down to that increment

x 1800

x 1600

x 1600

TORQUE PROBE TEST

The results of the torque probe test is 291 inch pounds or check here if you are declaring 5' anchors without testing A test showing 275 inch pounds or less will require 4 foot anchors

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the foundation locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Quinty Howard

Installer Name

Date Tested

12-26-05

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source This includes the bonding wire between multi-wide units Pg

Plumbing

Pg

Connect all sewer drains to an existing sewer tap or septic tank
Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems Pg

Site Preparation

Debris and organic material removed Swale Pad Other
Water drainage: Natural

Fastening multi wide units

Floor Type Fastener 3/8 lag Length 6" Spacing 24"OC
Walls Type Fastener 1/4 screw Length 3" Spacing 24"OC
Roof Type Fastener 3/8 lag Length 6" Spacing 24"OC
For used homes a min 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv roofing nails at 2" on center on both sides of the centerline

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket

Installer's initials

Installed

Between Floors Yes

Between Walls Yes

Bottom of ridgebeam Yes

Type gasket foam/plastic

Weatherproofing

The bottomboard will be repaired and/or taped Yes Pg

Siding on units is installed to manufacturer's specifications Yes

Fireplace chimney installed so as not to allow intrusion of rain water Yes

Miscellaneous

Skirting to be installed Yes No

Dryer vent installed outside of skirting Yes N/A

Range downflow vent installed outside of skirting Yes N/A

Drain lines supported at 4 foot intervals Yes

Electrical crossovers protected Yes

Other

Installer verifies all information given with this permit worksheet is accurate and true based on the

manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature

Date

DEER
VALLEY


STEEL BEAM PIER LOADS (LBS.)

ROOF ZONE	SPACING	24'	UNIT WIDTH	
			14' & 28'	16' & 32'
			2562	2748
SOUTH	4' O.C.	-	3203	3435
SOUTH	5' O.C.	-	3844	4122
SOUTH	6' O.C.	-	4484	4809
SOUTH	7' O.C.	-	5125	5496
SOUTH	8' O.C.	-		

SIDEWALL OPENING PIER LOADS (LBS)

OPENING WIDTH	ROOF ZONE	24'	UNIT WIDTH	
			14' & 28'	16' & 32'
			475	510
4'	SOUTH	-	713	765
6'	SOUTH	-	950	1020
8'	SOUTH	-	1188	1275
10'	SOUTH	-	1426	1530
12'	SOUTH	-	1663	1785
14'	SOUTH	-	1901	2040
16'	SOUTH	-		

- NOTES: (1) OPENING WIDTH = opening width of the door and/or window opening in sidewall; if the same pier supports loads from two adjacent openings add the adjacent opening widths together before using the chart above.
- (2) The table is applicable to the nominal home widths when constructed from the module dimensions specified below:
- 24': N/A
 - 28': 166" floor with 12" max. roof overhang
 - 32': 180" floor with 12" max. roof overhang
 - 14': N/A
 - 16': N/A
- (3) The table is applicable to floor systems which do not require perimeter blocking.



RECOMMENDED FOOTING SIZES
BASED ON 1500 PSF ALLOWABLE SOIL BEARING CAPACITY

<u>PIER LOAD</u>	<u>MIN. FOOTING SIZE</u>
2000#	16" x 16"
2500#	18" x 18"
3000#	19" x 19"
3500#	20" x 20"
4000#	21" X 21"
4500#	23" x 23"
5000#	24" x 24"
5500#	25" x 25"
6000#	26" X 26"
7000#	28" x 28"
8000#	30" X 30"
9000#	32" x 32"
10000#	34" X 34"
12000#	36" X 36"
14000#	40" X 40"
16000#	42" X 42"

- NOTES: (1) The thickness and depth of the footing must be in compliance with local code requirements. The footing must, however, have a minimum thickness equal to the maximum projection of the footing beyond the pier and must extend below the frost depth in the area the home is located.
- (2) All organic material must be removed below the footing and the footing must bear on stable soil at least 12 inches below natural grade with a minimum allowable bearing capacity of 1500 PSF.
- (3) Footing material to be concrete with a minimum compressive strength @ 28 days equal to 2500 psi.
- (4) Alternative footing materials acceptable to the local building official may be used in lieu of the footing specifications listed above.



DEER VALLEY

TYPICAL FOOTING SPECIFICATIONS

16" x 16"

- (1) 16" x 16" x 4" PRECAST FOOTING OR
- (2) 16" x 8" x 4" PRECAST FOOTING OR
- (1) 16" x 16" x 6" POURED-IN-PLACE FOOTING

SINGLE OR DOUBLE TIERED PIERS

MAXIMUM PIER LOADS	1773 LB	2659 LB	3546 LB	4432 LB
SOIL CAPACITY (PSF)	1000	1500	2000	2500

24" x 16"

- (3) 16" x 8" x 4" PRECAST FOOTING OR
- (1) 24" x 16" x 6" POURED-IN-PLACE FOOTING

SINGLE OR DOUBLE TIERED PIERS

MAXIMUM PIER LOADS	2666 LB	3999 LB	5332 LB	6665 LB
SOIL CAPACITY (PSF)	1000	1500	2000	2500

24" x 24"

- (5) 16" x 8" x 4" PRECAST FOOTING (SHOWN) OR
- (1) 24" x 24" x 6" POURED-IN-PLACE FOOTING


DOUBLE TIERED PIERS ONLY

MAXIMUM PIER LOADS	4000 LB	6000 LB	8000 LB	10000 LB
SOIL CAPACITY (PSF)	1000	1500	2000	2500


GENERAL NOTES:

1. CONCRETE COMPRESSIVE STRENGTH:
PRECAST = 4000 PSI AT 28 DAYS
POURED-IN-PLACE = 2500 PSI AT 28 DAYS

2. POURED-IN-PLACE FOOTINGS MUST BE
POURED OVER (MIN) 4 MIL POLETHYLENE.


	THIRD PARTY	REVISIONS			DEER VALLEY SUPPORT SYSTEM FIELD INSTALLED
		LTR:	BY:	DATE:	
		DRAWN BY: WK			DAPIA NO.: 14

DOUBLE WIDE BLOCKING INSTALLATION

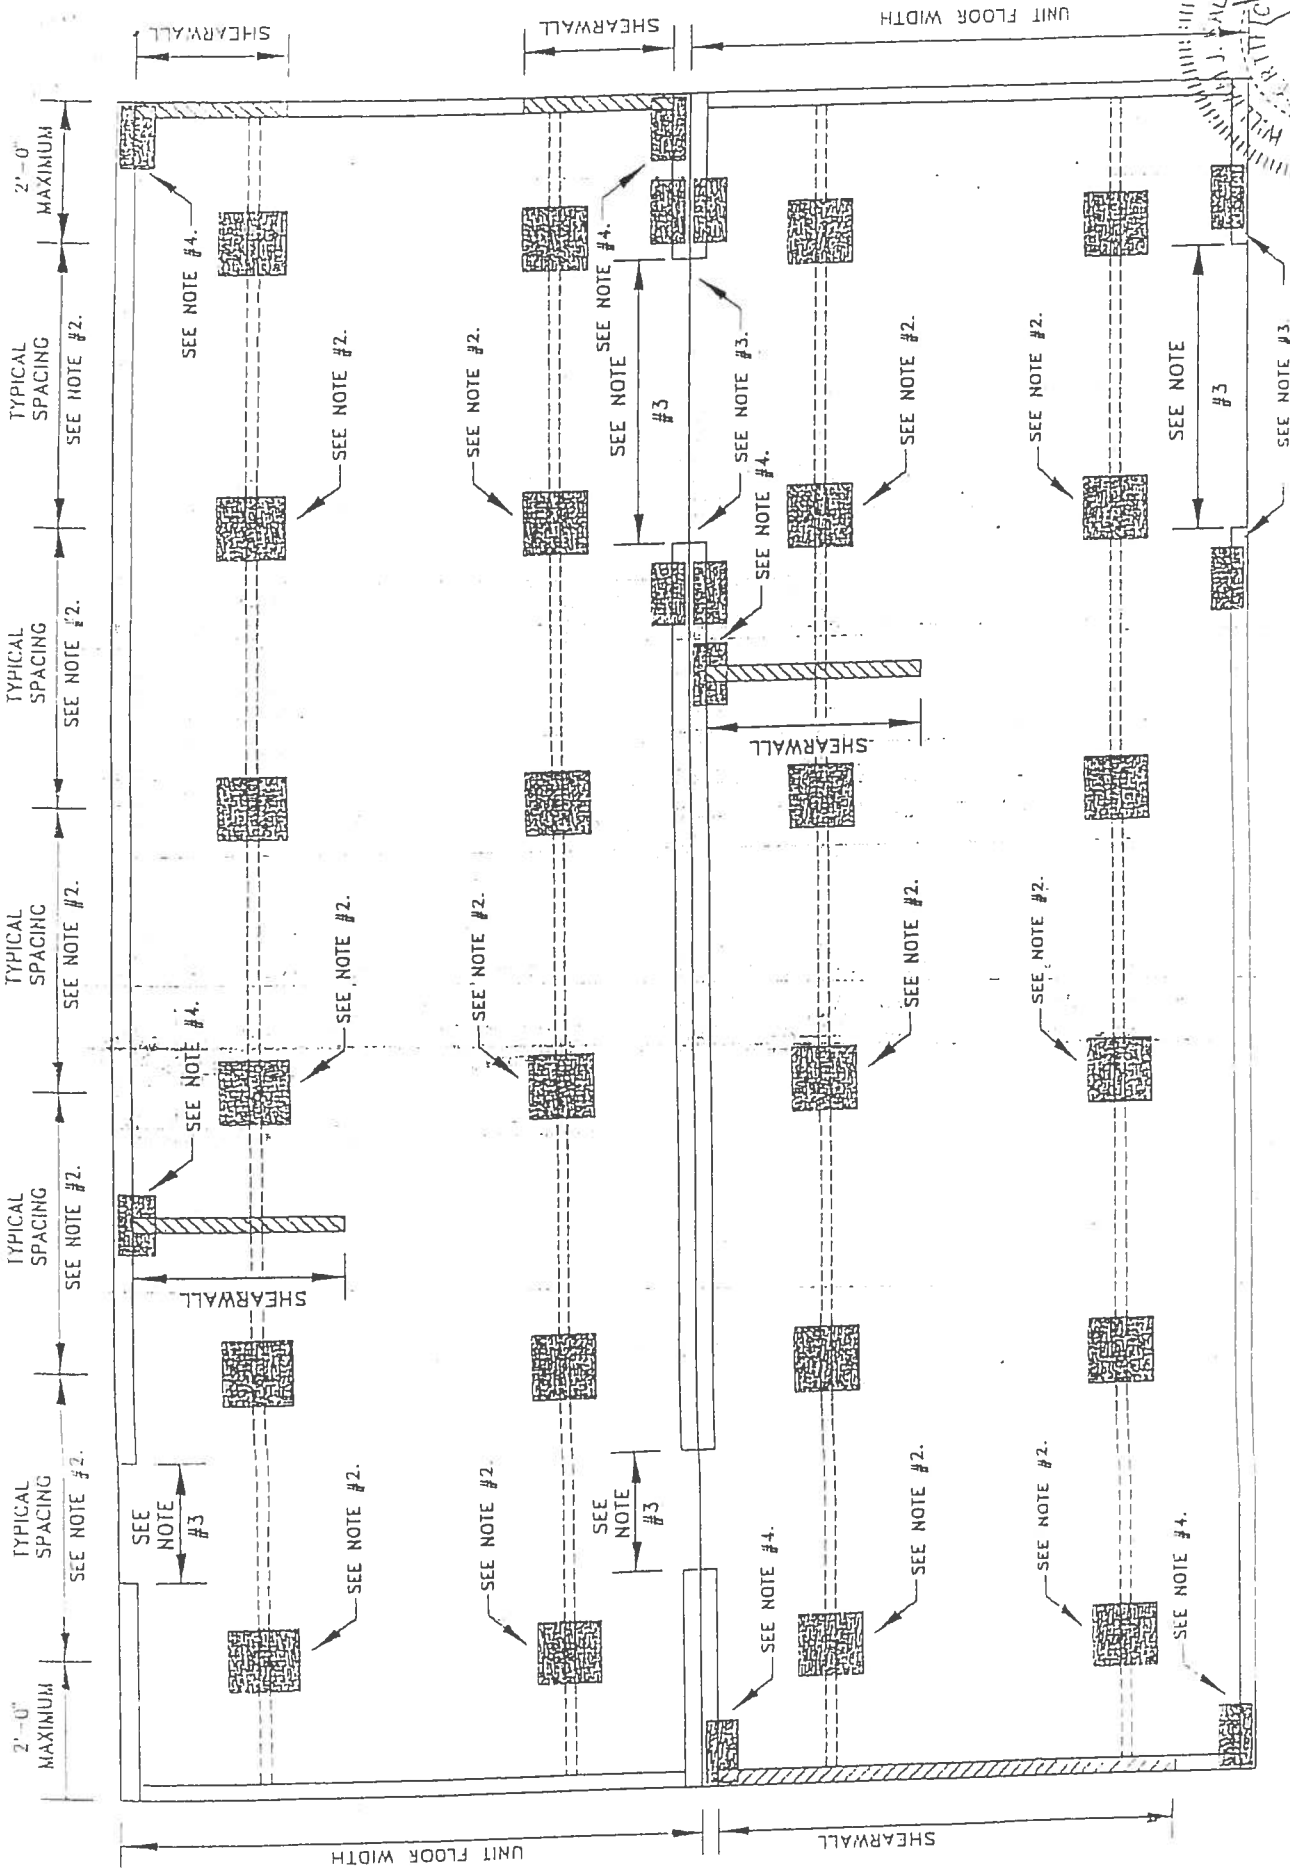

- NOTES:
1. SEE OTHER DETAILS FOR TIEDOWN AND ANCHORAGE SPECIFICATIONS.
 2. SEE MINIMUM FOOTING SIZE TABLE FOR STEEL I-BEAM PIERS.
 3. SEE MINIMUM FOOTING SIZE TABLE FOR SIDEWALL AND MARRIAGE WALL OPENINGS.
 4. SEE MINIMUM FOOTING SIZE TABLE FOR SIDEWALL AND MARRIAGE WALL OPENINGS.

OPENINGS GREATER THAN 4'-0" MAXIMUM BLOCKING IS REQUIRED AT EACH SIDE OF THE OPENING.






STATE OF FLORIDA
DEPARTMENT OF HEALTH
APPLICATION FOR ONSITE SEWAGE DISPOSAL SYSTEM CONSTRUCTION PERMIT

Permit Application Number 05-1284N

PART II - SITE PLAN

Scale: Each block represents 5 feet and 1 inch = 50 feet.

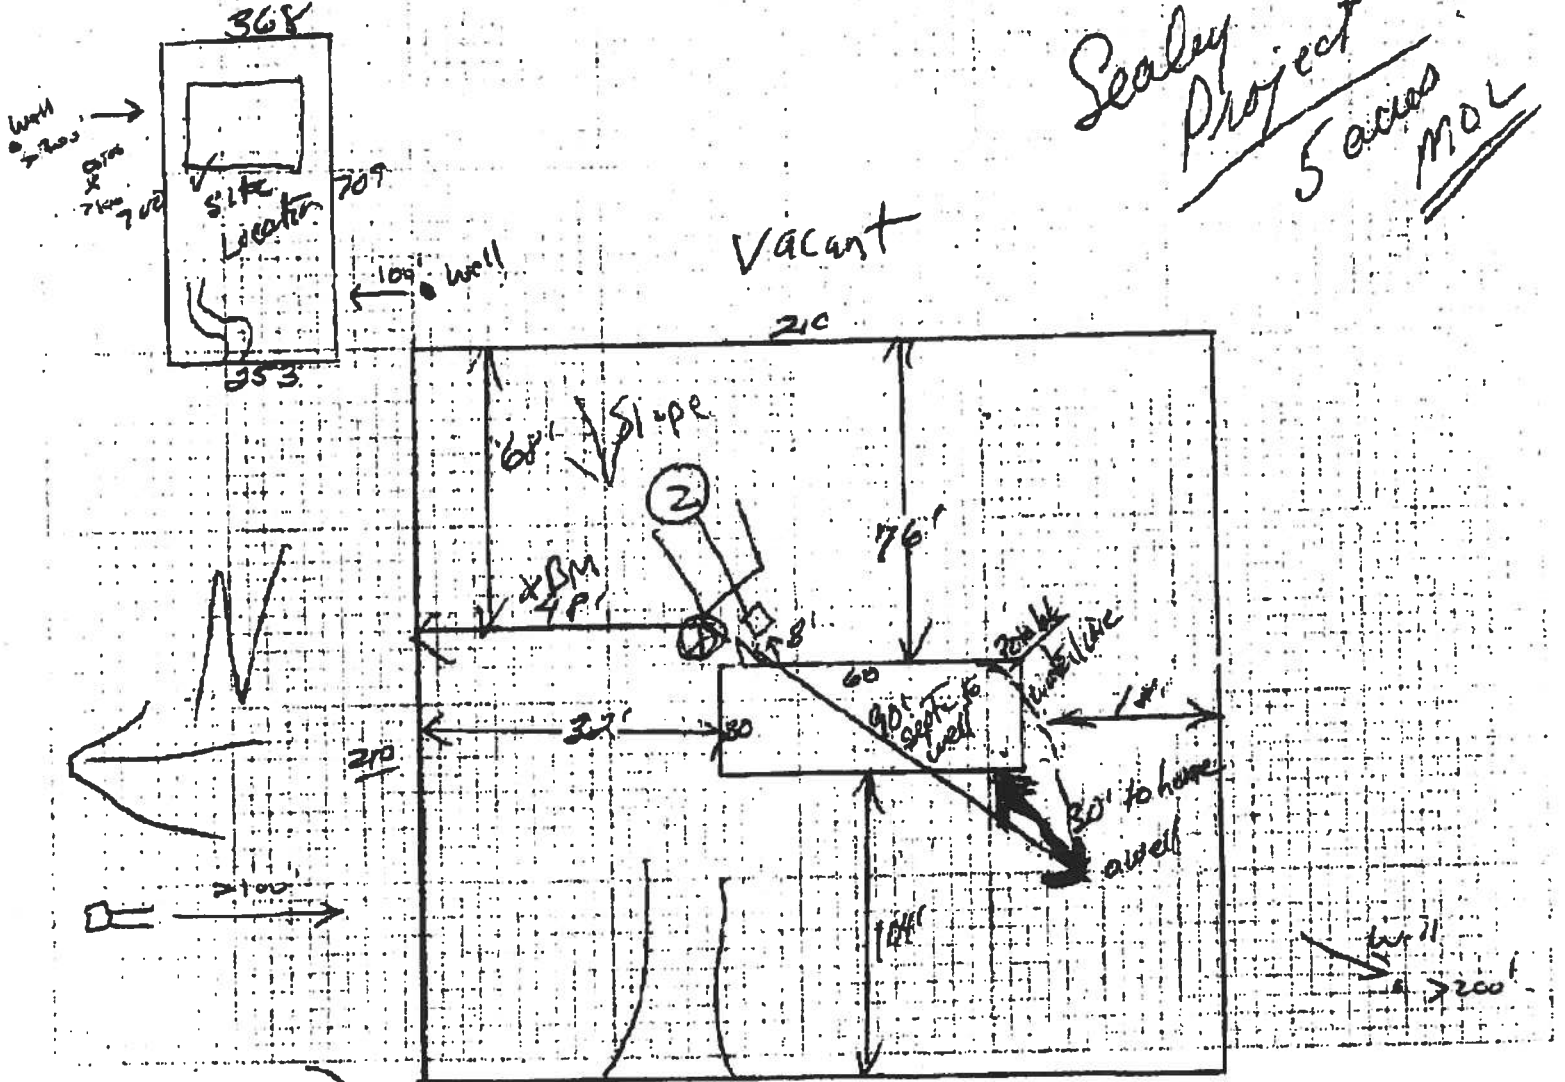

Notes: (2331) OLD LAK City TERR

Site Plan submitted by: Gary Hamilton

Plan Approved ☒

Signature
Not Approved ☐

By Mr S. L. L.

Columbia

Agent
Title
Date 1-11-08
County Health Department

ALL CHANGES MUST BE APPROVED BY THE COUNTY HEALTH DEPARTMENT.



Engineers • Planners

24037

161 N.W. Madison St., Suite 102
Lake City, Florida 32055
Tel: 386-758-4209
Fax: 386-758-4290

February 16, 2006

Columbia County Building and Zoning

RE: Tammy Sealey Residence

To whom it may concern:

I have reviewed the Flood Insurance Rate Map and have determined the property is not located in a flood zone. I have performed a site evaluation of the existing area. I certify that placing the bottom of the steel frame a minimum of 18" above the existing grade is adequate to prevent flood and water damage. Grade the perimeter so that all runoff drains away from the building.

Sincerely,

William H. Freeman, P.E.
President
Cert. Of Authorization #00008701



**513 SW Deputy J Davis Lane
Lake City, FL 32024
Phone: (386) 758-6755
(Fax) 758-9875**

Quality Built Manufactured and Modular Homes At Affordable Prices

January 31, 2006

Columbia County Building Dept.
Lake City, Fl

Ph: 758-1008
Fx: 758-2160

3 pages
faxed @
10:30

RE: Permit No. 24037
Tammy Sealey

Bruce Goodson will no longer be the installer for the above referenced permit. The new installer is Bernard Thrift. His installer paperwork is attached. The address for Bernard Thrift is 212 NW Nyc Hunter Dr Lake City, Fl 32055. His License # is IH0000075. Phone numbers 386-752-9561,(cell)386-623-0046.

Please contact us if anything further is needed.

Thank you


Gary Hamilton

PERMIT NUMBER 24037
Installer Bernard Thrift **License #** TH0000075
Address of home being installed 2231 SW Old Lake City Terrace
High Springs, FL 32643
Manufacturer Deer Valley **Length x width** 64' (60') x 32'

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials BT

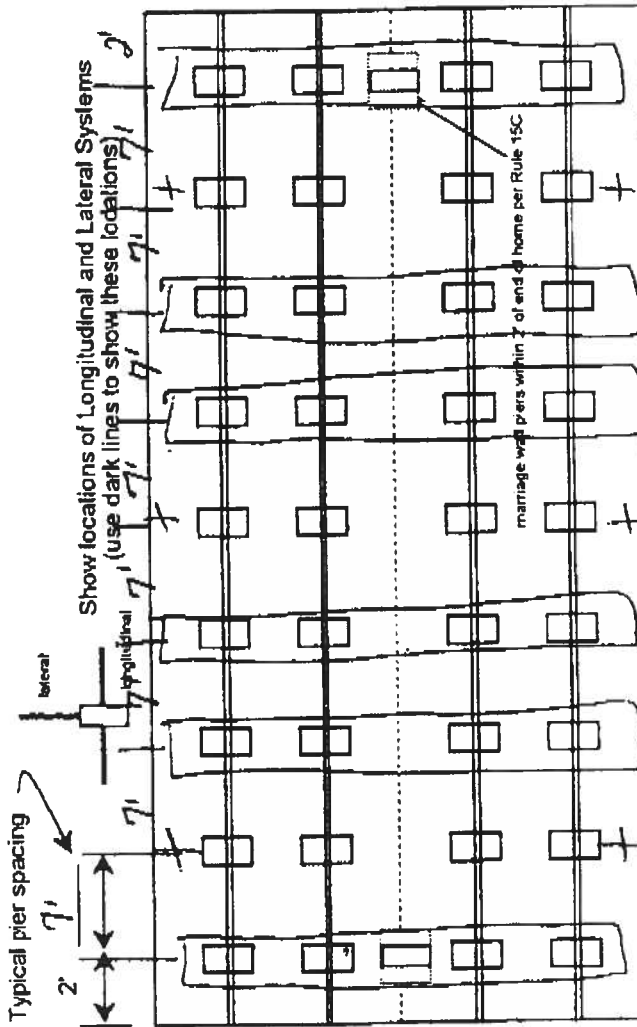

poured concrete 16" to 20" wide by 24" deep
 continuous w/ 2#5 bars steel
 ABS pads elsewhere 17x22
 Galvanized Anchors 5" x 8" x 10" long
 (6) Oliver 1101 US

☒ New Home ☐ Used Home
 Home installed to the Manufacturer's Installation Manual
 Home is installed in accordance with Rule 15-C
☐ Single wide ☐ Wind Zone II ☐ Wind Zone III
☒ Double wide ☒ Installation Decal # 257820
☐ Triple/Quad ☐ Serial # 8VAH0600994AB

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footer size (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)	24" x 24" (576)	26" x 26" (676)
1000 psi	3'	3'	4'	5'	6'	7'	8'
1500 psi	4' 6"	4' 6"	6'	7'	8'	8'	8'
2000 psi	6'	6'	8'	8'	8'	8'	8'
2500 psi	7' 6"	7' 6"	8'	8'	8'	8'	8'
3000 psi	8'	8'	8'	8'	8'	8'	8'
3500 psi	8'	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 17 1/2 x 22 1/2

Perimeter pier pad size 16 x 16

Other pier pad sizes (required by the mfg.) forced 8" deep
2#5 bars continuous

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening 20' Pier pad size 22x17

5'

POPULAR PAD SIZES

Pad Size	Sq In
16 x 16	256
16 x 18	288
18 1/2 x 18 1/2	342
16 x 22 1/2	360
17 x 22	374
13 1/4 x 28 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

4 ft ☒ 5 ft

FRAME TIES

within 2' of end of home spaced at 5' 4" oc

OTHER TIES

Number

Sidewall
 Longitudinal
 Marriage wall
 Shearwall

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer Oliver (3)

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to 1500 psf or check here to declare 1000 lb. soil without testing.

1800 x 1600 x 1600

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

1500 x 1600 x 1800

TORQUE PROBE TEST

The results of the torque probe test is 291 inch pounds or check here if you are declaring 5' anchors without testing. A test showing 275 inch pounds or less will require 4 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name Bernard Thrift

Date Tested 1-31-06

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. ✓

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. ✓
 Connect all potable water supply piping to an existing water meter, water tap, or other water supply systems. Pg. ✓

Site Preparation

Debris and organic material removed ✓
 Water drainage: Natural ✓ Swale ✓ Pad ✓ Other ✓

Fastening multi wide units

Floor: Type Fastener: 3/8x6" Length: 6" Spacing: 24"
 Walls: Type Fastener: 1/2x50" Length: 3" Spacing: 12"
 Roof: Type Fastener: 3/8x6" Length: 6" Spacing: 24"
 For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials BT

Installed:

Between Floors Yes ✓
 Between Walls Yes ✓
 Bottom of ridgebeam Yes ✓

Type gasket Flashed

Weatherproofing

The bottomboard will be repaired and/or lapped. Yes ✓ Pg. ✓
 Siding on units is installed to manufacturer's specifications. Yes ✓
 Fireplace chimney installed so as not to allow intrusion of rain water. Yes ✓

Miscellaneous

Skirting to be installed. Yes ✓ No ✓
 Dryer vent installed outside of skirting. Yes ✓ N/A ✓
 Range downflow vent installed outside of skirting. Yes ✓ N/A ✓
 Drain lines supported at 4 foot intervals Yes ✓
 Electrical crossovers protected. Yes ✓
 Other: ✓

Installer verifies all information given with this permit worksheet is accurate and true based on the

manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Bernard Thrift

Date 1-31-06

CHRYSLER AVENUE
OF

M/H O C C U P A N C Y

COLUMBIA COUNTY, FLORIDA

Department of Building and Zoning Inspection

This Certificate of Occupancy is issued to the below named permit holder for the building and premises at the below named location, and certifies that the work has been completed in accordance with the Columbia County Building Code.

Parcel Number 04-7S-17-09891-005


Building permit No. 0000224037

Permit Holder BRUCE GOODSON

Owner of Building TAMMY SEALEY

Location: 2231 SW OLD LAKE CITY TERR

Date: 02/17/2006



Building Inspector

POST IN A CONSPICUOUS PLACE
(Business Places Only)
