

Department of Information Technology

PERMIT WORKSHEET


PERMIT NUMBER

Installer Ernest Scott Johnson License # IH-1025249
 Installer Mobile Phone # 352-494-8099
 Address of home being installed 1817 SW US Hwy 27
Fort White FL 32038
 Manufacturer dcervalley Length x width 66 x 30

NOTE: if home is a single wide fill out one half of the blocking plan
 if home is a triple or quad wide sketch in remainder of home

I understand Lateral Arm Systems cannot be used on any home (new or used)
 where the sidewall ties exceed 5 ft 4 in.

Installer's initials ESJ

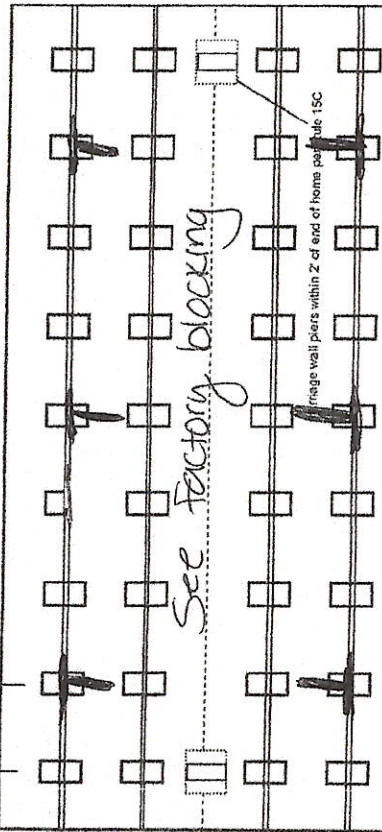

New Home ☒ Used Home ☐
 Home installed to the Manufacturer's Installation Manual ☒
 Home is installed in accordance with Rule 15-C ☐
 Single wide ☐ Wind Zone II ☐ Wind Zone III ☒
 Double wide ☒ Installation Decal # 103572
 Triple/Quad ☐ Serial # _____

Roof System: ☒ Typical ☐ Hinged

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (sq in)	16" x 16" (256)	18 1/2" x 18 1/2" (342)	20" x 20" (400)	22" x 22" (484)*	24" x 24" (576)*	26" x 26" (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	8'
2000 psf	5'	6'	7'	8'	8'	8'
2500 psf	6'	7'	8'	8'	8'	8'
3000 psf	7'	8'	8'	8'	8'	8'
3500 psf	8'	8'	8'	8'	8'	8'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 23x31 6.6
 Perimeter pier pad size 17.5 x 25.5
 Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

POPULAR PAD SIZES

Pad Size	Sq in
16 x 16	256
16 x 18	288
18.5 x 18.5	342
16 x 22.5	360
17 x 22	374
13 1/4 x 26 1/4	348
20 x 20	400
17 3/16 x 25 3/16	441
17 1/2 x 25 1/2	446
24 x 24	576
26 x 26	676

ANCHORS

Opening See factory blocking Pier pad size 23x31 6.6
 4 ft ☒ 5 ft ☒

FRAME TIES

within 2' of end of home spaced at 5' 4" oc ☒

OTHER TIES

Number _____
 Sidewall 38
 Longitudinal 30
 Marriage wall 10
 Shearwall 2

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
 Manufacturer _____
 Longitudinal Stabilizing Device w/ Lateral Arms
 Manufacturer Oliver Ho

PERMIT NUMBER

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to _____ psf or check here to declare 1000 lb. soil _____ without testing.

x 1000 x 1000 x 1000

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 6 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

x 1000 x 1000 x 1000

TORQUE PROBE TEST

The results of the torque probe test is _____ inch pounds or check here if you are declaring 5' anchors without testing _____ A test showing 275 inch pounds or less will require 5 foot anchors.

Note: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewall locations. I understand 5 ft anchors are required at all centerline tie points where the torque test reading is 275 or less and where the mobile home manufacturer may requires anchors with 4000 lb. holding capacity.

Installer's initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Date Tested

Ernest Scott Johnson
Assumed Oliver 1101V
Uses 4 x 5' Anchors

Electrical

Connect electrical conductors between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg. _____

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg. _____

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg. _____

Site Preparation

Debris and organic material removed _____
Water drainage: Natural _____ Swale _____ Pad ☒ Other _____

Fastening multi wide units

Floor: Type Fastener: lags Length: 6 Spacing: 20
Walls: Type Fastener: lags Length: 4 Spacing: 12
Roof: Type Fastener: lags Length: 6 Spacing: 20
For used homes a min. 30 gauge, 8" wide, galvanized metal strip will be centered over the peak of the roof and fastened with galv. roofing nails at 2" on center on both sides of the centerline.

Gasket (weatherproofing requirement)

I understand a properly installed gasket is a requirement of all new and used homes and that condensation, mold, mildew and buckled marriage walls are a result of a poorly installed or no gasket being installed. I understand a strip of tape will not serve as a gasket.

Installer's initials ESJ

Type gasket Pg. pull

Installed:

Between Floors Yes ☒
Between Walls Yes ☒
Bottom of ridgebeam Yes ☒

Weatherproofing

The bottomboard will be repaired and/or taped. Yes ☒ Pg. _____
Siding on units is installed to manufacturer's specifications. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes _____

Miscellaneous

Skirting to be installed. Yes ☒ No _____
Dryer vent installed outside of skirting. Yes ☒ N/A _____
Range downflow vent installed outside of skirting. Yes ☒ N/A _____
Drain lines supported at 4 foot intervals. Yes ☒
Electrical crossovers protected. Yes ☒ Other: _____

Installer verifies all information given with this permit worksheet is accurate and true based on the manufacturer's installation instructions and or Rule 15C-1 & 2

Installer Signature Ernest Scott Johnson Date _____



License Number: IH / 1025249 / 1 Name: ERNEST SCOTT JOHNSON

Order #: 5948	Label #: 103572	Manufacturer:	(Check Size of Home)
Homeowner:		Year Model:	Single _____
Address:		Length & Width:	Double _____
			Triple _____
City/State/Zip:		Type Longitudinal System:	HUD Label #:
Phone #:		Type Lateral Arm System:	Soil Bearing / PSF:
Date Installed:		New Home: _____ Used Home: _____	Torque Probe / in-lbs:
Installed Wind Zone:		Data Plate Wind Zone:	Permit #:

Note:

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

103572

LABEL #

DATE OF INSTALLATION

ERNEST SCOTT JOHNSON

NAME

IH / 1025249 / 1

5948

LICENSE #

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES.

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.



MOBILE HOME INSTALLATION SUBCONTRACTOR VERIFICATION FORM

APPLICATION NUMBER _____ CONTRACTOR _____ PHONE _____

THIS FORM MUST BE SUBMITTED PRIOR TO THE ISSUANCE OF A PERMIT

In Columbia County one permit will cover all trades doing work at the permitted site. It is REQUIRED that we have records of the subcontractors who actually did the trade specific work under the permit. Per Florida Statute 440 and Ordinance 89-6, a contractor shall require all subcontractors to provide evidence of workers' compensation or exemption, general liability insurance and a valid Certificate of Competency license in Columbia County.

Any changes, the permitted contractor is responsible for the corrected form being submitted to this office prior to the start of that subcontractor beginning any work. Violations will result in stop work orders and/or fines.

ELECTRICAL	Print Name <u>Glenn Whittington</u> Signature <u></u> License #: <u>EC13002957</u> Phone #: <u>386-972-1700</u> Qualifier Form Attached ☒
MECHANICAL/ A/C _____	Print Name <u>Timothy Shatto</u> Signature <u></u> License #: <u>CAC057875</u> Phone #: <u>386-496-8224</u> Qualifier Form Attached ☒

F. S. 440.103 Building permits; identification of minimum premium policy.--Every employer shall, as a condition to applying for and receiving a building permit, show proof and certify to the permit issuer that it has secured compensation for its employees under this chapter as provided in ss. 440.10 and 440.38, and shall be presented each time the employer applies for a building permit.

WHITTINGTON ELECTRIC INC

164 QUEENS COUNTRY RD, INTERLACHEN FLORIDA 32148

PHONE: 386-684-4601 CELL: 386-972-1700 OR 1701

FAX: 386-684-3906 E-FAX#:866-496-3066 EMAIL:-whitt1954@gmail.com

This letter is to state that I, Glenn Whittington, state certified electrical contractor #EC13002957 authorize Kimberly koon to act on my behalf in obtaining permits in any county or city in the state of florida.

This authorization is to remain in effect indefinitely, unless cancelled by me in writing.


Glenn Whittington

Sworn to and subscribed to before me this 19 day of Aug 2019 by Glenn Whittington who is personally known to me.

Susan M. Pahl

Notary public

My commission expires 11-30-21.





October 20, 2022

STATE OF FLORIDA

PERMIT AUTHORIZATION LETTER

I, RONALD E BONDS, SR, Mechanical License number CAC1817658, Electrical License number EC13007246, hereby authorize the following to obtain a mechanical HVAC permit and corresponding HVAC wiring permit (if necessary) for ANY install in the STATE OF FLORIDA, on behalf of Style Crest, Inc.

Kimberly Koon

This authorization is to remain in effect indefinitely, unless cancelled by me in writing.

A handwritten signature in blue ink, appearing to read "Ronald E Bonds", written over a horizontal line.

Contractor's Signature

Sworn to and subscribed before me this 20 day of October, 2022
By RONALD E BONDS, SR who is personally known to me or has produced _____
as identification and who did/did not take an oath.

A handwritten signature in blue ink, appearing to read "Stephanie Heidelberg", written over a horizontal line.
Notary Public

My commission expires: 3-29-2025



STEPHANIE HEIDELBURG
Notary Public, State of Ohio
My Commission Expires:
03/29/2025

PURCHASE AGREEMENT

278 SW Deputy J. Davis Ln.
Lake City, Florida 32024



752-3743 or
752-3744




Fax: 386-755-2386
Email: cgmfg homes@comcast.net

C & G MANUFACTURED HOMES

Locally Owned and Operated

SOLD TO Rodney & Leslie Pritchard		PHONE 386-454-3757		DATE 6/2/23	
ADDRESS 1817 SW US Hwy 27 Fort White FL 32038				COUNTY Columbia	
In consideration of and subject to the terms and conditions stated in this purchase agreement Seller agrees to sell and Buyers to purchase the following described property:				EMAIL	
MAKE Deer Valley	MODEL Aimon	B. ROOMS 3	FLOOR SIZE L 66 W 32	HITCH SIZE L 70 W 32	
SERIAL NUMBER DVAL12311080AB	2024	☒ NEW ☐ USED	COLOR Stone Lion	SALESMAN Pratt Koon	
OPTIONAL EQUIPMENT, LABOR AND ACCESSORIES			PRICE OF UNIT 285,605.00		
Price Includes:					
Ordered unit built to most recent signed spec sheet			SALES TAX 3% + 75.00 7,743.15		
Set-up & delivery according to C&G Homes Set-up agreement			NON-TAXABLE ITEMS		
3 sets of Code steps			VARIOUS FEES		
Hardie lap to the ground			1. CASH PRICE \$293,348.15		
4 ton AC with Heat Pump			TRADE-IN ALLOWANCE \$30,000.00		
Pad Installed			LESS BAL. DUE ON ABOVE \$		
Hookups(water,sewer,power) included			NET ALLOWANCE		
			CASH DOWN PAYMENT 16,740.00		
			2. LESS TOTAL CREDITS		
			3. UNPAID BALANCE OF CASH SALE PRICE \$246,608.015		
			Title to said unit shall remain in the Seller until the agreed purchase price there for is paid in full in cash or by the execution of a Retail Installment Contract, or a Security Agreement and its acceptance by a financing agency; there upon title to the within described unit passes to the buyer as of the date of either full cash payment or on the signing of said credit instruments even though the actual physical delivery may not be made until a later date.		
			IT IS MUTUALLY UNDERSTOOD THAT THIS AGREEMENT IS SUBJECT TO NECESSARY CORRECTIONS, AND ADJUSTMENTS CONCERNING CHANGES IN NET PAYOFF ON TRADE-IN TO BE MADE AT THE TIME OF SETTLEMENT.		
FOR THE PURPOSE OF THIS AGREEMENT THE TERM (BUYER) OR (BUYERS) MAY BE USED INTERCHANGEABLE AND MAY REPRESENT SINGULAR OR PLURAL IN MEANING.			Buyer represents he/she examined the unit and found it suitable for his/her particular needs, and that it is of acceptable quality and that buyer relied upon his/her judgment and inspection in making this determination.		
Seller is not permitted to make plumbing or electrical connections, or connecting certain natural gas or propane appliances where state or local ordinances require a licensed plumber or electrician so to do. Special building ordinances or laws requiring plumbing, electrical or construction changes are not the responsibility of Seller or the manufacturer. Seller is not responsible for obtaining health or sanitation permits, nor for local, county or state permits involving restrictive zoning. (COST OF CHANGES NEEDED FOR COMPLIANCE MUST BE BORNE BY BUYER. IT IS SOLELY THE BUYERS RESPONSIBILITY TO ASSURE THEIR CHOSEN HOME SITE IS ACCEPTABLE FOR HOME PLACEMENT WITHOUT VIOLATION OF ANY LOCAL, STATE, OR FEDERAL GUIDELINES.)			There is no assurance a mobile home can remain level when placed, upon any surface other than of level blacktop or concrete.		
Seller is not responsible or liable for any delays caused by the manufacturer, accidents, strikes, fires, Acts of God, Independent Subcontractors, or any other cause beyond Seller's control.			Buyers warrant that they have read and fully understand and agree to this purchase agreement and the additional terms and conditions; that buyers are of statutory age or older; or have been legally emancipated; that the within described unit, the optional equipment and accessories thereon and, insurance if included, has been voluntarily purchased. The Buyer warrant that the property being traded in is free from all encumbrances whatsoever, except as noted above. Buyer agrees each paragraph and provision of this contract is severable; if one portion thereof is invalid the remaining portion shall, nevertheless, remain in full force and effect.		
BUYERS FULLY UNDERSTAND AND AGREE THAT THE BUYERS WILL BE SOLELY RESPONSIBLE TO PAY ANY PRICE INCREASES GIVEN BY THE MANUFACTURER UNTIL AT WHICH TIME THE HOME IS BUILT AND INVOICED BY THE MANUFACTURER.			BUYERS HEREBY ACKNOWLEDGE RECEIPT OF A COPY OF THE PURCHASE AGREEMENT AND ADDITIONAL TERMS AND CONDITIONS		
C&G MANUFACTURED HOMES Not Valid Unless Signed and Accepted by an officer of the Company		DEALER	SIGNED X <i>Leslie Pritchard</i>		BUYER
By <i>[Signature]</i>			SIGNED X <i>Leslie Pritchard</i>		BUYER
Approved subject to complete and final acceptance of financing by bank, finance company or cash payment in full					
THIS AGREEMENT (TOGETHER WITH ITS ATTACHED SCHEDULES, ADDENDUM, AND EXHIBITS) CONTAINS AND SETS FORTH THE COMPLETE UNDERSTANDING AND AGREEMENT OF THE BUYERS AND THE SELLER, AND SUPERSEDES ALL PRIOR WRITTEN OR ORAL DISCUSSIONS, AGREEMENTS, COMMUNICATIONS, OR REPRESENTATIONS. THIS AGREEMENT MAY BE MODIFIED ONLY BY MEANS OF A WRITING SIGNED BY THE PARTIES TO THIS AGREEMENT. BUYERS AND SELLER BOTH HAD AN OPPORTUNITY TO REVIEW THIS ENTIRE AGREEMENT WITH THE COUNSEL OF THEIR CHOOSING. IN THE EVENT OF LITIGATION OR RELATED LEGAL ACTIONS INVOLVING THIS AGREEMENT, THE TERMS AND CONDITIONS OF THIS AGREEMENT SHALL BE INTERPRETED AS OF EQUAL WEIGHT BETWEEN BUYERS AND SELLER.					

WOODLAND

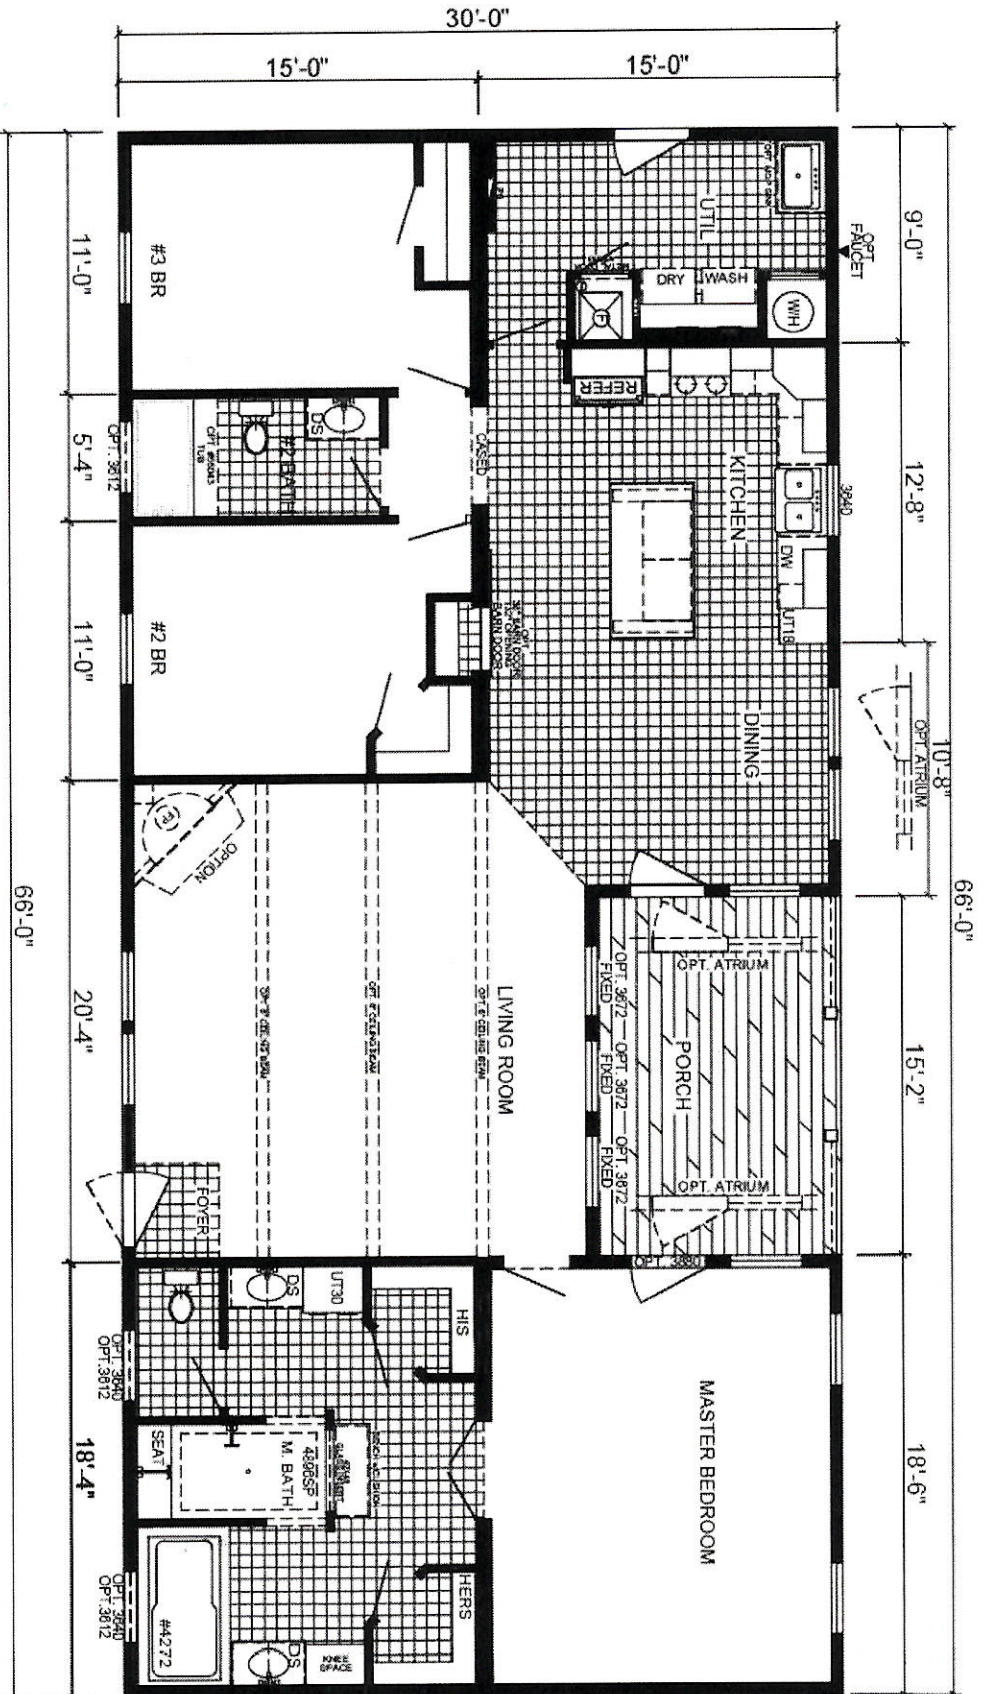

MODEL: **THE AIMON B WL-7012B**
32'-0" x 70'-0" 1,980 Sq.Ft
3 Beds 2 Baths

NEW home

Due to continued improvements and material change, specifications may change without notice. Room sizes are approximate.

Columbia County Property Appraiser


Jeff Hampton | Lake City, Florida | 386-758-1083

Owner & Property Info

Parcel ID: 19-7S-17-10026-007 (37542)

Name	PRITCHARD RODNEY D (exempt: HX-HB--)
Site Addr	1817 SW US HIGHWAY 27, FORT WHITE
Mailing	1817 SW US HWY 27 FORT WHITE, FL 32038
Description	COMM SE COR, RUN W 515.46 FT TO E R/W OF US-27, NW'LY ALONG R/W 2055.87 FT FOR POB, CONT N 26 DEG W ALONG R/W 396.80 FT, N 63 DE 19-7S-17-10026-007

	Bldg Item	Bldg Desc	Year Blt	Base S.F.	Actual S.F.	Bldg Value
Show Sub-Area Codes	1	MOBILE HME (0800)	1985	1568	2092	\$34,319.00

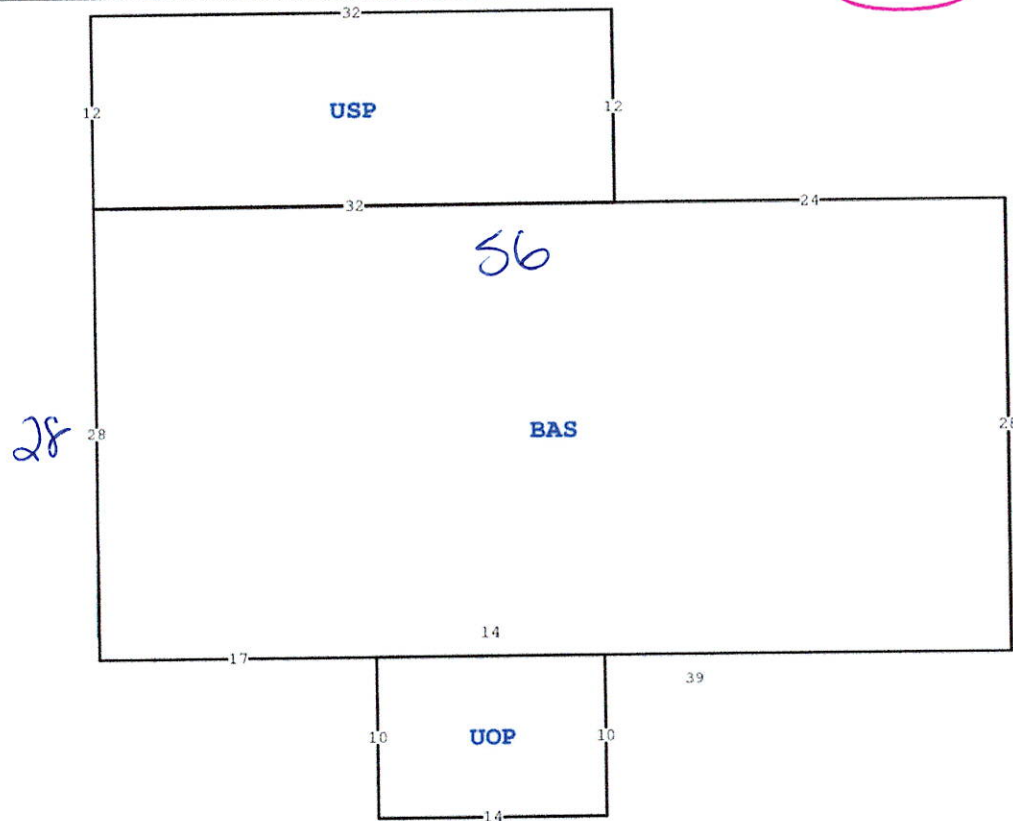


Existing home
to be removed

28x56
3bedroom 2bath
1568 sq ft.

North
1"=60'
S.Oloc.

Drawn by Kim Hoon
386.688.2345
kimh@hcn

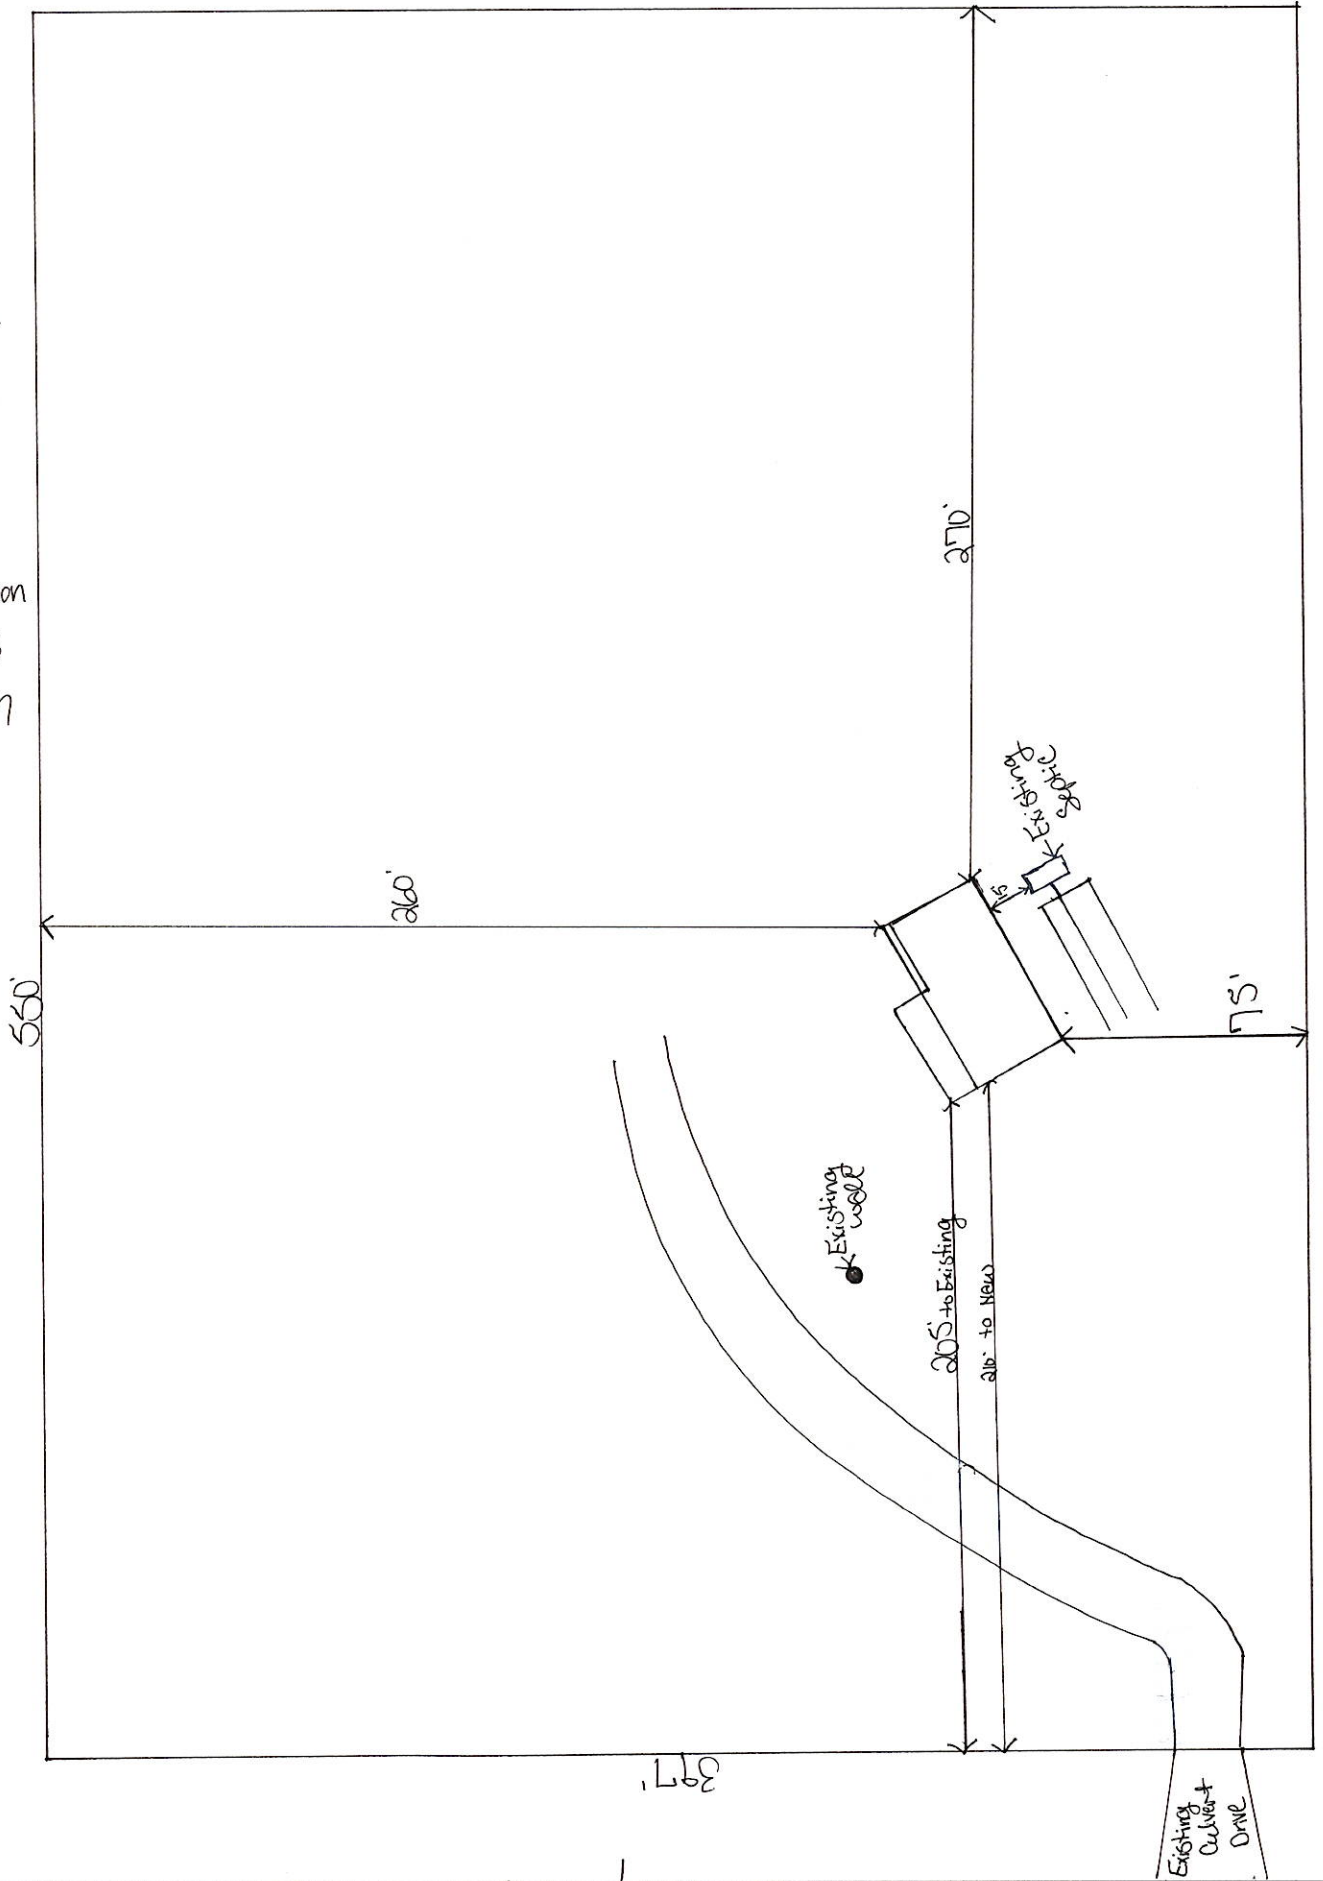

SWUS Hwy 27
