

Mobile Home Permit Worksheet


Installer: Ernest S. Johnson License # EH 1025249

Address of home being installed

Manufacturer Clayton Length x width 28' x 56'

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home (understand Lateral Arm Systems cannot be used on any home where the sidewall has exceed 5 ft 4 in).

Installer's initials

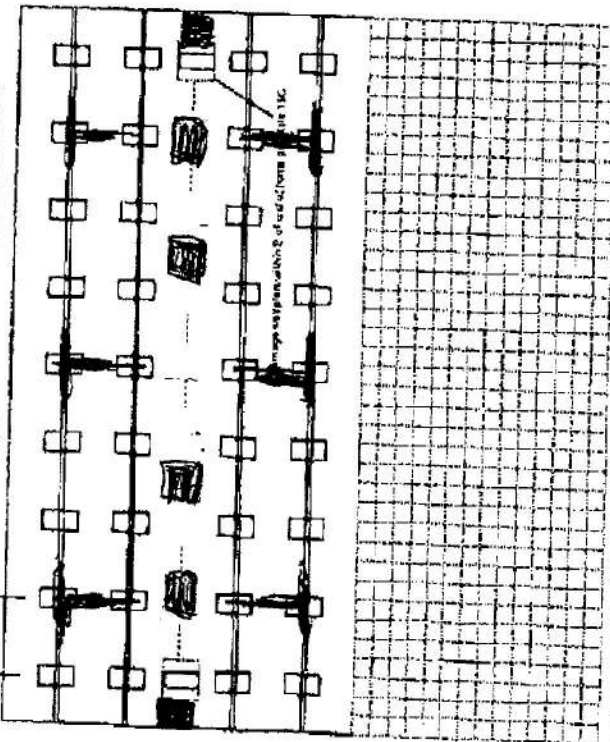

Application Number:

Date:

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Detail # 71901

Triplet/Quad ☐ Serial #

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (40 in)	16' x 16' (256)	18' 1/2' x 18' 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	28' x 28' (676)
1000 lbs	3'	4'	5'	6'	7'	8'
1500 lbs	4'	5'	6'	7'	8'	9'
2000 lbs	5'	6'	7'	8'	9'	10'
2500 lbs	6'	7'	8'	9'	10'	11'
3000 lbs	7'	8'	9'	10'	11'	12'
3500 lbs	8'	9'	10'	11'	12'	13'

Interpolated from Rule 15-C, 1 per spacing table.

PIER PAD SIZES

I-beam pier pad size 23' x 31' 6" x 6"

Perimeter pier pad size 17' 5" x 25' 5"

Other pier pad sizes (measured by the mfg.)

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings smaller than 4 foot and their pier pad sizes below.

Opening Pier pad size

17' 5" x 25' 5"
17' 5" x 25' 5"
17' 5" x 25' 5"

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)

Manufacturer

Longitudinal Stabilizing Device w/ Lateral Arms

Manufacturer

ANCHORS

FRAME TIES

Within 2' of end of home spaced at 5' 4" or

OTHER TIES

Number

Side wall

Longitudinal

Marriage Wall

Shearwall

01/06/2010
