

PERMIT NUMBER

PERMIT WORKSHEET

page 1 of 2



Installer Ernest S Johnson License # EA 1025249

Owner Name & Address of home being installed Convey Hoppel
2855 E Kottler Ct High Springs FL 32643

Manufacturer Scot B.I.F. Length x width 60' x 32'

NOTE: If home is a single wide fill out one half of the blocking plan. If home is a triple or quad wide sketch in remainder of home.

Insulator's initials [Signature]

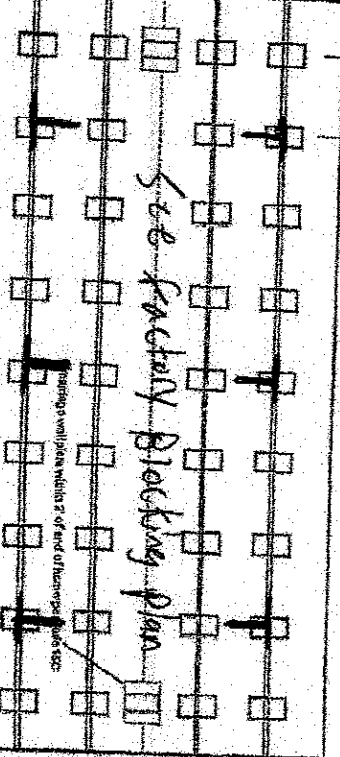

New Home ☒ Used Home ☐ Year Model

Frame installed to the Manufacturer's Installation Manual ☒

Home is installed in accordance with Rule 15-C ☐

Single wide ☐ Wind Zone II ☒ Wind Zone III ☐

Double wide ☒ Installation Detail # 166098

Triple/Quad ☐ Serial # 052-000-H-A52180207

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity (psf)	18' x 16' (252)	18' x 12' x 18' (216)	20' x 16' (320)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	4'	5'	6'	7'	8'
1500 psf	4'	5'	6'	7'	8'	9'
2000 psf	5'	6'	7'	8'	9'	10'
2500 psf	6'	7'	8'	9'	10'	11'
3000 psf	7'	8'	9'	10'	11'	12'

PIER PAD SIZES

1-Beam pier pad size 23' x 31' L.C.

Perimeter pier pad size 54" x wall 17.5 ft

Other pier pad sizes w/ 1/4" hole 1055-11 1/4" hole 56" x 56"

Draw the approximate location of all pier well openings & footing greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4' and their pier pad sizes below.

POPULAR PAD SIZES	Pad size	Weight
16' x 16'	16' x 16'	256
18' x 18'	18' x 18'	324
20' x 20'	20' x 20'	400
22' x 22'	22' x 22'	484
24' x 24'	24' x 24'	576
26' x 26'	26' x 26'	676

Opening ☐ Pier pad size

ANCHORS ☒ 4" ☐ 6" ☐ 8"

FRAME TIES ☐

within 2' of end of home spaced at 5' o.c.

OTHER TIES ☐

Longitudinal Stabilizing Device (L.S.D.) Manufacturer See factory blocking

Longitudinal Stabilizing Device w/ Lateral Arms Manufacturer See factory blocking

Sidewall Longitudinal Marriage wall Strengthening 20

PERMIT WORKSHEET

page 2 of 2

PERMIT NUMBER _____

Page 2 of 2

POCKET PENETROMETER TEST

The pocket penetrometer tests are rounded down to psi or check here to declare 1000 lb. soil without testing.

$\times 1000$ $\times$ $\times$

POCKET PENETROMETER TESTING METHOD

1. Test the perimeter of the home at 5 locations.
2. Take the reading at the depth of the footer.
3. Using 500 lb. increments, take the lowest reading and round down to that increment.

$\times$ $\times$ $\times 1000$

TORQUE PROBE TEST

The results of the torque probe test is first pounds or check here if you are declaring 5 anchors without testing. A test showing 275 foot pounds or less will require 5 foot anchors.

Notes: A state approved lateral arm system is being used and 4 ft. anchors are allowed at the sidewalk locations. I understand 5 ft. anchors are required at all centerline locations where the torque test reading is 275 or less and where the mobile home manufacturer may require anchors with 4000 lb. holding capacity.

Installer's Initials

ALL TESTS MUST BE PERFORMED BY A LICENSED INSTALLER

Installer Name

Ernest S Johnson

Date Tested

Assumed Oliver 11/01/05
495 foot together

Electrical

Connect electrical connections between multi-wide units, but not to the main power source. This includes the bonding wire between multi-wide units. Pg.

Plumbing

Connect all sewer drains to an existing sewer tap or septic tank. Pg.

Connect all potable water supply piping to an existing water meter, water tap, or other independent water supply systems. Pg.

Site Preparation

Debris and organic material removed ☒ Pad ☒ Other ☐

Water drainage: Natural Swale

Existing multi-wide unit

Floor: Type Fastener: 1/4x3 Length: 64 Spacing: 20
Walls: Type Fastener: 1/4x3 Length: 64 Spacing: 10
Roof: Type Fastener: 1/4x3 Length: 64 Spacing: 20

For used homes a 6" x 10" x 1/4" galvanized metal strip will be delivered over the peak of the roof and fastened with galv. roofing nails at 2' on center on both sides of the centerline.

General Installation Requirements

I understand a properly installed anchor is a requirement of all new and used homes and that contamination, mold, mildew and buckled marriage walls are a result of a poorly fastened or no anchor being installed. I understand a strip of tape will not serve as a gasket.

Installer's Initials

Type gasket

factory ok fill

Installed: Between Floors ☒
Between Walls ☒
Bottom of Ridgebeam ☒

Weatherproofing


The bottomboard will be required and/or lapped. Yes ☒
Sliding on units is installed to ensure proper ventilation. Yes ☒
Fireplace chimney installed so as not to allow intrusion of rain water. Yes ☒

Mechanicals

Shutting to be installed. Yes ☒ No ☒
Dryer vent installed outside of skirting. Yes ☒ No ☒
Range hood vent installed outside of skirting. Yes ☒ No ☒
Drain lines supported at 4 foot intervals. Yes ☒ No ☒
Electrical crossovers protected. Yes ☒ No ☒
Other: ☐

Installer verifies all information given with this permit worksheet is accurate and true based on the

Installer Signature Ernest S Johnson Date _____
All information on this worksheet must be filled out completely to be accepted.



NOTE: DO NOT ENCLOSE PORCH AREA.
SKIKING TO BE RUN ALONG THE DASHED LINE.
DO NOT COVER THE GROUND WITH PLASTIC
IN PORCH AREA.

HOARES, INC.

Footnote

part of the

Case

100

030 FT.

License Number: IH / 1025249 / 1 Name: ERNEST SCOTT JOHNSON

Order #: 6039	Label #: 106098	Manufacturer:	Year Model:	Length & Width:	Type Longitudinal System:	Type Lateral Arm System:	New Home:	Used Home:	Data Plate Wind Zone:	Permit #:
Homeowner:	Address:	City/State/Zip:	Phone #:	Date Installed:	Installed Wind Zone:	Note:				
Single	Double	Triple	HUD Label #:	Soil Bearing / PSF:	Torque Probe / In-lbs:					
(Check Size of Home)										

STATE OF FLORIDA
INSTALLATION CERTIFICATION LABEL

106098

LABEL #

ERNEST SCOTT JOHNSON

NAME

IH / 1025249 / 1

6039

ORDER #

CERTIFIES THAT THE INSTALLATION OF THIS MOBILE HOME IS
IN ACCORDANCE WITH FLORIDA STATUTES 320.8249, 320.8325
AND RULES OF THE HIGHWAY SAFETY AND MOTOR VEHICLES

INSTRUCTIONS

PLEASE WRITE DATE OF
INSTALLATION AND AFFIX
LABEL NEXT TO HUD LABEL.
USE PERMANENT INK PEN
OR MARKER ONLY.
COMPLETE INFORMATION
ABOVE AND KEEP ON FILE
FOR A MINIMUM OF 2 YEARS.
YOU ARE REQUIRED TO
PROVIDE COPIES WHEN
REQUESTED.
