

RESIDENTIAL ENERGY CONSERVATION CODE DOCUMENTATION CHECKLIST

Florida Department of Business and Professional Regulation Simulated Performance Alternative (Performance) Method

Applications for compliance with the 2022 Florida Building Code, Energy Conservation via the Residential Simulated Performance Alternative shall include:

- ☐ *This checklist*
- ☐ *Form R405-2022 report*
- ☐ *Input summary checklist that can be used for field verification (usually four pages/may be greater)*
- ☐ *Energy Performance Level (EPL) Display Card (one page)*
- ☐ *HVAC system sizing and selection based on ACCA Manual S or per exceptions provided in Section R403.7*
- ☐ *Mandatory Requirements (five pages)*

Required prior to CO:

- ☐ *Air Barrier and Insulation Inspection Component Criteria checklist (Table R402.4.1.1 - one page)*
- ☐ *A completed 2022 Envelope Leakage Test Report (usually one page); exception in R402.4 allows dwelling units of R-2 Occupancies and multiple attached single family dwellings to comply with Section C402.5*
- ☐ *If Form R405 duct leakage type indicates anything other than "default leakage", then a completed 2020 Duct Leakage Test Report - Performance Method (usually one page)*

FLORIDA ENERGY EFFICIENCY CODE FOR BUILDING CONSTRUCTION

Florida Department of Business and Professional Regulation - Residential Performance Method

Project Name: BUTLER RESIDENCE Street: City, State, Zip: , FL, Owner: Design Location: FL, Gainesville	Builder Name: Permit Office: Columbia Permit Number: Jurisdiction: County: Columbia(Florida Climate Zone 2)
--	---

1. New construction or existing New (From Plans) 2. Single family or multiple family Detached 3. Number of units, if multiple family 1 4. Number of Bedrooms 3 5. Is this a worst case? No 6. Conditioned floor area above grade (ft²) 2255 Conditioned floor area below grade (ft²) 0 7. Windows(220.5 sqft.) Description Area a. U-Factor: Dbl, U=0.55 168.50 ft² SHGC: SHGC=0.25 b. U-Factor: Dbl, U=0.40 32.00 ft² SHGC: SHGC=0.25 c. U-Factor: Dbl, U=0.40 20.00 ft² SHGC: SHGC=0.25 Area Weighted Average Overhang Depth: 2.803 ft Area Weighted Average SHGC: 0.250 8. Skylights Description Area U-Factor:(AVG) N/A N/A ft² SHGC(AVG): N/A 9. Floor Types Insulation Area a. Slab-On-Grade Edge Insulation R= 1.0 2255.00 ft² b. N/A R= ft² c. N/A R= ft²	10. Wall Types(2486.7 sqft.) Insulation Area a. Frame - Wood, Exterior R=19.0 2075.00 ft² b. Frame - Wood, Exterior R=13.0 411.67 ft² c. N/A d. N/A 11. Ceiling Types(2255.0 sqft.) Insulation Area a. Flat ceiling under att (Vented) R=38.0 2255.00 ft² b. N/A c. N/A 12. Roof(Comp. Shingles, Vented) Deck R=0.0 2710 ft² 13. Ducts, location & insulation level R ft² a. Sup: Attic, Ret: Main, AH: Main 6 128 b. c. 14. Cooling Systems kBtu/hr Efficiency a. Central Unit 23.1 SEER:16.00 15. Heating Systems kBtu/hr Efficiency a. Electric Heat Pump 32.9 HSPF:8.00 16. Hot Water Systems a. Electric Cap: 50 gallons EF: 0.920 b. Conservation features None 17. Credits CF, Pstat
--	---

Glass/Floor Area: 0.098

Total Proposed Modified Loads: 48.73

Total Baseline Loads: 60.99

PASS

I hereby certify that the plans and specifications covered by this calculation are in compliance with the Florida Energy Code.

PREPARED BY: David Royal

DATE: SEPT. 12 2023

I hereby certify that this building, as designed, is in compliance with the Florida Energy Code.

OWNER/AGENT: _____

DATE: _____

Review of the plans and specifications covered by this calculation indicates compliance with the Florida Energy Code. Before construction is completed this building will be inspected for compliance with Section 553.908 Florida Statutes.



BUILDING OFFICIAL: _____

DATE: _____

- Compliance requires certification by the air handler unit manufacturer that the air handler enclosure qualifies as certified factory-sealed in accordance with R403.3.2.1.
- Compliance with a proposed duct leakage Qn requires a PERFORMANCE Duct Leakage Test Report confirming duct leakage to outdoors, tested in accordance with ANSI/RESNET/ICC 380, is not greater than 0.030 Qn for whole house.
- Compliance requires an Air Barrier and Insulation Inspection Checklist in accordance with R402.4.1.1 and this project requires a PERFORMANCE envelope leakage test report with envelope leakage no greater than 6.20 ACH50 (R402.4.1.2).

Page 2

INPUT SUMMARY CHECKLIST REPORT

WALLS															(Total Exposed Area = 2487 sq.ft.)				
✓ #	Ornt	Adjacent To	Wall Type	Space	Cavity R-Value	Width Ft	In	Height Ft	In	Area sq.ft.	U-Factor	Sheath R-Value	Frm. Frac.	Solar Absor.	Below Grade				
___ 1	S	Exterior	Frame - Wood	Main	19.0	10.0	4	10.0	0	103.3	0.061		0.23	0.75	0 %				
___ 2	E	Exterior	Frame - Wood	Main	19.0	5.0	0	10.0	0	50.0	0.061		0.23	0.75	0 %				
___ 3	S	Exterior	Frame - Wood	Main	19.0	11.0	0	10.0	0	110.0	0.061		0.23	0.75	0 %				
___ 4	W	Exterior	Frame - Wood	Main	19.0	5.0	0	10.0	0	50.0	0.061		0.23	0.75	0 %				
___ 5	S	Exterior	Frame - Wood	Main	19.0	20.0	8	10.0	0	206.7	0.061		0.23	0.75	0 %				
___ 6	E	Exterior	Frame - Wood	Main	19.0	5.0	0	10.0	0	50.0	0.061		0.23	0.75	0 %				
___ 7	S	Exterior	Frame - Wood	Main	19.0	10.0	2	10.0	0	101.7	0.061		0.23	0.75	0 %				
___ 8	E	Exterior	Frame - Wood	Main	19.0	3.0	2	10.0	0	31.7	0.061		0.23	0.75	0 %				
___ 9	S	Exterior	Frame - Wood	Main	19.0	14.0	4	10.0	0	143.3	0.061		0.23	0.75	0 %				
___ 10	W	Exterior	Frame - Wood	Main	19.0	34.0	6	10.0	0	345.0	0.061		0.23	0.75	0 %				
___ 11	N	Exterior	Frame - Wood	Main	19.0	24.0	0	10.0	0	240.0	0.061		0.23	0.75	0 %				
___ 12	W	Exterior	Frame - Wood	Main	19.0	2.0	6	10.0	0	25.0	0.061		0.23	0.75	0 %				
___ 13	N	Exterior	Frame - Wood	Main	19.0	14.0	2	10.0	0	141.7	0.061		0.23	0.75	0 %				
___ 14	E	Exterior	Frame - Wood	Main	19.0	2.0	6	10.0	0	25.0	0.061		0.23	0.75	0 %				
___ 15	N	Exterior	Frame - Wood	Main	19.0	17.0	4	10.0	0	173.3	0.061		0.23	0.75	0 %				
___ 16	W	Exterior	Frame - Wood	Main	19.0	14.0	10	10.0	0	148.3	0.061		0.23	0.75	0 %				
___ 17	N	Exterior	Frame - Wood	Main	19.0	13.0	0	10.0	0	130.0	0.061		0.23	0.75	0 %				
___ 18	E	Exterior	Frame - Wood	Main	13.0	41.0	2	10.0	0	411.7	0.084		0.23	0.75	0 %				

DOORS										(Total Exposed Area = 136 sq.ft.)			
✓ #	Ornt	Adjacent To	Door Type	Space	Storms	U-Value	Width Ft	In	Height Ft	In	Area		
___ 1	S(Front)		Insulated	Main	None	0.40	3.00	0	6.00	8	20.0ft²		
___ 2	N		Insulated	Main	None	0.46	3.00	0	6.00	8	20.0ft²		
___ 3	N		Insulated	Main	None	0.46	12.00	0	8.00	0	96.0ft²		

WINDOWS															(Total Exposed Area = 221 sq.ft.)			
✓ #	Ornt	Wall ID	Frame	Panes	NFRC U-Factor	SHGC	Imp	Storm	Total Area (ft²)	Same Units	Width (ft)	Height (ft)	--Overhang-- Depth (ft)	Sep. (ft)	Interior Shade	Screen		
___ 1	S	1	Vinyl	Low-E Double	Y	0.40	0.25	N	N	20.0	2	1.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 2	S	1	Vinyl	Double (Tinted)	Y	0.40	0.25	N	N	16.0	1	2.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 3	S	3	Vinyl	Double (Tinted)	Y	0.40	0.25	N	N	16.0	1	2.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 4	S	5	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	36.0	2	3.00	6.00	6.3	2.0	Drapes/blinds	None	
___ 5	S	7	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	16.0	1	2.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 6	S	9	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	16.0	1	2.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 7	S	9	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	20.0	2	1.67	6.00	1.3	3.0	Drapes/blinds	None	
___ 8	W	10	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	16.0	1	4.00	4.00	1.3	2.0	Drapes/blinds	None	
___ 9	N	13	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	16.0	1	4.00	4.00	10.3	2.0	Drapes/blinds	None	
___ 10	N	17	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	36.0	2	3.00	6.00	1.3	3.0	Drapes/blinds	None	
___ 11	E	18	Vinyl	Double (Tinted)	Y	0.55	0.25	N	N	12.5	1	2.50	5.00	1.3	2.0	Drapes/blinds	None	

INFILTRATION										
✓ #	Scope	Method	SLA	CFM50	ELA	EqLA	ACH	ACH50	Space(s)	Infiltration Test Volume
___ 1	Wholehouse	Proposed ACH(50)	0.00039	2330	127.84	240.01	0.1328	6.2	All	22550 cu ft

INPUT SUMMARY CHECKLIST REPORT

MASS													
✓ #	Mass Type	Area	Thickness	Furniture Fraction	Space								
___ 1	Default(8 lbs/sq.ft.)	0 ft²	0 ft	0.30	Main								

HEATING SYSTEM											
✓ #	System Type	Subtype/Speed	AHRI #	Efficiency	Capacity kBtu/hr	---Geothermal Entry	HeatPump--- Power	Volts	Current	Ducts	Block
___ 1	Electric Heat Pump	Single/Single		HSPF: 8.00	32.9		0.00	0.00	0.00	sys#1	1

COOLING SYSTEM									
✓ #	System Type	Subtype/Speed	AHRI #	Efficiency	Capacity kBtu/hr	Air Flow cfm	SHR	Duct	Block
___ 1	Central Unit	Single/Single		SEER:16.0	23.1	720	0.70	sys#1	1

HOT WATER SYSTEM										
✓ #	System Type	Subtype	Location	EF(UEF)	Cap	Use	SetPnt	Fixture Flow	Pipe Ins.	Pipe length
___ 1	Electric	None	Exterior	0.92 (0.92)	50.00 gal	40 gal	120 deg	Standard	=>R-3	50
	Recirculation System	Recirc Control Type	Loop length	Branch length	Pump power	DWHR	Facilities Connected	Equal Flow	DWHR Eff	Other Credits
___ 1	No		NA	NA	NA	No	NA	NA	NA	None

DUCTS													
✓ Duct #	Location	-----Supply----- R-Value	Area	-----Return----- R-Value	Area	Leakage Type	Air Handler	CFM 25 TOT	CFM 25 OUT	QN	RLF	HVAC # Heat	Cool
___ 1	Attic	6.0	128 ft²	Main	6.0	32 ft²	Prop. Leak Free	Main	---	---	0.03	0.60	1 1

MECHANICAL VENTILATION													
✓ Type	Supply CFM	Exhaust CFM	HRV	Fan	Run Time	Heating System	Cooling System						
___ Fans/ERV	100.0	120.0	0.0	400.0 W	10 %	1 - Electric Heat Pump	1 - Central Unit						

TEMPERATURES													
Programable Thermostat: Y				Ceiling Fans: Y									
Cooling	[] Jan	[] Feb	[] Mar	[] Apr	[] May	[X] Jun	[X] Jul	[X] Aug	[X] Sep	[] Oct	[] Nov	[] Dec	
Heating	[X] Jan	[X] Feb	[X] Mar	[] Apr	[] May	[] Jun	[] Jul	[] Aug	[] Sep	[] Oct	[X] Nov	[X] Dec	
Venting	[] Jan	[] Feb	[X] Mar	[X] Apr	[] May	[] Jun	[] Jul	[] Aug	[] Sep	[X] Oct	[X] Nov	[] Dec	
✓ Thermostat Schedule: HERS 2006 Reference	Hours												
Schedule Type	1	2	3	4	5	6	7	8	9	10	11	12	
___ Cooling (WD)	AM PM	78 80	78 80	78 78	78 78	78 78	78 78	78 78	78 78	80 78	80 78	80 78	80 78
___ Cooling (WEH)	AM PM	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78	78 78

INPUT SUMMARY CHECKLIST REPORT

TEMPERATURES(Continued)

___ Heating (WD)	AM	66	66	66	66	66	68	68	68	68	68	68	68
	PM	68	68	68	68	68	68	68	68	68	68	66	66
___ Heating (WEH)	AM	66	66	66	66	66	68	68	68	68	68	68	68
	PM	68	68	68	68	68	68	68	68	68	68	66	66

ENERGY PERFORMANCE LEVEL (EPL) DISPLAY CARD

ESTIMATED ENERGY PERFORMANCE INDEX* = 80

The lower the EnergyPerformance Index, the more efficient the home.

„FL,

1. New construction or existing	New (From Plans)	10. Wall Types(2486.7 sqft.)	Insulation	Area
2. Single family or multiple family	Detached	a. Frame - Wood, Exterior	R=19.0	2075.00 ft ²
3. Number of units, if multiple family	1	b. Frame - Wood, Exterior	R=13.0	411.67 ft ²
4. Number of Bedrooms	3	c. N/A		
5. Is this a worst case?	No	d. N/A		
6. Conditioned floor area above grade (ft ²)	2255	11. Ceiling Types(2255.0 sqft.)	Insulation	Area
Conditioned floor area below grade (ft ²)	0	a. Flat ceiling under att (Vented)	R=38.0	2255.00 ft ²
7. Windows**	Description	b. N/A		
a. U-Factor:	Dbl, U=0.55	c. N/A		
SHGC:	SHGC=0.25	12. Roof(Comp. Shingles, Vented) Deck	R=0.0	2710 ft ²
b. U-Factor:	Dbl, U=0.40	13. Ducts, location & insulation level	R	ft ²
SHGC:	SHGC=0.25	a. Sup: Attic, Ret: Main, AH: Main	6	128
c. U-Factor:	Dbl, U=0.40	b.		
SHGC:	SHGC=0.25	c.		
Area Weighted Average Overhang Depth:	2.803 ft	14. Cooling Systems	kBtu/hr	Efficiency
Area Weighted Average SHGC:	0.250	a. Central Unit	23.1	SEER:16.00
8. Skylights	Description	15. Heating Systems	kBtu/hr	Efficiency
U-Factor:(AVG)	N/A	a. Electric Heat Pump	32.9	HSPF:8.00
SHGC(AVG):	N/A			
9. Floor Types	Insulation	16. Hot Water Systems		
a. Slab-On-Grade Edge Insulation	R= 1.0	a. Electric	Cap: 50 gallons	
b. N/A	R=		EF: 0.920	
c. N/A	R=	b. Conservation features		
		17. Credits	None	
			CF, Pstat	

I certify that this home has complied with the Florida Energy Efficiency Code for Building Construction through the above energy saving features which will be installed (or exceeded) in this home before final inspection. Otherwise, a new EPL Display Card will be completed based on installed Code compliant features.

Builder Signature: _____ Date: _____

Address of New Home: _____ City/FL Zip: „FL,



*Note: This is not a Building Energy Rating. If your Index is below 70, your home may qualify for energy efficient mortgage (EEM) incentives if you obtain a Florida Energy Rating. For information about the Florida Building Code, Energy Conservation, contact the Florida Building Commission's support staff.

**Label required by Section R303.1.3 of the Florida Building Code, Energy Conservation, if not DEFAULT.

Florida Building Code, Energy Conservation, 7th Edition (2020)

Mandatory Requirements for Residential Performance, Prescriptive and ERI Methods

ADDRESS:

, FL

Permit Number:

MANDATORY REQUIREMENTS - See individual code sections for full details.

SECTION R401 GENERAL

- ☐ **R401.3 Energy Performance Level (EPL) display card - (Mandatory).** The building official shall require that an energy performance level (EPL) display card be completed and certified by the builder to be accurate and correct before final approval of the building for occupancy. Florida law (Section 553.9085, Florida Statutes) requires the EPL display card to be included as an addendum to each sales contract for both presold and nonpresold residential buildings. The EPL display card contains information indicating the energy performance level and efficiencies of components installed in a dwelling unit. The building official shall verify that the EPL display card completed and signed by the builder accurately reflects the plans and specifications submitted to demonstrate code compliance for the building. A copy of the EPL display card can be found in Appendix RD.

SECTION R402 BUILDING THERMAL ENVELOPE

- ☐ **R402.4 Air leakage (Mandatory).** The building thermal envelope shall be constructed to limit air leakage in accordance with the requirements of Sections R402.4.1 through R402.4.5.
- Exception:** Dwelling units of R-2 Occupancies and multiple attached single family dwellings shall be permitted to comply with Section C402.5.
- ☐ **R402.4.1 Building thermal envelope.** The building thermal envelope shall comply with Sections R402.4.1.1 and R402.4.1.2. The sealing methods between dissimilar materials shall allow for differential expansion and contraction.
- ☐ **R402.4.1.1 Installation.** The components of the building thermal envelope as listed in Table R402.4.1.1 shall be installed in accordance with the manufacturer's instructions and the criteria listed in Table R402.4.1.1, as applicable to the method of construction. Where required by the code official, an approved third party shall inspect all components and verify compliance.
- ☐ **R402.4.1.2 Testing.** The building or dwelling unit shall be tested and verified as having an air leakage rate not exceeding seven air changes per hour in Climate Zones 1 and 2, and three air changes per hour in Climate Zones 3 through 8. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.
- Exception:** Testing is not required for additions, alterations, renovations, or repairs, of the building thermal envelope of existing buildings in which the new construction is less than 85 percent of the building thermal envelope.
- During testing:
1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures.
 2. Dampers including exhaust, intake, makeup air, backdraft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures.
 3. Interior doors, if installed at the time of the test, shall be open.
 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed.
 5. Heating and cooling systems, if installed at the time of the test, shall be turned off.
 6. Supply and return registers, if installed at the time of the test, shall be fully open.
- ☐ **R402.4.2 Fireplaces.** New wood-burning fireplaces shall have tight-fitting flue dampers or doors, and outdoor combustion air. Where using tight-fitting doors on factory-built fireplaces listed and labeled in accordance with UL 127, the doors shall be tested and listed for the fireplace. Where using tight-fitting doors on masonry fireplaces, the doors shall be listed and labeled in accordance with UL 907.
- ☐ **R402.4.3 Fenestration air leakage.** Windows, skylights and sliding glass doors shall have an air infiltration rate of no more than 0.3 cfm per square foot (1.5 L/s/m²), and swinging doors no more than 0.5 cfm per square foot (2.6 L/s/m²), when tested according to NFRC 400 or AAMA/WDMA/CSA 101/I.S.2/A440 by an accredited, independent laboratory and listed and labeled by the manufacturer.
- Exception:** Site-built windows, skylights and doors.
- ☐ **R402.4.4 Rooms containing fuel - burning appliances.** In Climate Zones 3 through 8, where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening shall be located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms shall be sealed and insulated in accordance with the envelope requirements of Table R402.1.2, where the walls, floors and ceilings shall meet not less than the basement wall R-value requirement. The door into the room shall be fully gasketed and any water lines and ducts in the room insulated in accordance with Section R403. The combustion air duct shall be insulated where it passes through conditioned space to a minimum of R-8.
- Exceptions:**
1. Direct vent appliances with both intake and exhaust pipes installed continuous to the outside.
 2. Fireplaces and stoves complying with Section R402.4.2 and Section R1006 of the Florida Building Code, Residential.

MANDATORY REQUIREMENTS (Continued)

- ☐ **R402.4.5 Recessed lighting.** Recessed luminaires installed in the building thermal envelope shall be sealed to limit air leakage between conditioned and unconditioned spaces. All recessed luminaires shall be IC-rated and labeled as having an air leakage rate not more than 2.0 cfm (0.944 L/s) when tested in accordance with ASTM E283 at a 1.57 psf (75 Pa) pressure differential. All recessed luminaires shall be sealed with a gasket or caulk between the housing and the interior wall or ceiling covering.

SECTION R403 SYSTEMS

R403.1 Controls

- ☐ **R403.1.1 Thermostat provision (Mandatory).** At least one thermostat shall be provided for each separate heating and cooling system
- ☐ **R403.1.3 Heat pump supplementary heat (Mandatory).** Heat pumps having supplementary electric-resistance heat shall have controls that, except during defrost, prevent supplemental heat operation when the heat pump compressor can meet the heating load.

- ☐ **R403.3.2 Sealing (Mandatory).** All ducts, air handlers, filter boxes and building cavities that form the primary air containment passageways for air distribution systems shall be considered ducts or plenum chambers, shall be constructed and sealed in accordance with Section C403.2.9.2 of the Commercial Provisions of this code and shall be shown to meet duct tightness criteria below.

Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC 380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes, to be "substantially leak free" in accordance with Section R403.3.3.

- ☐ **R403.3.2.1 Sealed air handler.** Air handlers shall have a manufacturer's designation for an air leakage of no more than 2 percent of the design airflow rate when tested in accordance with ASHRAE 193.
- ☐ **R403.3.3 Duct testing (Mandatory).** Ducts shall be pressure tested to determine air leakage by one of the following methods:
 1. Rough-in test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the system, including the manufacturer's air handler enclosure if installed at the time of the test. All registers shall be taped or otherwise sealed during the test.
 2. Postconstruction test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the entire system, including the manufacturer's air handler enclosure. Registers shall be taped or otherwise sealed during the test.**Exceptions;**
 1. A duct air leakage test shall not be required where the ducts and air handlers are located entirely within the building thermal envelope.
 2. Duct testing is not mandatory for buildings complying by Section 405 of this code. Duct leakage testing is required for Section R405 compliance where credit is taken for leakage, and a duct air leakage Q_n to the outside of less than 0.080 (where Q_n = duct leakage to the outside in cfm per 100 square feet of conditioned floor area tested at 25 Pascals) is indicated in the compliance report for the proposed design.A written report of the results of the test shall be signed by the party conducting the test and provided to the code official

- ☐ **R403.3.5 Building cavities (Mandatory).** Building framing cavities shall not be used as ducts or plenums

- ☐ **R403.4 Mechanical system piping insulation (Mandatory).** Mechanical system piping capable of carrying fluids above 105°F (41°C) or below 55°F (13°C) shall be insulated to a minimum of R-3.

- ☐ **R403.4.1 Protection of piping insulation.** Piping insulation exposed to weather shall be protected from damage, including that caused by sunlight, moisture, equipment maintenance and wind, and shall provide shielding from solar radiation that can cause degradation of the material. Adhesive tape shall not be permitted.

- ☐ **R403.5.1 Heated water circulation and temperature maintenance systems (Mandatory).** If heated water circulation systems are installed, they shall be in accordance with Section R403.5.1.1. Heat trace temperature maintenance systems shall be in accordance with Section R403.5.1.2. Automatic controls, temperature sensors and pumps shall be accessible. Manual controls shall be readily accessible.

- ☐ **R403.5.1.1 Circulation systems.** Heated water circulation systems shall be provided with a circulation pump. The system return pipe shall be a dedicated return pipe or a cold water supply pipe. Gravity and thermosiphon circulation systems shall be prohibited. Controls for circulating hot water system pumps shall start the pump based on the identification of a demand for hot water within the occupancy. The controls shall automatically turn off the pump when the water in the circulation loop is at the desired temperature and when there is no demand for hot water.

- ☐ **R403.5.1.2 Heat trace systems.** Electric heat trace systems shall comply with IEEE 515.1 or UL 515. Controls for such systems shall automatically adjust the energy input to the heat tracing to maintain the desired water temperature in the piping in accordance with the times when heated water is used in the occupancy.

MANDATORY REQUIREMENTS (Continued)

- ☐ **R403.5.5 Heat traps (Mandatory).** Storage water heaters not equipped with integral heat traps and having vertical pipe risers shall have heat traps installed on both the inlets and outlets. External heat traps shall consist of either a commercially available heat trap or a downward and upward bend of at least 3 ½ inches (89 mm) in the hot water distribution line and cold water line located as close as possible to the storage tank.
- ☐ **R403.5.6 Water heater efficiencies (Mandatory).**
- ☐ **R403.5.6.1.1 Automatic controls.** Service water-heating systems shall be equipped with automatic temperature controls capable of adjustment from the lowest to the highest acceptable temperature settings for the intended use. The minimum temperature setting range shall be from 100°F to 140°F (38°C to 60°C).
- ☐ **R403.5.6.1.2 Shut down.** A separate switch or a clearly marked circuit breaker shall be provided to permit the power supplied to electric service systems to be turned off. A separate valve shall be provided to permit the energy supplied to the main burner(s) of combustion types of service water-heating systems to be turned off.
- ☐ **R403.5.6.2 Water-heating equipment.** Water-heating equipment installed in residential units shall meet the minimum efficiencies of Table C404.2 in Chapter 4 of the Florida Building Code, Energy Conservation, Commercial Provisions, for the type of equipment installed. Equipment used to provide heating functions as part of a combination system shall satisfy all stated requirements for the appropriate water-heating category. Solar water heaters shall meet the criteria of Section R403.5.6.2.1.
- ☐ **R403.5.6.2.1 Solar water-heating systems.** Solar systems for domestic hot water production are rated by the annual solar energy factor of the system. The solar energy factor of a system shall be determined from the Florida Solar Energy Center Directory of Certified Solar Systems. Solar collectors shall be tested in accordance with ISO Standard 9806, Test Methods for Solar Collectors, and SRCC Standard TM-1, Solar Domestic Hot Water System and Component Test Protocol. Collectors in installed solar water-heating systems should meet the following criteria:
1. Be installed with a tilt angle between 10 degrees and 40 degrees of the horizontal; and
 2. Be installed at an orientation within 45 degrees of true south.
- ☐ **R403.6 Mechanical ventilation (Mandatory).** The building shall be provided with ventilation that meets the requirements of the Florida Building Code, Residential, or Florida Building Code, Mechanical, as applicable, or with other approved means of ventilation including: Natural, Infiltration or Mechanical means. Outdoor air intakes and exhausts shall have automatic or gravity dampers that close when the ventilation system is not operating.
- ☐ **R403.6.1 Whole-house mechanical ventilation system fan efficacy.** When installed to function as a whole-house mechanical ventilation system, fans shall meet the efficacy requirements of Table R403.6.1.
- Exception:** Where an air handler that is integral to tested and listed HVAC equipment is used to provide whole-house mechanical ventilation, the air handler shall be powered by an electronically commutated motor.
- ☐ **R403.6.2 Ventilation Air.** Residential buildings designed to be operated at a positive indoor pressure or for mechanical ventilation shall meet the following criteria:
1. The design air change per hour minimums for residential buildings in ASHRAE 62.2, Ventilation for Acceptable Indoor Air Quality, shall be the maximum rates allowed for residential applications.
 2. No ventilation or air-conditioning system make-up air shall be provided to conditioned space from attics, crawlspaces, attached enclosed garages or outdoor spaces adjacent to swimming pools or spas.
 3. If ventilation air is drawn from enclosed space(s), then the walls of the space(s) from which air is drawn shall be insulated to a minimum of R-11 and the ceiling shall be insulated to a minimum of R-19, space permitting, or R-10 otherwise.
- ☐ **R403.7 Heating and cooling equipment.**
- ☐ **R403.7.1 Equipment sizing (Mandatory).** Heating and cooling equipment shall be sized in accordance with ACCA Manual S based on the equipment loads calculated in accordance with ACCA Manual J or other approved heating and cooling calculation methodologies, based on building loads for the directional orientation of the building. The manufacturer and model number of the outdoor and indoor units (if split system) shall be submitted along with the sensible and total cooling capacities at the design conditions described in Section R302.1. This Code does not allow designer safety factors, provisions for future expansion or other factors that affect equipment sizing. System sizing calculations shall not include loads created by local intermittent mechanical ventilation such as standard kitchen and bathroom exhaust systems. New or replacement heating and cooling equipment shall have an efficiency rating equal to or greater than the minimum required by federal law for the geographic location where the equipment is installed.

MANDATORY REQUIREMENTS (Continued)

TABLE R403.6.1
WHOLE-HOUSE MECHANICAL VENTILATION SYSTEM FAN EFFICACY

FAN LOCATION	AIRFLOW RATE MINIMUM (CFM)	MINIMUM EFFICACY ^a (CFM/WATT)	AIRFLOW RATE MAXIMUM (CFM)
HRV or ERV	Any	1.2 cfm/watt	Any
Range hoods	Any	2.8 cfm/watt	Any
In-line fan	Any	2.8 cfm/watt	Any
Bathroom, utility room	10	1.4 cfm/watt	<90
Bathroom, utility room	90	2.8 cfm/watt	Any

For SI: 1 cfm = 28.3 L/min.

a. When tested in accordance with HVI Standard 916

- ☐ **R403.7.1.1 Cooling equipment capacity.** Cooling only equipment shall be selected so that its total capacity is not less than the calculated total load but not more than 1.15 times greater than the total load calculated according to the procedure selected in Section R403.7, or the closest available size provided by the manufacturer's product lines. The corresponding latent capacity of the equipment shall not be less than the calculated latent load.
- The published value for AHRI total capacity is a nominal, rating-test value and shall not be used for equipment sizing. Manufacturer's expanded performance data shall be used to select cooling-only equipment. This selection shall be based on the outdoor design dry-bulb temperature for the load calculation (or entering water temperature for water-source equipment), the blower CFM provided by the expanded performance data, the design value for entering wet-bulb temperature and the design value for entering dry-bulb temperature.

Design values for entering wet-bulb and dry-bulb temperatures shall be for the indoor dry bulb and relative humidity used for the load calculation and shall be adjusted for return side gains if the return duct(s) is installed in an unconditioned space.

Exceptions:

1. Attached single- and multiple-family residential equipment sizing may be selected so that its cooling capacity is less than the calculated total sensible load but not less than 80 percent of that load.
2. When signed and sealed by a Florida-registered engineer, in attached single- and multiple-family units, the capacity of equipment may be sized in accordance with good design practice.

R403.7.1.2 Heating equipment capacity.

- ☐ **R403.7.1.2.1 Heat pumps.** Heat pump sizing shall be based on the cooling requirements as calculated according to Section R403.7.1.1, and the heat pump total cooling capacity shall not be more than 1.15 times greater than the design cooling load even if the design heating load is 1.15 times greater than the design cooling load.
- ☐ **R403.7.1.2.2 Electric resistance furnaces.** Electric resistance furnaces shall be sized within 4 kW of the design requirements calculated according to the procedure selected in Section R403.7.1.
- ☐ **R403.7.1.2.3 Fossil fuel heating equipment.** The capacity of fossil fuel heating equipment with natural draft atmospheric burners shall not be less than the design load calculated in accordance with Section R403.7.1.
- ☐ **R403.7.1.3 Extra capacity required for special occasions.** Residences requiring excess cooling or heating equipment capacity on an intermittent basis, such as anticipated additional loads caused by major entertainment events, shall have equipment sized or controlled to prevent continuous space cooling or heating within that space by one or more of the following options:
1. A separate cooling or heating system is utilized to provide cooling or heating to the major entertainment areas.
 2. A variable capacity system sized for optimum performance during base load periods is utilized.
- ☐ **R403.8 Systems serving multiple dwelling units (Mandatory).** Systems serving multiple dwelling units shall comply with Sections C403 and C404 of the Florida Building Code, Energy Conservation—Commercial Provisions in lieu of Section R403.
- ☐ **R403.9 Snow melt and ice system controls (Mandatory).** Snow- and ice-melting systems, supplied through energy service to the building, shall include automatic controls capable of shutting off the system when the pavement temperature is above 50°F (10°C), and no precipitation is falling and an automatic or manual control that will allow shutoff when the outdoor temperature is above 40°F (4.8°C).
- ☐ **403.10 Pools and permanent spa energy consumption (Mandatory).** The energy consumption of pools and permanent spas shall be in accordance with Sections R403.10.1 through R403.10.5.
- ☐ **R403.10.1 Heaters.** The electric power to heaters shall be controlled by a readily accessible on-off switch that is an integral part of the heater mounted on the exterior of the heater, or external to and within 3 feet (914 mm) of the heater. Operation of such switch shall not change the setting of the heater thermostat. Such switches shall be in addition to a circuit breaker for the power to the heater.
- Gas-fired heaters shall not be equipped with continuously burning ignition pilots.

MANDATORY REQUIREMENTS (Continued)

- ☐ **R403.10.2 Time switches.** Time switches or other control methods that can automatically turn off and on according to a preset schedule shall be installed for heaters and pump motors. Heaters and pump motors that have built-in time switches shall be in compliance with this section.

Exceptions:

1. Where public health standards require 24-hour pump operation.
2. Pumps that operate solar- and waste-heat-recovery pool heating systems
3. Where pumps are powered exclusively from on-site renewable generation.

- ☐ **R403.10.3 Covers.** Outdoor heated swimming pools and outdoor permanent spas shall be equipped with a vapor-retardant cover on or at the water surface or a liquid cover or other means proven to reduce heat loss.

Exception: Where more than 70 percent of the energy for heating, computed over an operation season, is from site-recovered energy, such as from a heat pump or solar energy source, covers or other vapor-retardant means shall not be required

- ☐ **R403.10.4 Gas- and oil-fired pool and spa heaters.** All gas- and oil-fired pool and spa heaters shall have a minimum thermal efficiency of 82 percent for heaters manufactured on or after April 16, 2013, when tested in accordance with ANSI Z 21.56. Pool heaters fired by natural or LP gas shall not have continuously burning pilot lights.
- ☐ **R403.10.5 Heat pump pool heaters.** Heat pump pool heaters shall have a minimum COP of 4.0 when tested in accordance with AHRI 1160, Table 2, Standard Rating Conditions-Low Air Temperature. A test report from an independent laboratory is required to verify procedure compliance. Geothermal swimming pool heat pumps are not required to meet this standard.
- ☐ **R403.11 Portable spas (Mandatory).** The energy consumption of electric-powered portable spas shall be controlled by the requirements of APSP-14
- ☐ **R403.13 Dehumidifiers (Mandatory).** If installed, a dehumidifier shall conform to the following requirements:
1. The minimum rated efficiency of the dehumidifier shall be greater than 1.7 liters/ kWh if the total dehumidifier capacity for the house is less than 75 pints/day and greater than 2.38 liters/kWh if the total dehumidifier capacity for the house is greater than or equal to 75 pints/day.
 2. The dehumidifier shall be controlled by a sensor that is installed in a location where it is exposed to mixed house air.
 3. Any dehumidifier unit located in unconditioned space that treats air from conditioned space shall be insulated to a minimum of R-2.
 4. Condensate disposal shall be in accordance with Section M1411.3.1 of the Florida Building Code, Residential.
- ☐ **R403.13.1 Ducted dehumidifiers.** Ducted dehumidifiers shall, in addition to conforming to the requirements of Section R403.13, conform to the following requirements:
1. If a ducted dehumidifier is configured with return and supply ducts both connected into the supply side of the cooling system, a backdraft damper shall be installed in the supply air duct between the dehumidifier inlet and outlet duct.
 2. If a ducted dehumidifier is configured with only its supply duct connected into the supply side of the central heating and cooling system, a backdraft damper shall be installed in the dehumidifier supply duct between the dehumidifier and central supply duct.
 3. A ducted dehumidifier shall not be ducted to or from a central ducted cooling system on the return duct side upstream from the central cooling evaporator coil.
 4. Ductwork associated with a dehumidifier located in unconditioned space shall be insulated to a minimum of R-6.

SECTION R404 ELECTRICAL POWER AND LIGHTING SYSTEMS

- ☐ **R404.1 Lighting equipment (Mandatory).** Not less than 90 percent of the lamps in permanently installed luminaires shall have an efficacy of at least 45 lumens-per-watt or shall utilize lamps with an efficacy of not less than 65 lumens-per-watt.

R404.1.1 Lighting equipment (Mandatory). uel gas lighting systems shall not have continuously burning pilot lights.

2020 - AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA

TABLE 402.4.1.1

AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA^a

Project Name: BUTLER RESIDENCE		Builder Name:	
Street:		Permit Office: Columbia	
City, State, Zip: , FL,		Permit Number:	
Owner:		Jurisdiction:	
Design Location: FL, Gainesville		County: Columbia(Florida Climate Zone 2)	
		CHECK	
COMPONENT	AIR BARRIER CRITERIA	INSULATION INSTALLATION CRITERIA	
General requirements	A continuous air barrier shall be installed in the building envelope. The exterior thermal envelope contains a continuous air barrier. Breaks or joints in the air barrier shall be sealed.	Air-permeable insulation shall not be used as a sealing material.	
Ceiling/attic	The air barrier in any dropped ceiling/soffit shall be aligned with the insulation and any gaps in the air barrier shall be sealed. Access openings, drop down stairs or knee wall doors to unconditioned attic spaces shall be sealed.	The insulation in any dropped ceiling/soffit shall be aligned with the air barrier.	
Walls	The junction of the foundation and sill plate shall be sealed. The junction of the top plate and the top of exterior walls shall be sealed. Knee walls shall be sealed.	Cavities within corners and headers of frame walls shall be insulated by completely filling the cavity with a material having a thermal resistance of R-3 per inch minimum. Exterior thermal envelope insulation for framed walls shall be installed in substantial contact and continuous alignment with the air barrier.	
Windows, skylights and doors	The space between window/door jambs and framing, and skylights and framing shall be sealed.		
Rim joists	Rim joists shall include the air barrier.	Rim joists shall be insulated.	
Floors (including above-garage and cantilevered floors)	The air barrier shall be installed at any exposed edge of insulation.	Floor framing cavity insulation shall be installed to maintain permanent contact with the underside of subfloor decking, or floor framing cavity insulation shall be permitted to be in contact with the top side of sheathing, or continuous insulation installed on the underside of floor framing and extends from the bottom to the top of all perimeter floor framing members.	
Crawl space walls	Exposed earth in unvented crawl spaces shall be covered with a Class I vapor retarder with overlapping joints taped.	Where provided instead of floor insulation, insulation shall be permanently attached to the crawlspace walls.	
Shafts, penetrations	Duct shafts, utility penetrations, and flue shafts opening to exterior or unconditioned space shall be sealed.		
Narrow cavities		Batts in narrow cavities shall be cut to fit, or narrow cavities shall be filled by insulation that on installation readily conforms to the available cavity spaces.	
Garage separation	Air sealing shall be provided between the garage and conditioned spaces.		
Recessed lighting	Recessed light fixtures installed in the building thermal envelope shall be sealed to the finished surface.	Recessed light fixtures installed in the building thermal envelope shall be air tight and IC rated.	
Plumbing and wiring		Batt insulation shall be cut neatly to fit around wiring and plumbing in exterior walls, or insulation that on installation readily conforms to available space shall extend behind piping and wiring.	
Shower/tub on exterior wall	The air barrier installed at exterior walls adjacent to showers and tubs shall separate them from the showers and tubs.	Exterior walls adjacent to showers and tubs shall be insulated.	
Electrical/phone box on exterior walls	The air barrier shall be installed behind electrical or communication boxes or air-sealed boxes shall be installed.		
HVAC register boots	HVAC supply and return register boots that penetrate building thermal envelope shall be sealed to the sub-floor, wall covering or ceiling penetrated by the boot.		
Concealed sprinklers	When required to be sealed, concealed fire sprinklers shall only be sealed in a manner that is recommended by the manufacturer. Caulking or other adhesive sealants shall not be used to fill voids between fire sprinkler cover plates and walls or ceilings.		

a. In addition, inspection of log walls shall be in accordance with the provisions of ICC-400.

Envelope Leakage Test Report (Blower Door Test)
Residential Prescriptive, Performance or ERI Method Compliance
2020 Florida Building Code, Energy Conservation, 7th Edition

Jurisdiction:	Permit #:	
Job Information		
Builder:	Community:	Lot: NA
Address:		
City:	State: FL	Zip:
Air Leakage Test Results <i>Passing results must meet either the Performance, Prescriptive, or ERI Method</i>		
☐ PRESCRIPTIVE METHOD-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding 7 air changes per hour at a pressure of 0.2 inch w.g. (50 Pascals) in Climate Zones 1 and 2. ☒ PERFORMANCE or ERI METHOD-The building or dwelling unit shall be tested and verified as having an air leakage rate of not exceeding the selected ACH(50) value, as shown on Form R405-2020 (Performance) or R406-2020 (ERI), section labeled as infiltration, sub-section ACH50. <i>ACH(50) specified on Form R405-2020-Energy Calc (Performance) or R406-2020 (ERI):</i> 6.200		
x 60 ÷ 22550 = CFM(50)Building VolumeACH(50) ☐ PASS ☐ When ACH(50) is less than 3, Mechanical Ventilation installation must be verified by building department. <u>Method for calculating building volume:</u> ☐ Retrieved from architectural plans ☒ Code software calculated ☐ Field measured and calculated		
R402.4.1.2 Testing. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 Pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), <i>Florida Statutes</i>, or individuals licensed as set forth in Section 489.105(3)(f), (g), or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the <i>code official</i>. Testing shall be performed at any time after creation of all penetrations of the <i>building thermal envelope</i>. During testing: 1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures. 2. Dampers including exhaust, intake, makeup air, back draft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures. 3. Interior doors, if installed at the time of the test, shall be open. 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed. 5. Heating and cooling systems, if installed at the time of the test, shall be turned off. 6. Supply and return registers, if installed at the time of the test, shall be fully open.		
Testing Company		
Company Name: _____Phone: _____ I hereby verify that the above Air Leakage results are in accordance with the 2020 7th Edition Florida Building Code Energy Conservation requirements according to the compliance method selected above. Signature of Tester: _____Date of Test: _____ Printed Name of Tester: _____ License/Certification #: _____Issuing Authority: _____		

Duct Leakage Test Report

Residential Prescriptive, Performance or ERI Method Compliance 2020 Florida Building Code, Energy Conservation, 7th Edition

Jurisdiction:	Permit #:										
Job Information											
Builder:	Community: Lot: NA										
Address:											
City:	State: FL Zip:										
Duct Leakage Test Results											
<table border="1" style="width: 100%; border-collapse: collapse;"> <tr><td style="padding: 2px 5px;">System 1</td><td style="padding: 2px 5px;">_____ cfm25</td></tr> <tr><td style="padding: 2px 5px;">System 2</td><td style="padding: 2px 5px;">_____ cfm25</td></tr> <tr><td style="padding: 2px 5px;">System 3</td><td style="padding: 2px 5px;">_____ cfm25</td></tr> <tr><td style="padding: 2px 5px;">Sum of others</td><td style="padding: 2px 5px;">_____ cfm25</td></tr> <tr><td style="padding: 2px 5px;">Total of all</td><td style="padding: 2px 5px;">_____ cfm25</td></tr> </table> _____ ÷ $\frac{2255}{\text{Total of all systems}}$ = _____ Qn Total of all systems Total Conditioned Square Footage PASS FAIL	System 1	_____ cfm25	System 2	_____ cfm25	System 3	_____ cfm25	Sum of others	_____ cfm25	Total of all	_____ cfm25	☐ Prescriptive Method cfm25 (Total) To qualify as "substantially leak free" Qn Total must be less than or equal to 0.04 if air handler unit is installed. If air handler unit is not installed, Qn Total must be less than or equal to 0.03. This testing method meets the requirements in accordance with Section R403.3.3. <i>Is the air handler unit installed during testing?</i> ☐ YES ($= \frac{0.04}{Qn}$) ☐ NO ($= \frac{0.03}{Qn}$) ☒ Performance/ERI Method cfm25 (Out or Total) To qualify using this method, Qn must not be greater than the proposed duct leakage Qn specified on Form R405-2020 or R406-2020. <i>Leakage Type selected on Form R405-2020 (EnergyCalc) or R406-2020</i> <i>Qn specified on Form R405-2020 (EnergyCalc) or R406-2020</i> Proposed Leak Free 0.03
System 1	_____ cfm25										
System 2	_____ cfm25										
System 3	_____ cfm25										
Sum of others	_____ cfm25										
Total of all	_____ cfm25										
Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes.											
Testing Company											
Company Name: _____ Phone: _____ I hereby verify that the above duct leakage testing results are in accordance with the Florida Building Code requirements with the selected compliance path as stated above, either the Prescriptive Method or Performance Method.											
Signature of Tester: _____ Date of Test: _____											
Printed Name of Tester: _____											
License/Certification #: _____ Issuing Authority: _____											

Residential System Sizing Calculation

Summary

Project Title:
BUTLER RESIDENCE

, FL


9/14/2023

Location for weather data: Gainesville, FL - Defaults: Latitude(29.7) Altitude(152 ft.) Temp Range(M)			
Humidity data: Interior RH (50%) Outdoor wet bulb (77F) Humidity difference(51gr.)			
Winter design temperature(TMY3 99%)	30 F	Summer design temperature(TMY3 99%)	94 F
Winter setpoint	70 F	Summer setpoint	75 F
Winter temperature difference	40 F	Summer temperature difference	19 F
Total heating load calculation	32853 Btuh	Total cooling load calculation	18453 Btuh
Submitted heating capacity	% of calc Btuh	Submitted cooling capacity	% of calc Btuh
Total (Electric Heat Pump)	100.0 32853	Sensible (SHR = 0.70)	106.9 16170
Heat Pump + Auxiliary(0.0kW)	100.0 32853	Latent	208.2 6930
		Total (Electric Heat Pump)	125.2 23100

WINTER CALCULATIONS

Winter Heating Load (for 2255 sqft)


Load component	Load
Window total 221 sqft	4539 Btuh
Wall total 2130 sqft	6768 Btuh
Door total 136 sqft	2454 Btuh
Ceiling total 2255 sqft	2289 Btuh
Floor total 2255 sqft	11800 Btuh
Infiltration 80 cfm	3499 Btuh
Duct loss	1066 Btuh
Subtotal	32415 Btuh
Ventilation Ex:120 cfm; Sup:10 cfm	438 Btuh
TOTAL HEAT LOSS	32853 Btuh

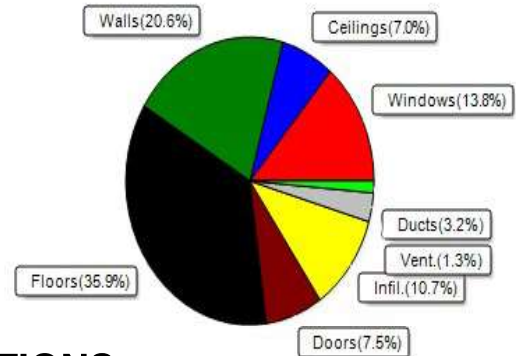

SUMMER CALCULATIONS

Summer Cooling Load (for 2255 sqft)

Load component	Load
Window total 221 sqft	3120 Btuh
Wall total 2130 sqft	3766 Btuh
Door total 136 sqft	1841 Btuh
Ceiling total 2255 sqft	1946 Btuh
Floor total	0 Btuh
Infiltration 60 cfm	1247 Btuh
Internal gain	2120 Btuh
Duct gain	877 Btuh
Sens.VentilationEx:120 cfm; Sup:10 cfm	208 Btuh
Blower Load	0 Btuh
Total sensible gain	15125 Btuh
Latent gain(ducts)	114 Btuh
Latent gain(infiltration)	2069 Btuh
Latent gain(ventilation)	345 Btuh
Latent gain(internal/occupants/other)	800 Btuh
Total latent gain	3328 Btuh
TOTAL HEAT GAIN	18453 Btuh

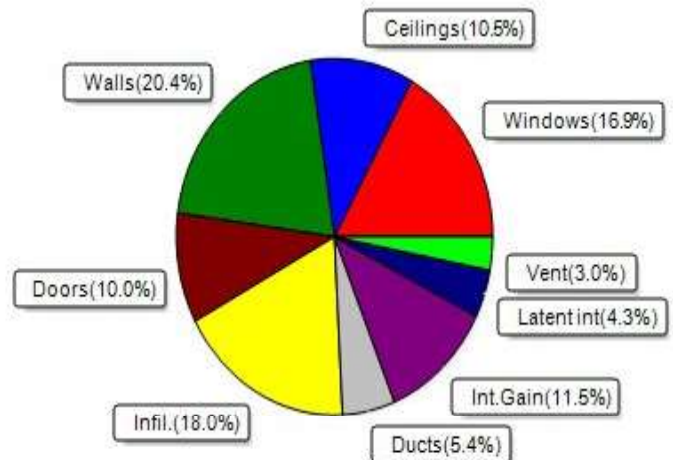

8th Edition

EnergyGauge® System Sizing

PREPARED BY: _____

DATE: _____

System Sizing Calculations - Summer

Residential Load - Whole House Component Details

Project Title:
BUTLER RESIDENCE

, FL

9/14/2023

Reference City: Gainesville, FL (Defaults)
Humidity difference: 51gr.

Temperature Difference: 19.0F(TMY3 99%)
Summer Setpoint: 75 °F (Required Manual J default)

Component Loads for Whole House

Window	Type*						Overhang		Window Area(sqft)			HTM		Load	
	Panes	SHGC	U	InSh	IS	Ornt	Len	Hgt	Gross	Shaded	Unshaded	Shaded	Unshaded		
1	2 NFRC	0.25, 0.40	B-L	No	S		1.3ft	3.0ft	20.0	15.3	4.7	10	12	209	Btuh
2	2 NFRC	0.25, 0.40	B-L	No	S		1.3ft	3.0ft	16.0	12.2	3.8	10	12	168	Btuh
3	2 NFRC	0.25, 0.40	B-L	No	S		1.3ft	3.0ft	16.0	12.2	3.8	10	12	168	Btuh
4	2 NFRC	0.25, 0.55	B-L	No	S		6.3ft	2.0ft	36.0	36.0	0.0	13	15	465	Btuh
5	2 NFRC	0.25, 0.55	B-L	No	S		1.3ft	3.0ft	16.0	12.2	3.8	13	15	213	Btuh
6	2 NFRC	0.25, 0.55	B-L	No	S		1.3ft	3.0ft	16.0	12.2	3.8	13	15	213	Btuh
7	2 NFRC	0.25, 0.55	B-L	No	S		1.3ft	3.0ft	20.0	15.3	4.7	13	15	266	Btuh
8	2 NFRC	0.25, 0.55	B-L	No	W		1.3ft	2.0ft	16.0	0.0	16.0	13	26	419	Btuh
9	2 NFRC	0.25, 0.55	B-L	No	N		10.3f	2.0ft	16.0	0.0	16.0	13	13	207	Btuh
10	2 NFRC	0.25, 0.55	B-L	No	N		1.3ft	3.0ft	36.0	0.0	36.0	13	13	465	Btuh
11	2 NFRC	0.25, 0.55	B-L	No	E		1.3ft	2.0ft	12.5	0.0	12.5	13	26	327	Btuh
	Window Total								221 (sqft)					3120 Btuh	
Walls	Type	U-Value				R-Value		Area(sqft)			HTM		Load		
						Cav/Sheath									
1	Frame - Wood - Ext					0.08	19.0/0.0		67.3		1.7		111	Btuh	
2	Frame - Wood - Ext					0.08	19.0/0.0		50.0		1.7		83	Btuh	
3	Frame - Wood - Ext					0.08	19.0/0.0		94.0		1.7		155	Btuh	
4	Frame - Wood - Ext					0.08	19.0/0.0		50.0		1.7		83	Btuh	
5	Frame - Wood - Ext					0.08	19.0/0.0		150.7		1.7		249	Btuh	
6	Frame - Wood - Ext					0.08	19.0/0.0		50.0		1.7		83	Btuh	
7	Frame - Wood - Ext					0.08	19.0/0.0		85.7		1.7		142	Btuh	
8	Frame - Wood - Ext					0.08	19.0/0.0		31.7		1.7		52	Btuh	
9	Frame - Wood - Ext					0.08	19.0/0.0		107.3		1.7		177	Btuh	
10	Frame - Wood - Ext					0.08	19.0/0.0		329.0		1.7		544	Btuh	
11	Frame - Wood - Ext					0.08	19.0/0.0		220.0		1.7		364	Btuh	
12	Frame - Wood - Ext					0.08	19.0/0.0		25.0		1.7		41	Btuh	
13	Frame - Wood - Ext					0.08	19.0/0.0		125.7		1.7		208	Btuh	
14	Frame - Wood - Ext					0.08	19.0/0.0		25.0		1.7		41	Btuh	
15	Frame - Wood - Ext					0.08	19.0/0.0		77.3		1.7		128	Btuh	
16	Frame - Wood - Ext					0.08	19.0/0.0		148.3		1.7		245	Btuh	
17	Frame - Wood - Ext					0.08	19.0/0.0		94.0		1.7		155	Btuh	
18	Frame - Wood - Ext					0.09	13.0/0.0		399.2		2.3		903	Btuh	
	Wall Total								2130 (sqft)					3766 Btuh	
Doors	Type					Area (sqft)			HTM		Load				
1	Insulated - Exterior								20.0		12.0		240	Btuh	
2	Insulated - Exterior								20.0		13.8		276	Btuh	
3	Insulated - Exterior								96.0		13.8		1325	Btuh	
	Door Total								136 (sqft)					1841 Btuh	
Ceilings	Type/Color/Surface	U-Value				R-Value		Area(sqft)			HTM		Load		
1	Vented Attic/Light/Shingle/RB					0.025	38.0/0.0		2255.0		0.86		1946	Btuh	
	Ceiling Total								2255 (sqft)					1946 Btuh	
Floors	Type					R-Value		Size			HTM		Load		
1	Slab On Grade						1.0		2255 (ft-perimeter)		0.0		0	Btuh	
	Floor Total								2255.0 (sqft)					0 Btuh	

Manual J Summer Calculations

Residential Load - Component Details (continued)

Project Title: Climate:FL_GAINESVILLE_REGIONAL_A
BUTLER RESIDENCE

, FL

9/14/2023

	Envelope Subtotal:					10673 Btuh
Infiltration	Type	Average ACH	Volume(cuft)	Wall Ratio	CFM=	Load
	Natural(Adjusted for ventilation)	0.16	22550	1	59.9	1247 Btuh
Internal gain	Occupants	4	Btuh/occupant		Appliance	Load
			X 230	+	1200	2120 Btuh
	Sensible Envelope Load:					14040 Btuh
Duct load	Extremely sealed, Supply(R6.0-Attic), Return(R6.0-Condi) (DGM of 0.062)					877 Btuh
	Sensible Load All Zones					14917 Btuh

Manual J Summer Calculations

Residential Load - Component Details (continued)

Project Title: Climate:FL_GAINESVILLE_REGIONAL_A
BUTLER RESIDENCE

, FL

9/14/2023

WHOLE HOUSE TOTALS

Whole House Totals for Cooling	Sensible Envelope Load All Zones	14040 Btuh
	Sensible Duct Load	877 Btuh
	Total Sensible Zone Loads	14917 Btuh
	Sensible ventilation (Ex:120 cfm; Sup:100 cfm)	208 Btuh
	Blower	0 Btuh
	Total sensible gain	15125 Btuh
	Latent infiltration gain (for 51 gr. humidity difference)	2069 Btuh
	Latent ventilation gain	345 Btuh
	Latent duct gain	114 Btuh
	Latent occupant gain (4.0 people @ 200 Btuh per person)	800 Btuh
	Latent other gain	0 Btuh
	Latent total gain	3328 Btuh
	TOTAL GAIN	18453 Btuh

EQUIPMENT

1. Central Unit	#	23100 Btuh
-----------------	---	------------

*Key: Window types (Panels - Number and type of panes of glass)
(SHGC - Shading coefficient of glass as SHGC numerical value)
(U - Window U-Factor)
(InSh - Interior shading device: none(No), Blinds(B), Draperies(D) or Roller Shades(R))
- For Blinds: Assume medium color, half closed
For Draperies: Assume medium weave, half closed
For Roller shades: Assume translucent, half closed
(IS - Insect screen: none(N), Full(F) or Half(½))
(Ornt - compass orientation)



Version 8

System Sizing Calculations - Winter

Residential Load - Whole House Component Details

Project Title:
BUTLER RESIDENCE
Building Type: User

, FL

9/14/2023

Reference City: Gainesville, FL (Defaults) Winter Temperature Difference: 40.0 °F (TMY3 99%)
Winter Setpoint: 70 °F (Required Manual J default)

Component Loads for Whole House

Window	Panes/Type	Frame	U	Orientation	Area(sqft)	X	HTM=	Load
1	2, NFRC 0.25	Vinyl	0.40	S	20.0		16.0	320 Btuh
2	2, NFRC 0.25	Vinyl	0.40	S	16.0		16.0	256 Btuh
3	2, NFRC 0.25	Vinyl	0.40	S	16.0		16.0	256 Btuh
4	2, NFRC 0.25	Vinyl	0.55	S	36.0		22.0	792 Btuh
5	2, NFRC 0.25	Vinyl	0.55	S	16.0		22.0	352 Btuh
6	2, NFRC 0.25	Vinyl	0.55	S	16.0		22.0	352 Btuh
7	2, NFRC 0.25	Vinyl	0.55	S	20.0		22.0	440 Btuh
8	2, NFRC 0.25	Vinyl	0.55	W	16.0		22.0	352 Btuh
9	2, NFRC 0.25	Vinyl	0.55	N	16.0		22.0	352 Btuh
10	2, NFRC 0.25	Vinyl	0.55	N	36.0		22.0	792 Btuh
11	2, NFRC 0.25	Vinyl	0.55	E	12.5		22.0	275 Btuh
Window Total					220.5(sqft)			4539 Btuh
Walls	Type	Ornt.	Ueff.	R-Value (Cav/Sh)	Area	X	HTM=	Load
1	Frame - Wood	- Ext	(0.077)	19.0/0.0	67		3.09	208 Btuh
2	Frame - Wood	- Ext	(0.077)	19.0/0.0	50		3.09	155 Btuh
3	Frame - Wood	- Ext	(0.077)	19.0/0.0	94		3.09	291 Btuh
4	Frame - Wood	- Ext	(0.077)	19.0/0.0	50		3.09	155 Btuh
5	Frame - Wood	- Ext	(0.077)	19.0/0.0	151		3.09	466 Btuh
6	Frame - Wood	- Ext	(0.077)	19.0/0.0	50		3.09	155 Btuh
7	Frame - Wood	- Ext	(0.077)	19.0/0.0	86		3.09	265 Btuh
8	Frame - Wood	- Ext	(0.077)	19.0/0.0	32		3.09	98 Btuh
9	Frame - Wood	- Ext	(0.077)	19.0/0.0	107		3.09	332 Btuh
10	Frame - Wood	- Ext	(0.077)	19.0/0.0	329		3.09	1017 Btuh
11	Frame - Wood	- Ext	(0.077)	19.0/0.0	220		3.09	680 Btuh
12	Frame - Wood	- Ext	(0.077)	19.0/0.0	25		3.09	77 Btuh
13	Frame - Wood	- Ext	(0.077)	19.0/0.0	126		3.09	388 Btuh
14	Frame - Wood	- Ext	(0.077)	19.0/0.0	25		3.09	77 Btuh
15	Frame - Wood	- Ext	(0.077)	19.0/0.0	77		3.09	239 Btuh
16	Frame - Wood	- Ext	(0.077)	19.0/0.0	148		3.09	458 Btuh
17	Frame - Wood	- Ext	(0.077)	19.0/0.0	94		3.09	291 Btuh
18	Frame - Wood	- Ext	(0.089)	13.0/0.0	399		3.55	1417 Btuh
Wall Total					2130(sqft)			6768 Btuh
Doors	Type	Storm	Ueff.		Area	X	HTM=	Load
1	Insulated - Exterior, n		(0.400)		20		16.0	320 Btuh
2	Insulated - Exterior, n		(0.460)		20		18.4	368 Btuh
3	Insulated - Exterior, n		(0.460)		96		18.4	1766 Btuh
Door Total					136(sqft)			2454Btuh
Ceilings	Type/Color/Surface		Ueff.	R-Value	Area	X	HTM=	Load
1	Flat ceil/L/Shing		(0.025)	38.0/0.0	2255		1.0	2289 Btuh
Ceiling Total					2255(sqft)			2289Btuh

Manual J Winter Calculations

Residential Load - Component Details (continued)

Project Title:
BUTLER RESIDENCE
Building Type: User

, FL

9/14/2023

Floors 1	Type Slab On Grade Floor Total	Ueff. (1.180)	R-Value 1.0	Size X 250.0 ft(perim.) 2255 sqft	HTM= 47.2	Load 11800 Btuh 11800 Btuh
	Envelope Subtotal:					27850 Btuh
Infiltration	Type Natural(Adjusted for ventilation)	Wholehouse ACH 0.21	Volume(cuft) 22550	Wall Ratio 1.00	CFM= 79.9	3499 Btuh
Duct load	Extremely sealed, R6.0, Supply(Att), Return(Con) (DLM of 0.034)					1066 Btuh
All Zones	Sensible Subtotal All Zones					32415 Btuh

WHOLE HOUSE TOTALS

Totals for Heating	Subtotal Sensible Heat Loss Ventilation Sens. Heat Loss (Ex:120 cfm; Sup:100 cfm) Total Heat Loss	32415 Btuh 438 Btuh 32853 Btuh
---------------------------	---	--------------------------------------

EQUIPMENT

1. Electric Heat Pump	#	32853 Btuh
-----------------------	---	------------

Key: Window types - NFRC (Requires U-Factor and Shading coefficient(SHGC) of glass as numerical values)
or - Glass as 'Clear' or 'Tint' (Uses U-Factor and SHGC defaults)

U - (Window U-Factor)

HTM - (ManualJ Heat Transfer Multiplier)



Version 8
