

Manufacturer Data Report

State of Florida

Department of Highway Safety and Motor Vehicles
Division of Motor Vehicles

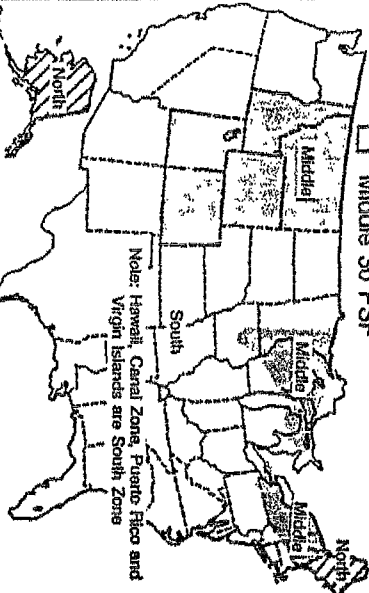
Nell Korman Building, 2800 Apalachee Parkway (Room A 139) Tallahassee, FL 32399-0640

DEALER'S NAME Sun CountryADDRESS Ocala, FloridaCITY Ocala, Florida STATE FL ZIP 32668DEALER NAME Norkus, Tompas, Assoc.ADDRESS 237 East RandolphCITY Nappanee, Indiana STATE IN ZIP 46550

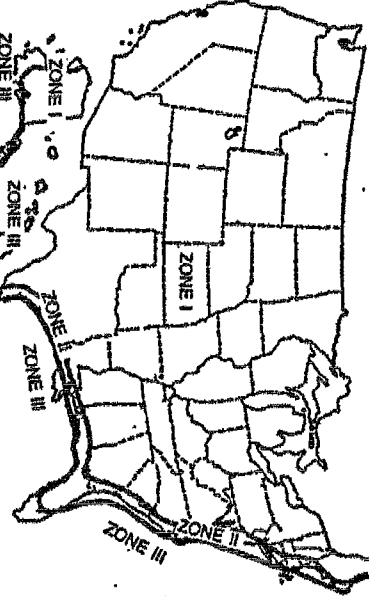
FL 559133 X 5591334

M.I.D. # 10124288XUDATE MANUFACTURED 11/30/94MODEL # KC286022 YEAR 95HFR NAME Liberty Homes, Inc.ADDRESS 495 Oak RoadCITY Ocala, Florida STATE FL ZIP 34477

ROOF LOAD ZONES

☐ North 40 PSF ☒ Middle 30 PSF ☐ South 20 PSF

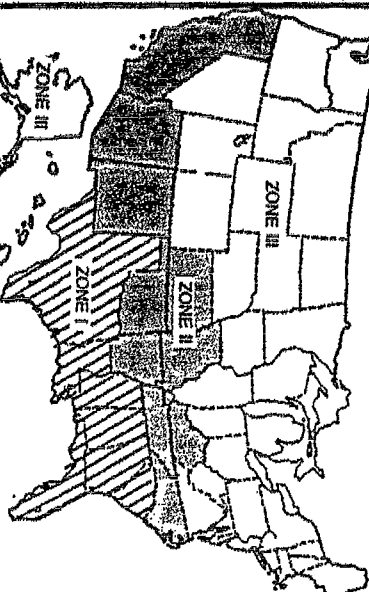
WIND ZONES

☐ Zone I 15 PSF Horizontal & 9 PSF Uplift
☒ Zone II 100 mph
☐ Zone III 110 mph
☐ Exposure D

HEATING & COOLING DESIGNED CERTIFICATE

Design Winter Climate Zone

This mobile home has been thermally insulated to conform with the requirements of the Federal Manufactured Home Construction and Safety Standards for all locations within climatic:

☒ ZONE I ☐ ZONE II ☐ ZONE III

Manufacturer shall provide "U" factors as designed below.

Walls (without windows & doors) "U" = 0.101

Ceilings & roofs of light color "U" = 0.045

Ceilings & roofs of dark color "U" = 0.074

Floors "U" = 0.074

Air Ducts in floor "U" = 0.074

Air Ducts in ceiling "U" = 0.0785

Air Ducts installed outside "U" = 0.400

Heat transfer area to outside of home from air ducts located:

Inside Home Sq. Ft. _____

Outside Home Sq. Ft. _____

The heating equipment has the capacity to maintain an average 70° F temperature in this home at outdoor temperatures of _____ °F.

To maximize furnace operating economy and to conserve energy, it is recommended that this home be installed where the outdoor winter design temperature (9/12/95) is not higher than _____ °F.

The above information has been calculated assuming a maximum wind velocity of 15 MPH at standard atmospheric pressure.

The supply air distribution system installed in this home is sized:

☐ Not designed for A/C ☒ A/C Ready ☐ A/C installed

** FOR TALLAHASSEE CENTRAL OFFICE USE ONLY **

READ INSTRUCTIONS
COMPLAINTS
NAME
ADDRESS
REGION
CITY
STATE
ZIP

This mobile home is designed to comply with the Federal Manufactured Home Construction and Safety Standards in force at the time of manufacture.

SIGNED

Myra Duke

Type or Print Name

DEC 06 1994

11/30/94

Date
