

RECEIVED 11/07/2018 03:49PM
3524814807

Nov 07 18 03:02p FMHS
2018-11-06 14:27

C&G MAN. HOMES 386 752 2853 >> 3524814807

p.3
P 2/9

p.1

Mobile Home Permit Worksheet

Installer: Ernest S. Johnson License # JH 1025249


Address of home
being installed _____

Manufacturer Clayton Length x width 28' X 56'


NOTE: If home is a single wide fill out one half of the blocking plan
if home is a triple or quad wide sketch in remainder of home
I understand Lateral Arm Systems cannot be used on any home (new or used)
where the sidewall lies exceed 5 ft 4 in.

Installer's initials ESJ

Typical pier spacing



Show locations of Longitudinal and Lateral Systems
(use dark lines to show these locations)

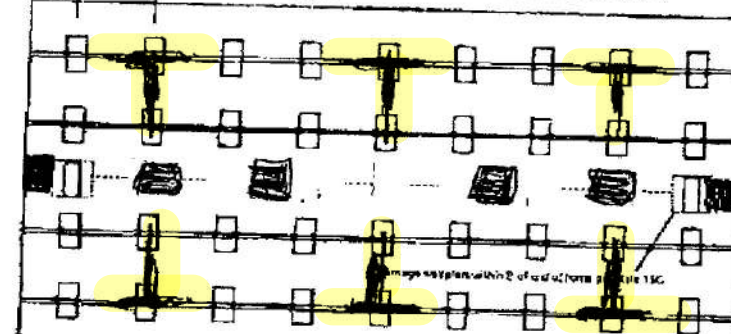

Digitally signed
by Laurie
Hodson
Date: 2020.06.26
15:50:20 -04:00

Page 1 of 2

Application Number: _____ Date: _____

New Home ☒ Used Home ☐

Home installed to the Manufacturer's Installation Manual
Home is installed in accordance with Rule 15-C

Single wide ☐ Wind Zone II ☒ Wind Zone II' ☐

Double wide ☒ Installation Decal # 71901

Triplet/Quad ☐ Serial # _____

PIER SPACING TABLE FOR USED HOMES

Load bearing capacity	Footc. size (sq in)	16' x 16' (256)	18 1/2' x 18 1/2' (342)	20' x 20' (400)	22' x 22' (484)	24' x 24' (576)	26' x 26' (676)
1000 psf	3'	3'	4'	5'	6'	7'	8'
1500 psf	4'	4'	5'	6'	7'	8'	9'
2000 psf	5'	5'	6'	7'	8'	9'	10'
2500 psf	6'	6'	7'	8'	9'	10'	11'
3000 psf	7'	7'	8'	9'	10'	11'	12'
3500 psf	8'	8'	9'	10'	11'	12'	13'

* Interpolated from Rule 15C-1 pier spacing table.

PIER PAD SIZES

I-beam pier pad size 23' x 31' 6" 06
Perimeter pier pad size 17.5' x 25.5'
Other pier pad sizes (required by the mfg.) _____

Draw the approximate locations of marriage wall openings 4 foot or greater. Use this symbol to show the piers.

List all marriage wall openings greater than 4 foot and their pier pad sizes below.

Opening	Pier pad size
<u>17.5' x 25.5'</u>	<u>17.5' x 25.5'</u>
<u>17.5' x 25.5'</u>	<u>17.5' x 25.5'</u>
<u>17.5' x 25.5'</u>	<u>17.5' x 25.5'</u>

TIEDOWN COMPONENTS

Longitudinal Stabilizing Device (LSD)
Manufacturer _____
Longitudinal Stabilizing Device w/ Lateral Arms
Manufacturer _____

POPULAR PAD SIZES

Pad Size	Sq ft
16' x 16'	256
18' x 18'	324
18.5' x 18.5'	342
18' x 22.5'	405
17' x 22'	374
13 1/4' x 28 1/4'	318
20' x 20'	400
17 3/16' x 25 3/16'	441
17 1/2' x 25 1/2'	446
24' x 24'	576
26' x 26'	676

ANCHORS

4" 5/8"

FRAME TIES

Within 2' of end of home spaced at 5' 4" oc

OTHER TIES

	Number
Sidewall	3
Longitudinal	0
Marriage wall	2
Shearwall	2

OLIVER 1101V

2020-05-19 11:52

C&G MAN. HOMES 386 752 2853 >> 3524814807

P 3/4
