

MANUFACTURER
ADDRESS

Fleetwood Homes Of Fl.
3804 Sydney Rd.
P.O. Drawer PP

Plant City, FL 33564-9035

Date of Manufacture 2-6-1998 HUD Label No.(s) FLA 639710-637711 Plant Number 079

Manufacturer's Serial Number and Model Unit Designation ELFLW19AB13453HE21 - 4523A

RADCO

Design Approval by (D.A.P.I.A.)

This manufactured home is designed to comply with the federal manufactured home construction and safety standards in force at time of manufacture. (For additional information, consult owner's manual.)

The factory installed equipment includes:

Equipment	Manufacturer	Model Designation
For heating	NA	
For air cooling	NA	
For cooking	Maytag	MER4320AAW
Refrigerator	Maytag	MSD2143ARW
Water Heater	Rheem	7140 DB
Washer	NA	
Clothes Dryer	NA	
Dishwasher	Maytag	PDB1100ADWE
Garbage Disposal	Whirlaway	PMIPC
Fireplace	S.M. I.	86ECMII
Stereo	NA	
Smoke Detector	FYRNETICS	1275
Microwave	Maytag	CMV1000ADW


HOME CONSTRUCTED FOR

Zone I Zone II Zone III


This home has not been designed for the higher wind pressure and anchoring provisions required for ocean/coastal areas and should not be located within 1500' of the coastline in Wind Zones II and III, unless the home and its anchoring and foundation system have been designed for the increased requirements specified for Exposure D in ANSI/ASCE 7-88.

This home has not been equipped with storm shutters or other protective coverings for windows and exterior door openings. For homes designed to be located in Wind Zones II and III, which have not been provided with shutters or equivalent covering devices, it is strongly recommended that the home be made ready to be equipped with these devices in accordance with the method recommended in manufacturers printed instructions.

BASIC WIND ZONE MAP

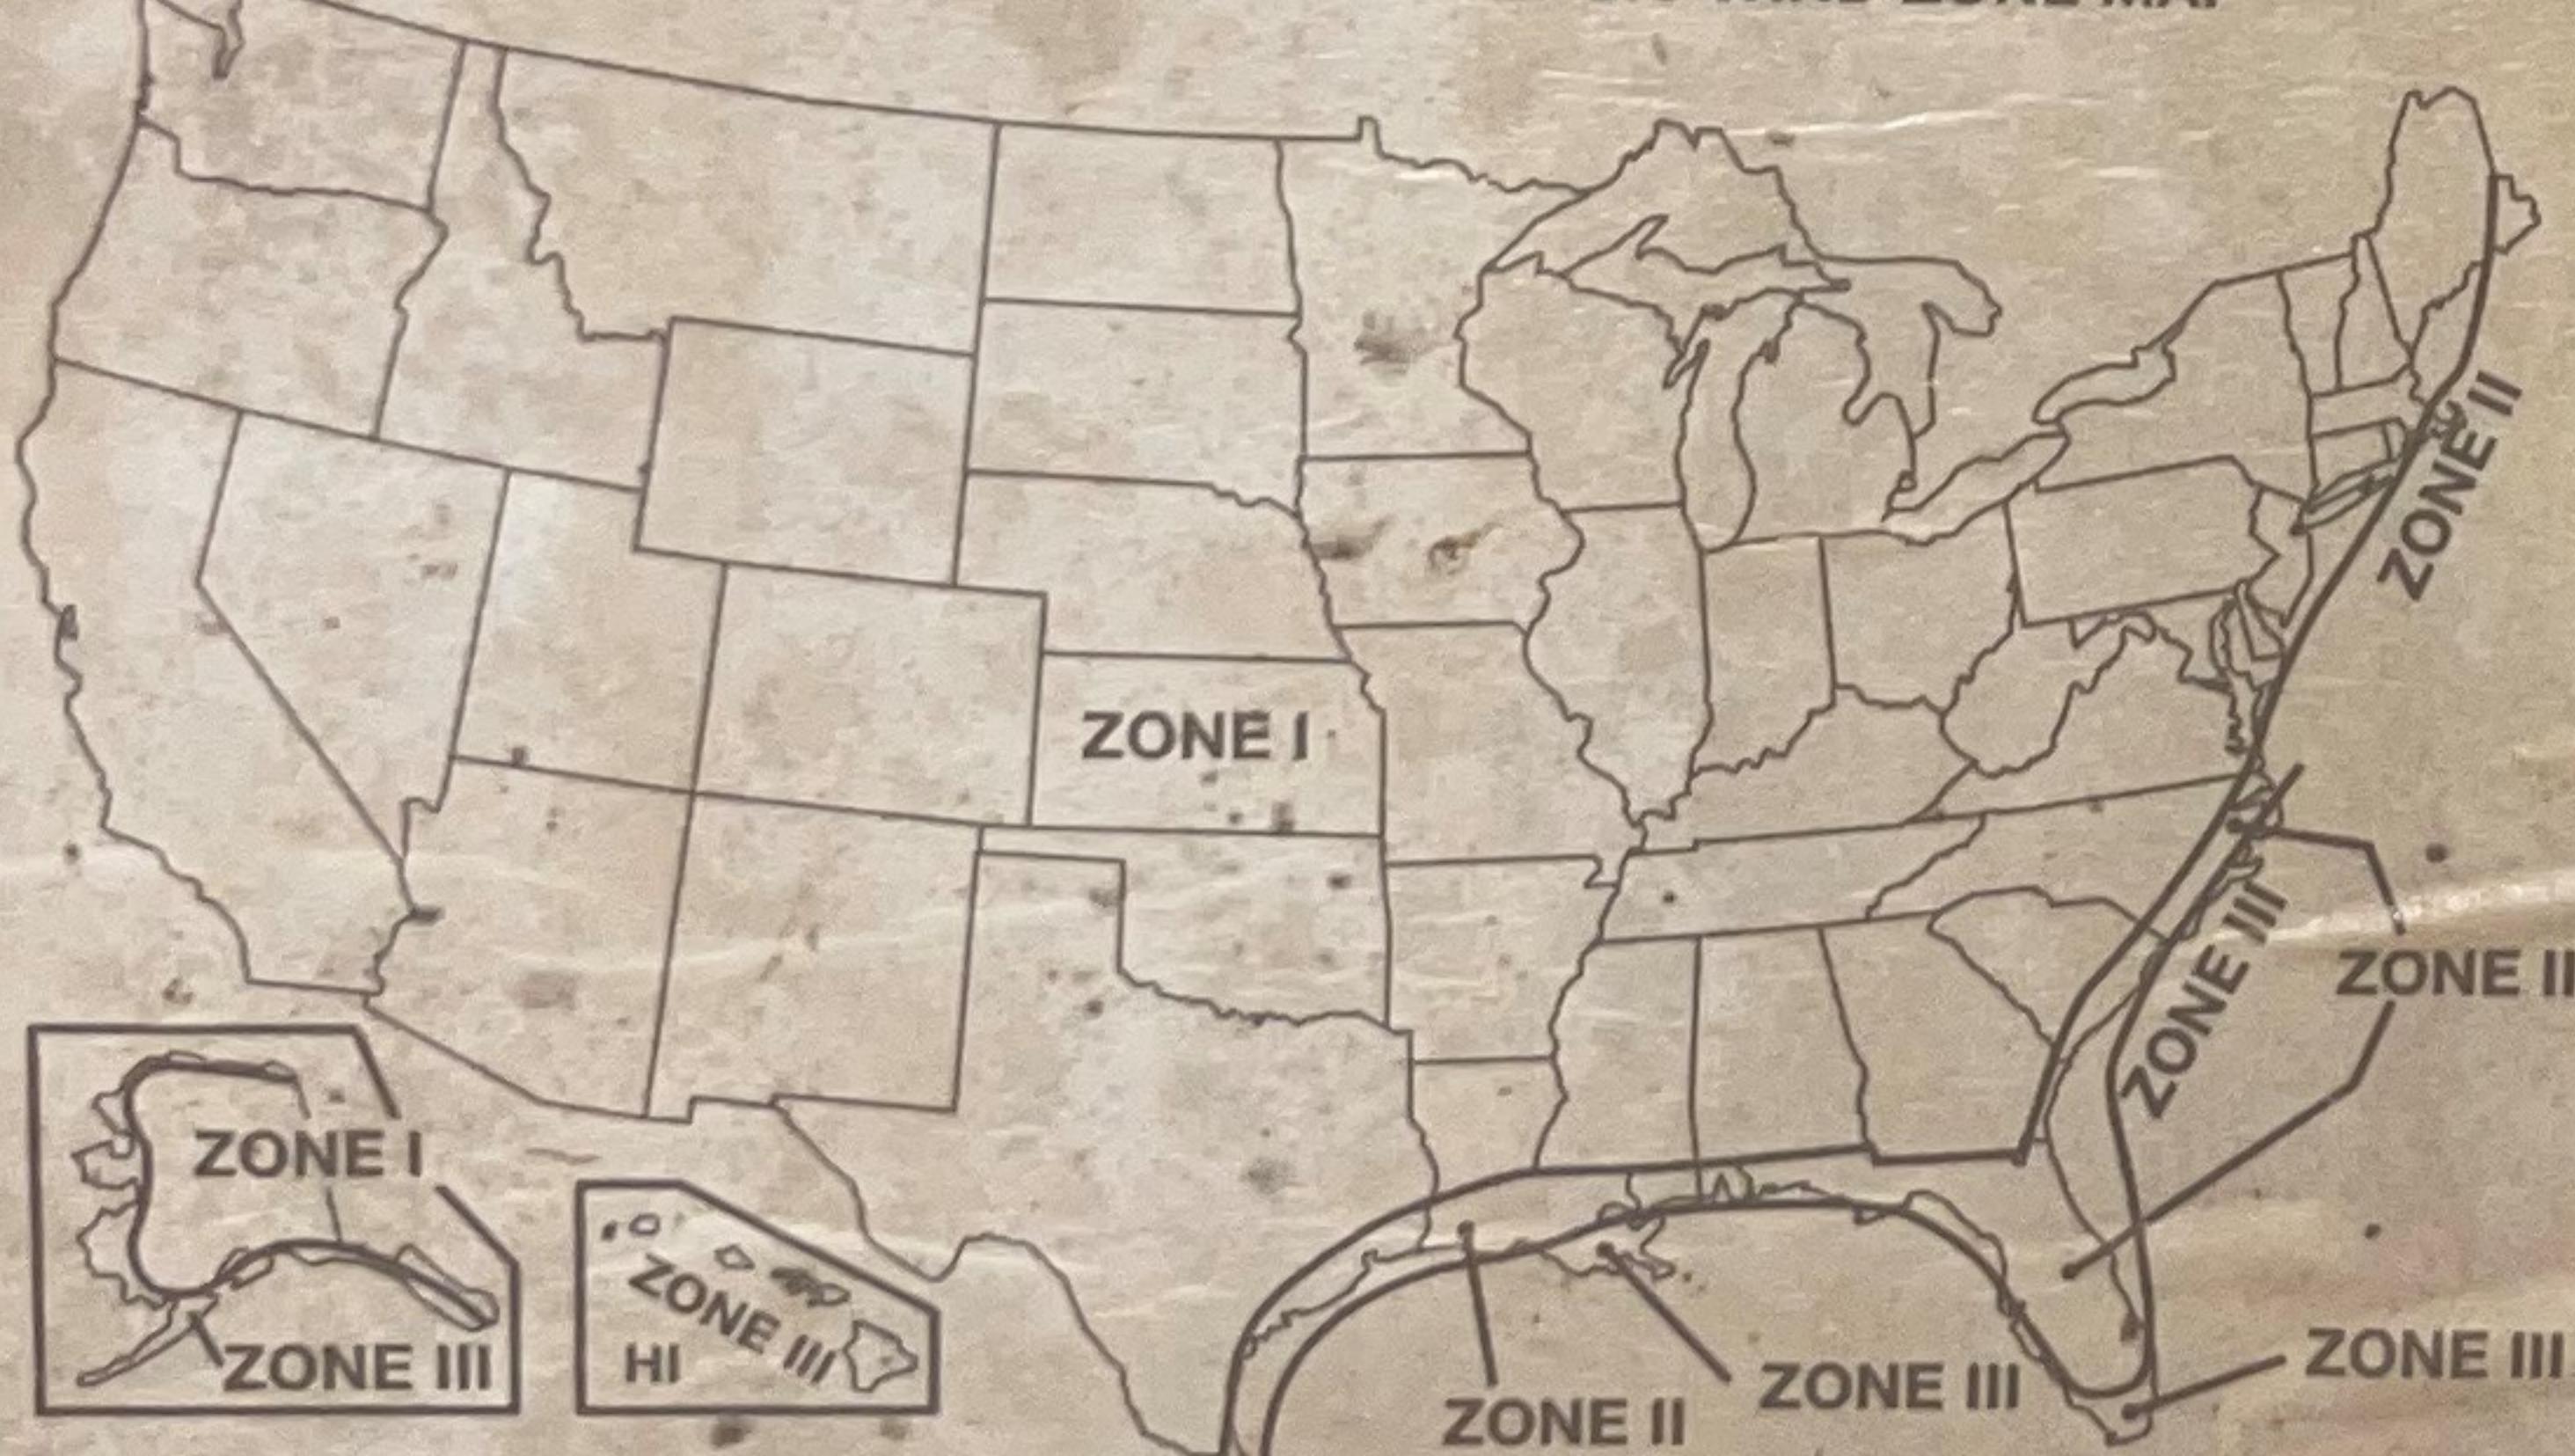

DESIGN ROOF LOAD ZONE MAP

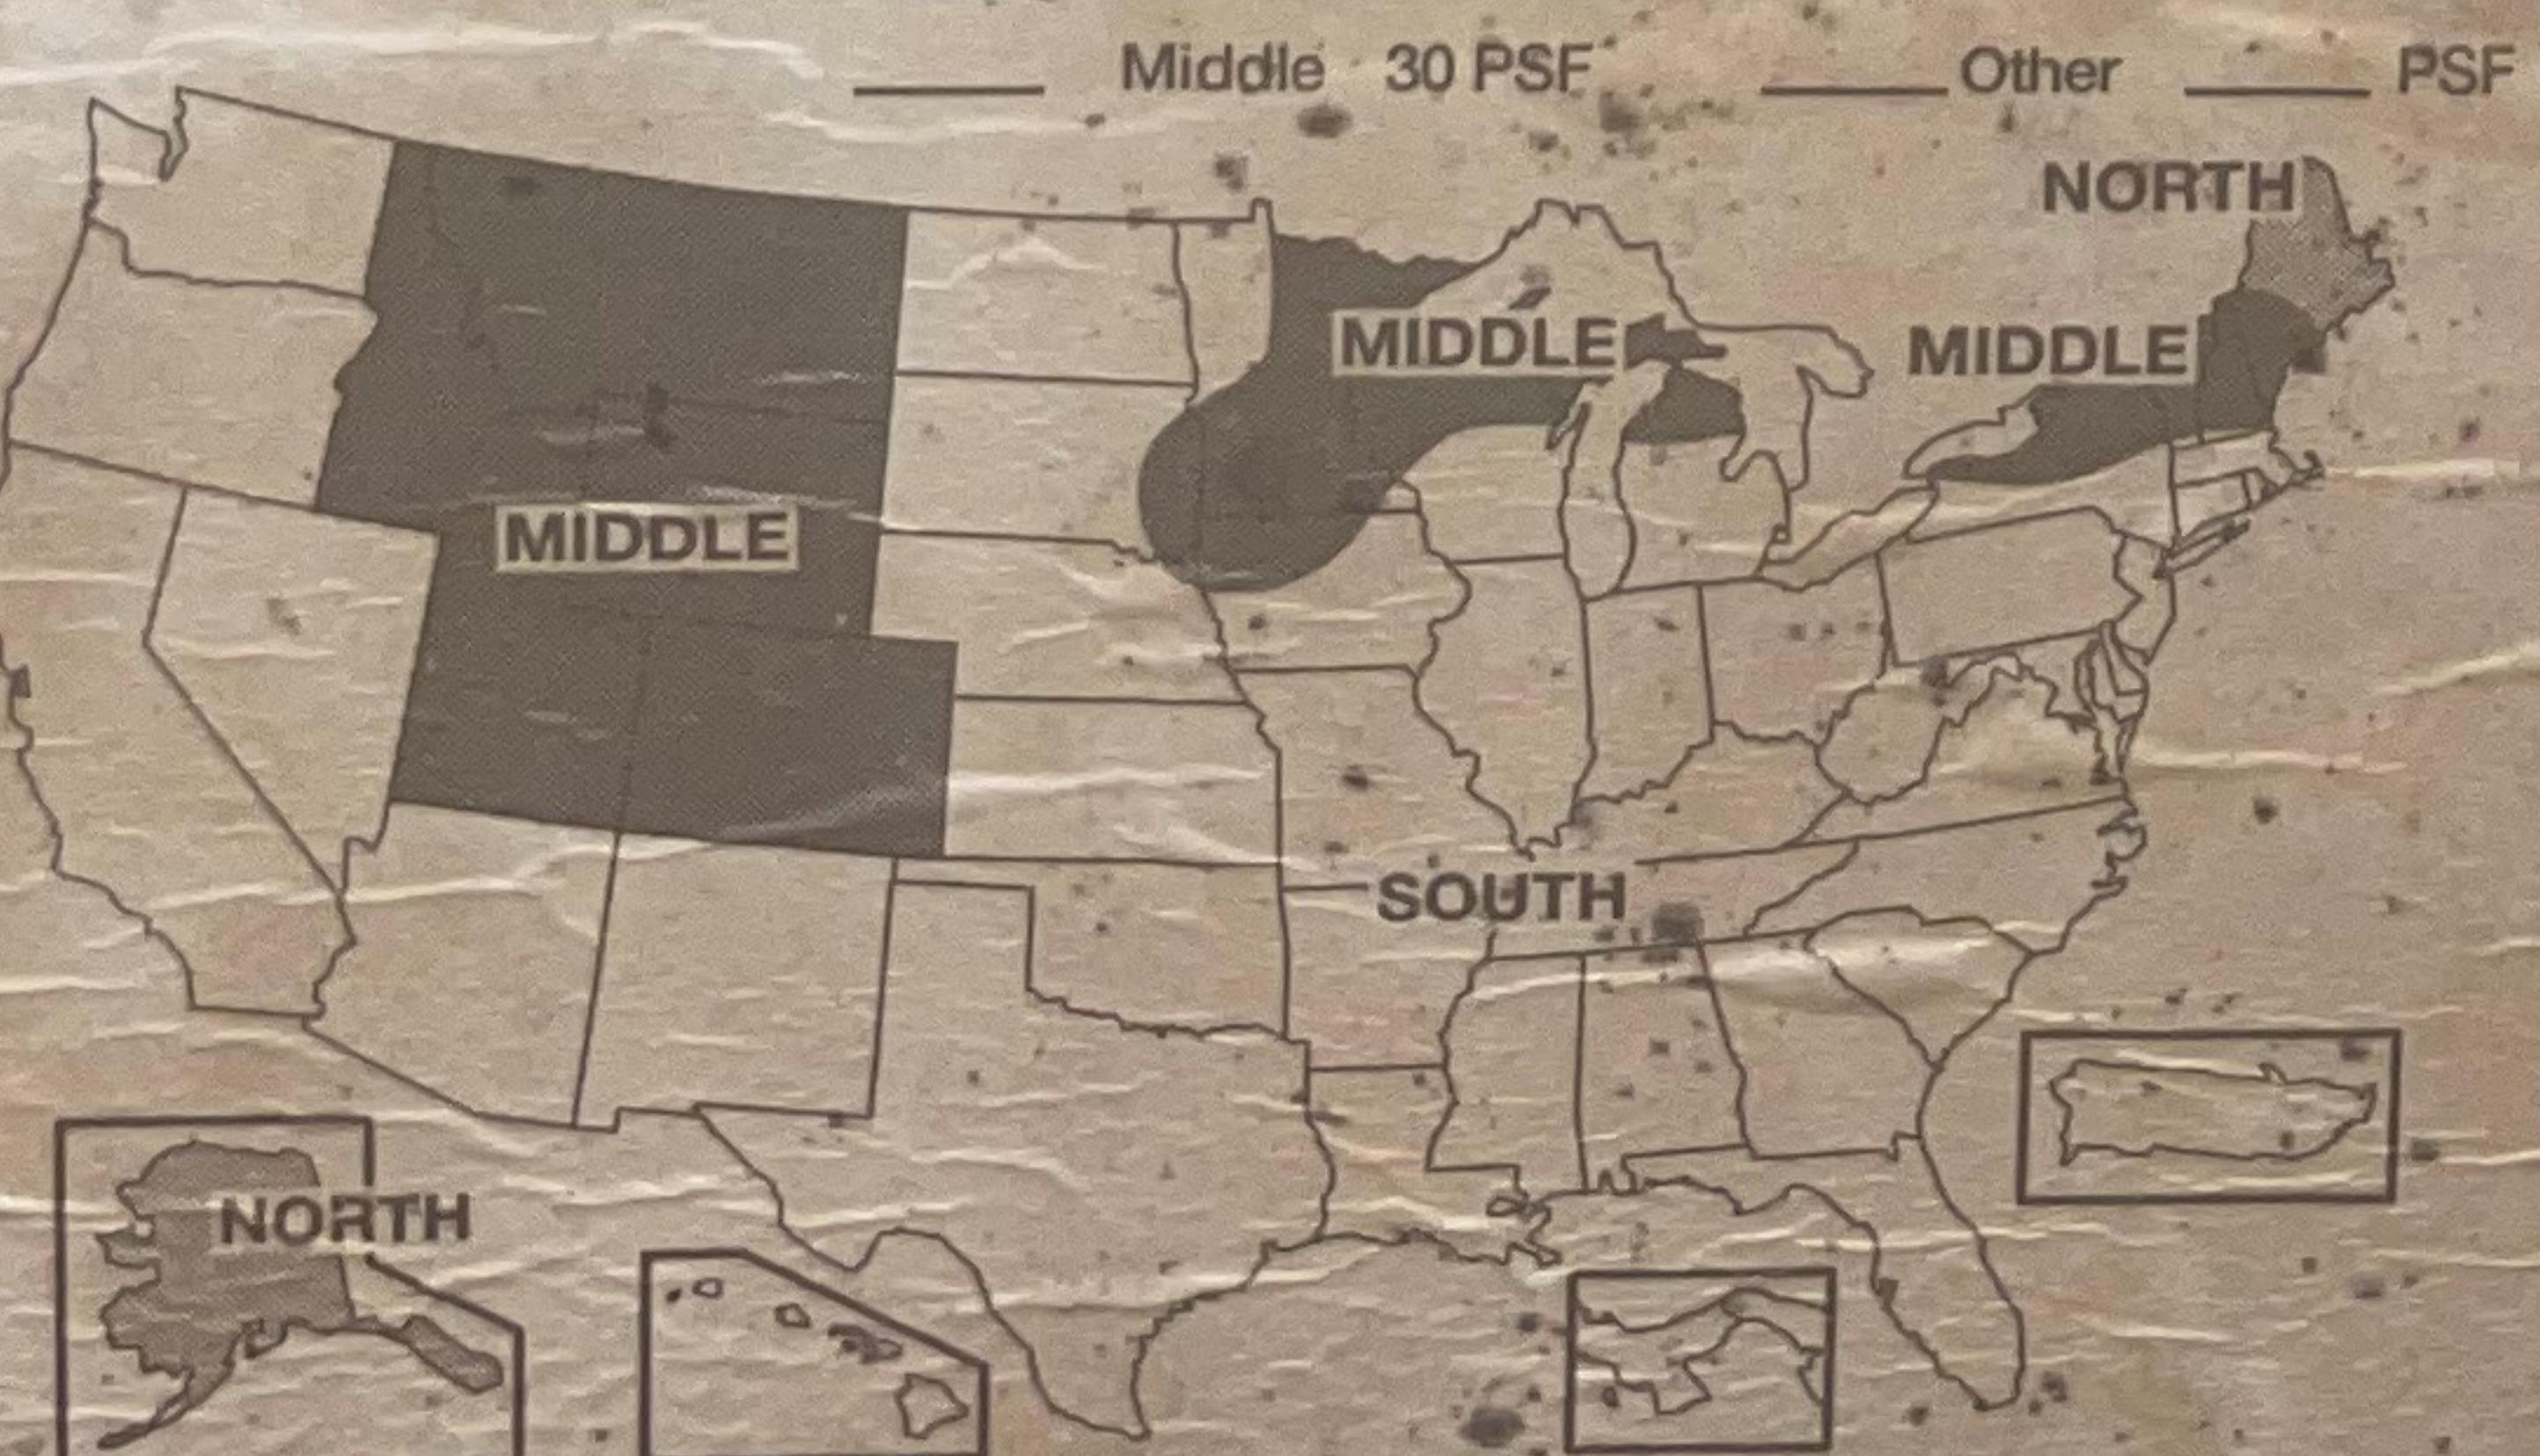

COMFORT HEATING
This manufactured home has been thermally insulated to conform with the requirements of the federal manufactured home construction and safety standards for all locations

within U/O value zone 1. Heating equipment manufacturer and model (see list at left). The above heating equipment has the capacity to maintain an average 70° F temperature in

this home at outdoor temperatures of NA °F. To maximize furnace operating economy, and to conserve energy, it is recommended that this home be installed where the outdoor winter design temperature (97 1/2%) is not higher than NA degrees Fahrenheit.

The above information has been calculated assuming a maximum wind velocity of 15 mph at standard atmospheric pressure.

COMFORT COOLING

Air conditioner provided at factory (Alternate I)

Air conditioner manufacturer and model (see list at left).

Certified capacity _____ B.T.U./hour in accordance with the appropriate air conditioning and refrigeration institute standards. The central air conditioning system provided in this home has been sized assuring an

orientation of the front (hitch end) of the home facing _____. On this basis the system is designed to maintain an indoor temperature of 75° F when outdoor

temperatures are _____ °F dry bulb and _____ °F wet bulb.

The temperature to which this home can be cooled will change depending upon the amount of exposure of the windows of this home to the sun's radiant heat. Therefore, the home's heat gains will vary dependent upon its orientation to the sun and any permanent shading provided. Information concerning the calculation of cooling loads at various locations, window exposures and shadings are provided in Chapter 22 of the 1989 edition of the ASHRAE Handbook of Fundamentals.

Information necessary to calculate cooling loads at various locations and orientations is provided in the special comfort cooling information provided with this home.

Air conditioner not provided at factory (Alternate II)

The air distribution system of this home is suitable for the installation of central air conditioning.

The supply air distribution system installed in this home is sized for a manufactured home

central air conditioning system of up to 40,000 B.T.U./hr. rated capacity which are certified in accordance with the appropriate air conditioning and refrigeration institute standards, when the air circulators of such air conditioners are rated at 0.3 inch water column static pressure or greater for the cooling air delivered to the manufactured home supply air duct system.

Information necessary to calculate cooling loads at various locations and orientations is provided in the special comfort cooling information provided with this manufactured home.

Air conditioning not recommended (Alternate III)

The air distribution system of this home has not been designed in anticipation of its use with a central air conditioning system.


To determine the required capacity of equipment to cool a home efficiently and economically, a cooling load (heat gain) calculation is required. The cooling load is dependent on the orientation, location and the structure of the home. Central air conditioners operate most efficiently and provide the greatest comfort when their capacity closely approximates the calculated cooling load. Each home's air conditioner should be sized in accordance with Chapter 22 of the American Society of Heating, Refrigerating and Air Conditioning Engineers (ASHRAE) Handbook of Fundamentals 1989 edition, once the location and orientation are known.

INFORMATION PROVIDED BY THE MANUFACTURER
NECESSARY TO CALCULATE SENSIBLE HEAT GAIN

Walls (without windows and doors)	"U" .09
Ceilings and roofs of light color)	"U" .05
Ceilings and roofs of dark color)	"U" .05
Floors	"U" .07
Air ducts in floor	"U" NA
Air ducts in ceiling	"U" .21
Air ducts installed outside the home	"U" .23

The following are the duct areas in this home:

Air ducts in floor	sq. ft. NA
Air ducts in ceiling	sq. ft. 6.943
Air ducts outside the home	sq. ft. NA

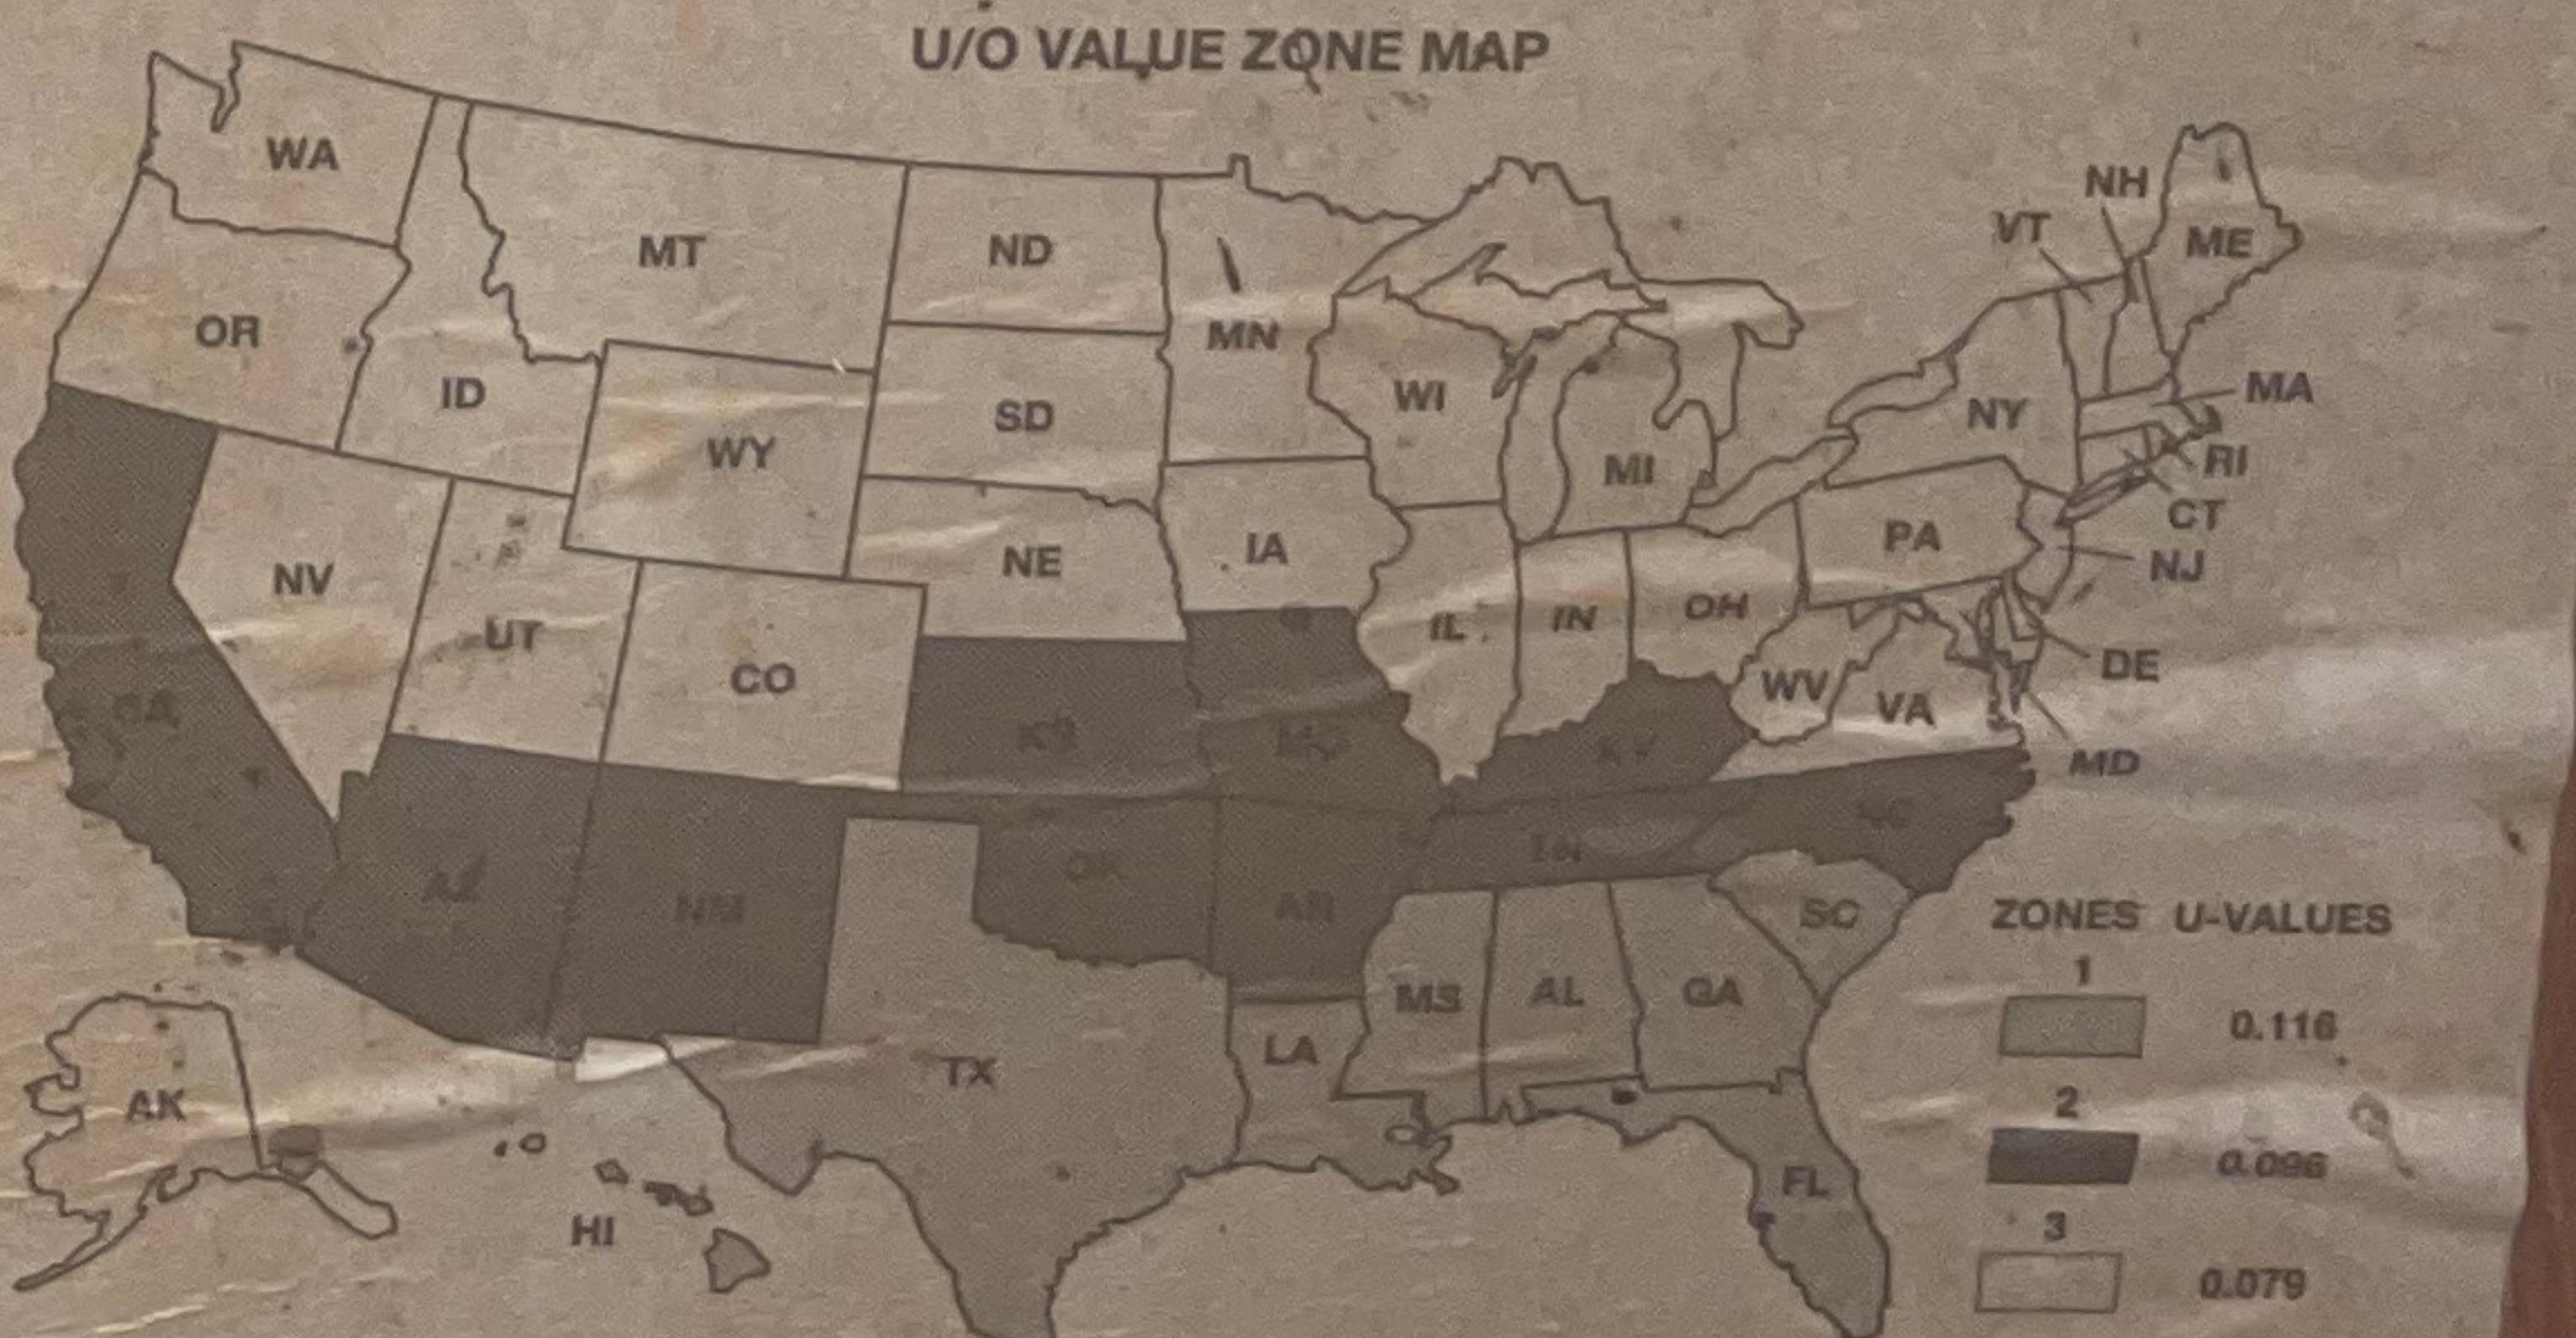

FM-056 ©Dec-O-Art, Inc. REV. 1/95 A

FLEETWOOD
3804 Sydney Road
P.O. Drawer PP
Plant City, FL 33564

ATTENTION
HOMEOWNER

TO ACTIVATE YOUR
FLEETWOOD
FACTORY SERVICE PLEASE
