

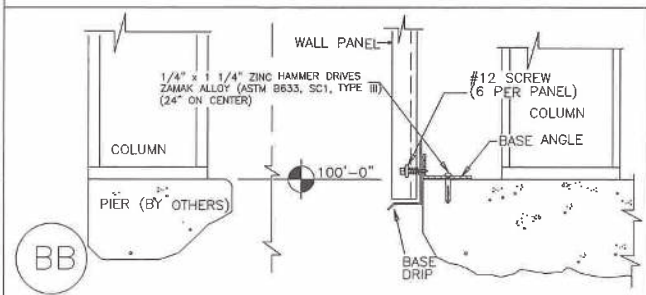
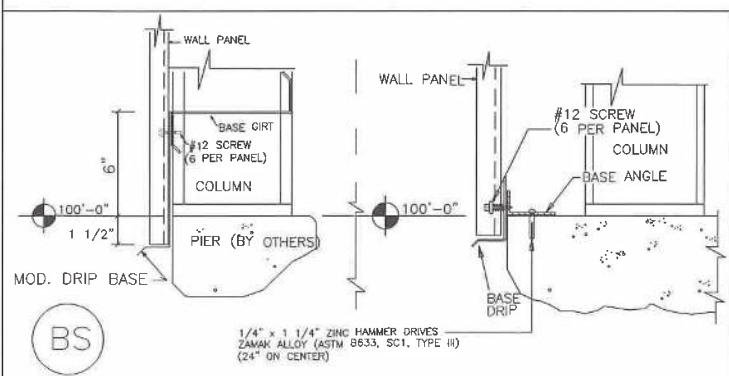
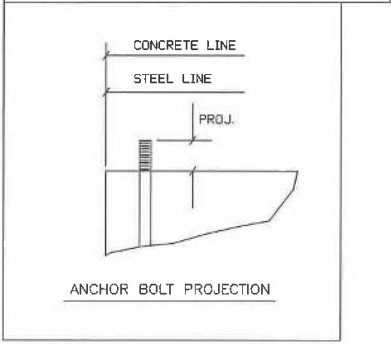
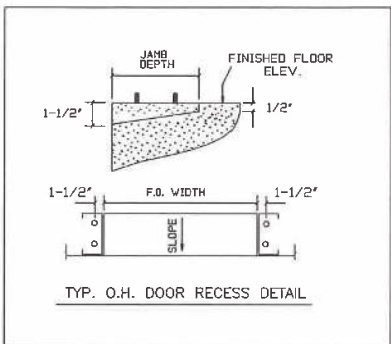
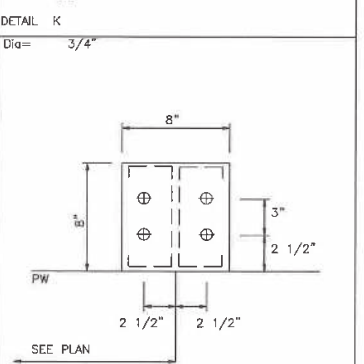
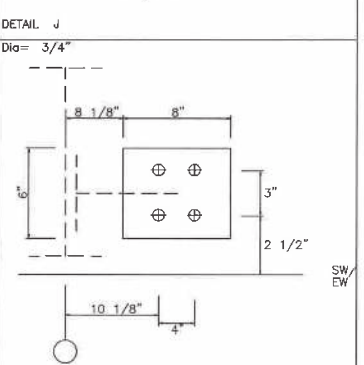
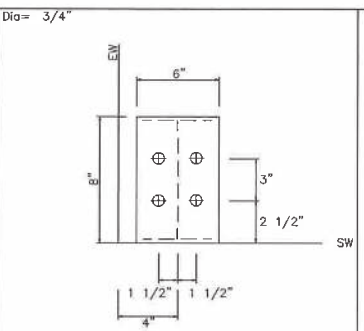
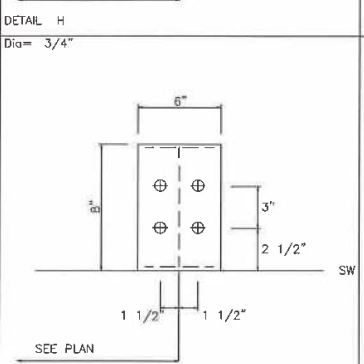
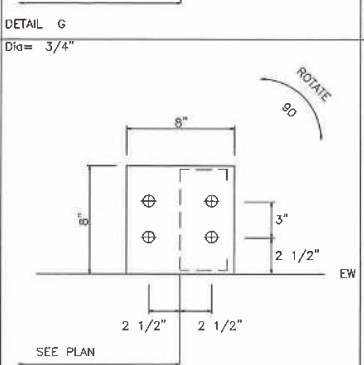
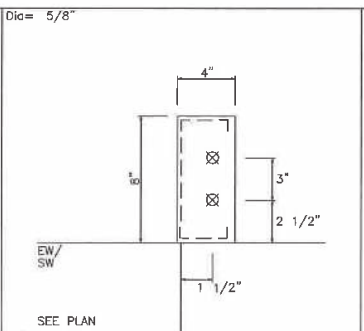
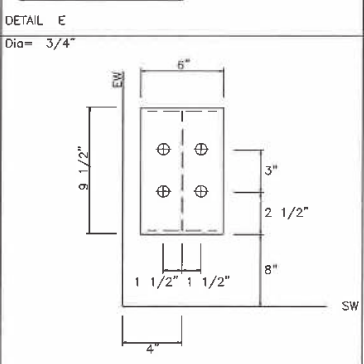
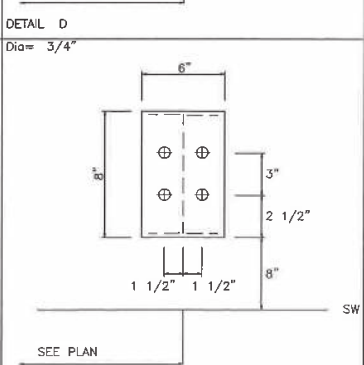
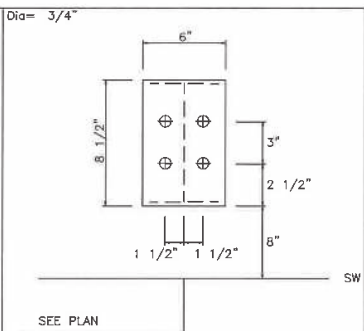
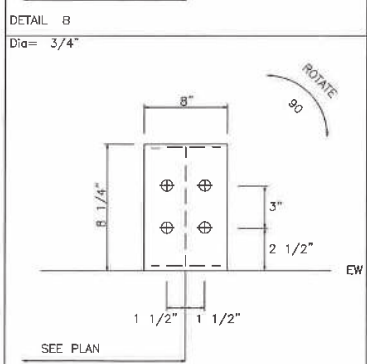


⊗ Dia= 5/8"
⊕ Dia= 3/4"

ANCHOR BOLT PLAN
NOTE: All Base Plates @ 100'-0" (Unless Noted)

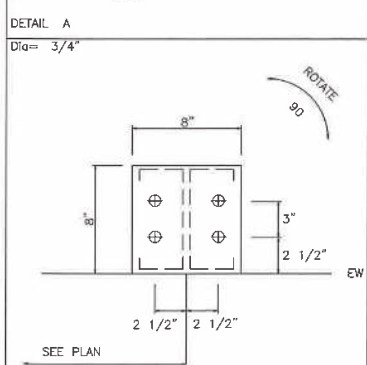


ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
TECHNOLOGIST:				
SPENCER TAYLOR				
JOB NO:		7733		DATE:
				11/23/22
LOCATION:				
LAKE CITY, FL 32025				
DRAWING NAME:				
ANCHOR BOLT LAYOUT				
CHECKING NO:	DRAWN BY:	CHECKED BY:	SCALE:	
PAGE 1	DAR	SPW	NONE	

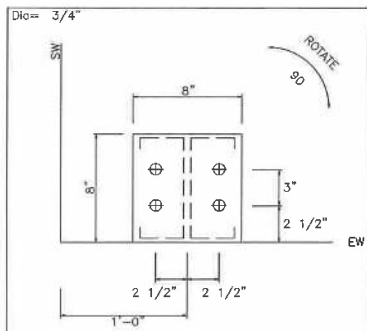

ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
JOB NO: 7733		DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING NAME: ANCHOR BOLT DETAILS				
ISSUED BY: PAGE 1.1		DRAWN BY: DAR	CHECKED BY: SPW	SCALE: NONE

FRAME LINES: 2 3 4 5 6 7

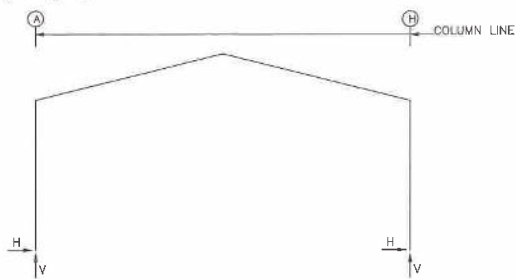

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frm Line	Col Line	Anc. Bolt Qty	Dia	Base Plate (in) Width	Length	Thick	Grout (in)
2	A	4	0.750	6.000	8.500	0.375	0.0
2	H	4	0.750	6.000	8.500	0.375	0.0

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frm Line	Col Line	Anc. Bolt Qty	Dia	Base Plate (in) Width	Length	Thick	Grout (in)
3	A	4	0.750	6.000	8.000	0.375	0.0
3	H	4	0.750	6.000	8.000	0.375	0.0

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frm Line	Col Line	Anc. Bolt Qty	Dia	Base Plate (in) Width	Length	Thick	Grout (in)
4*	A	4	0.750	6.000	8.000	0.500	0.0
4*	H	4	0.750	6.000	8.000	0.500	0.0

4* Frame lines: 4 5 6

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frm Line	Col Line	Anc. Bolt Qty	Dia	Base Plate (in) Width	Length	Thick	Grout (in)
7	A	4	0.750	6.000	9.500	0.375	0.0
7	H	4	0.750	6.000	9.500	0.375	0.0

ENDWALL COLUMN: ANCHOR BOLTS & BASE PLATES

Frm Line	Col Line	Anc. Bolt Qty	Dia	Base Plate (in) Width	Length	Thick	Grout (in)
1	A	4	0.750	8.000	8.000	0.375	0.0
1	C	4	0.750	8.000	8.000	0.375	0.0
1	F	4	0.750	8.000	8.000	0.375	0.0
1	H	4	0.750	8.000	8.000	0.375	0.0
7	G	4	0.750	8.000	8.250	0.250	0.0
7	B	4	0.750	8.000	8.250	0.250	0.0

NOTE: THE FRAMING AT BOTH ENDWALLS IS NOT DESIGNED TO ACCOMMODATE FUTURE ADDITIONS. REACTIONS CORRESPONDING TO THESE FRAME LINES REFLECT LOADINGS FOR ACTUAL TRIBUTARY AREA AND ARE NOT INTENDED TO INCLUDE ANY FUTURE MODIFICATIONS UNLESS NOTED OTHERWISE.

RIGID FRAME: BASIC COLUMN REACTIONS (k)

Frame Line	Column Line	Dead		Collateral		Live		Wind_Left1		Wind_Right1		Wind_Left2	
		Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert
2	A	0.6	2.1	0.2	0.6	2.9	7.5	-3.2	-10.4	-4.1	-9.4	-1.5	-5.6
2	H	-0.6	2.1	-0.2	0.6	-2.9	7.5	4.1	-9.4	3.2	-10.4	2.3	-4.6
3	A	0.6	1.9	0.2	0.6	2.8	7.5	-9.2	-14.2	0.7	-8.5	-7.8	-7.6
3	H	-0.6	2.5	-0.2	0.8	-2.7	10.7	-4.3	-9.3	5.6	-16.8	-1.2	-2.6
4*	A	0.6	1.9	0.2	0.6	2.8	7.4	-10.7	-15.5	-0.4	-9.4	-7.5	-7.2
4*	H	-0.6	3.0	-0.2	1.0	-2.7	12.0	-6.1	-10.9	4.3	-19.7	-0.6	-2.3
7	A	0.4	1.6	0.1	0.3	1.2	3.9	-4.3	-8.1	1.3	-4.7	-4.7	-5.6
7	H	-0.4	1.6	-0.1	0.3	-1.2	3.9	-1.3	-4.7	4.3	-8.1	-1.0	-2.2

Frame Line	Column Line	Wind_Right2	Wind_Long1	Wind_Long2	Seismic_Left	Seismic_Right					
		Horiz	Vert	Horiz	Vert	Horiz	Vert				
2	A	-2.3	-4.8	-3.0	-10.1	-4.0	-8.9	-0.1	0.1	0.1	0.1
2	H	1.5	-5.6	4.0	-9.9	3.0	-10.1	-0.1	0.1	-0.1	-0.1
3	A	2.0	-1.9	-1.2	-11.9	-2.2	-10.7	-0.1	-0.1	0.1	0.1
3	H	8.8	-10.0	-2.3	-11.4	-3.4	-12.6	-0.2	0.1	0.2	-0.1
4*	A	2.7	-1.1	-3.1	-13.6	-4.2	-12.4	-0.2	-0.1	0.2	0.1
4*	H	9.8	-11.1	-4.7	-13.8	-5.7	-15.0	-0.2	0.2	-0.1	-0.1
7	A	1.0	-2.2	0.7	-5.3	0.1	-4.6	-0.1	-0.1	0.1	0.1
7	H	4.7	-5.6	-0.1	-4.6	-0.7	-5.3	-0.1	0.1	0.1	-0.1

4* Frame lines: 4 5 6

4* Frame lines: 4 5 6

ENDWALL COLUMN: BASIC COLUMN REACTIONS (k)

Frm Line	Col Line	Dead Horiz	Dead Vert	Live Horiz	Live Vert	Wind Left1 Horiz	Wind Left1 Vert	Wind Right1 Horiz	Wind Right1 Vert	Wind Left2 Horiz	Wind Left2 Vert	Wind Right2 Horiz	Wind Right2 Vert	Wind Press Horiz	Wind Suct Horiz	Wind Long1 Horiz	Wind Long1 Vert	Wind Long2 Horiz	Wind Long2 Vert	Seis Left Horiz	Seis Left Vert
1	A	0.3	0.1	1.4	-1.4	-1.6	-0.5	-0.7	-1.4	1.6	-2.2	-1.5	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
1	C	0.9	0.3	4.9	-5.4	-3.2	-4.0	-1.8	-3.5	4.0	-4.5	-2.8	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
1	F	0.9	0.3	4.9	-5.4	-3.2	-4.0	-1.8	-3.5	4.0	-4.5	-2.8	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
1	H	0.3	0.1	1.4	-1.6	-1.4	-0.7	-0.5	-1.4	1.6	-1.5	-2.2	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	
7	G	0.4	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.5	0.5	0.0	0.0	0.0	0.0	0.0	0.0
7	B	0.4	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	0.0	-0.5	0.5	0.0	0.0	0.0	0.0	0.0	0.0

Frm Line	Col Line	Seis Right Horiz	Seis Right Vert
1	A	0.0	0.0
1	C	0.0	0.0
1	F	0.0	0.0
1	H	0.0	0.0
7	G	0.0	0.0
7	B	0.0	0.0

ANCHOR BOLT SUMMARY

Qty	Locate	Dia (in)	Type	Projection (in)
12	Jamb	5/8"	A307	1.50
24	Endwall	3/4"	GR36	1.50
48	Frame	3/4"	GR36	2.50
8	PC	3/4"	GR36	1.50

BUILDING BRACING REACTIONS

Wall Loc	Col Line	Col Line	± Reactions (k) Horiz	± Reactions (k) Vert	Panel Shear (lb/ft) Wind	Panel Shear (lb/ft) Seis	Note
L_EW	1	C,F	2.7	3.0	0.2	0.2	
F_SW	3,4	5,6	3.4	2.5	0.5	0.4	
R_EW	7	A	4.7	3.4	0.7	0.5	(h)
B_SW	5,6						

(h) Rigid frame at endwall

NOTES FOR REACTIONS

- All loading conditions are examined and only maximum/minimum H or V and the corresponding H or V are reported.
- Positive reactions are as shown in the sketch. Foundation loads are in opposite directions.
- Bracing reactions are in the plane of the brace with the H pointing away from the braced bay. The vertical reaction is downward.
- Building reactions are based on the following building data:
 - Width (ft) = 50.0
 - Length (ft) = 180.0
 - Eave Height (ft) = 20.0/ 20.0
 - Roof Slope (Rise/12) = 3.0/ 3.0
 - Dead Load (psf) = 2.0
 - Collateral Load (psf) = 1.0
 - Roof Live Load (psf) = 20.0
 - Frame Live Load (psf) = 12.0
 - Wind Speed (mph) = 110.0
 - Wind Code = FBC 20 (IBC 18)
 - Exposure = B
 - Enclosed/Open/Partial = ENCLOSED
 - Importance Wind = 1.00
 - Importance Seismic = 1.00
 - Seismic Zone = B
 - Seismic Coeff (Fa/Ss) = 0.14

BUILDING "A"

BUILDINGS AND MORE

SUBMITTED BY: SPENCER TAYLOR


JOB NO: 7733 DATE: 11/23/22

LOCATION: LAKE CITY, FL 32025

DRAWING NAME: ANCHOR BOLT REACTIONS

DRAWING NO: PAGE 1.2 DRAWN BY: DAR CHECKED BY: SPW SCALE: NONE

ISSUE	DET	CHK	DATE

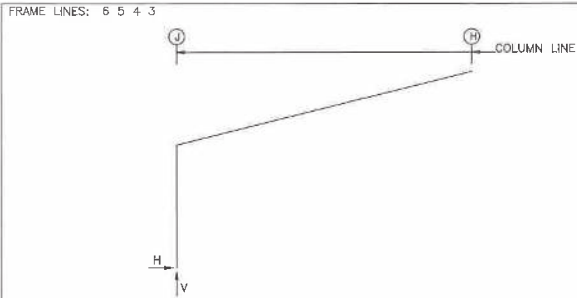

RIGID FRAME: BASIC COLUMN REACTIONS (k)

Frame Line	Column Line	Dead		Collateral		Live		Wind_Left1		Wind_Right1		Wind_Left2	
		Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert	Horiz	Vert
3	J	0.0	0.7	0.0	0.2	0.1	3.2	-0.2	-6.1	1.5	-5.2	-1.8	-0.8
6*	J	0.0	1.1	0.0	0.4	0.1	4.5	0.0	-10.7	2.5	-9.3	-3.1	-0.2
Frame Line	Column Line	Wind_Right2		Wind_Long1		Wind_Long2							
		Horiz	Vert	Horiz	Vert	Horiz	Vert						
3	J	-0.2	0.2	1.5	-5.9	1.5	-4.5						
6*	J	-0.5	1.1	2.8	-11.6	2.9	-8.8						
6* Frame lines:		6 5 4											

ENDWALL COLUMN: BASIC COLUMN REACTIONS (k)

Frame Line	Col Line	Dead Vert	Collat Vert	Live Vert	Wind_Left1 Vert	Wind_Right1 Vert	Wind_Left2 Vert	Wind_Right2 Vert	Wind Press Horiz	Wind Suct Horiz	Wind Suct Vert	Wind Long1 Vert	Wind Long2 Vert	Seis Left Vert
7	J	0.3	0.1	1.5	-1.9	-1.0	0.2	0.7	-1.0	1.1	-1.9	-1.5	0.0	0.0
7	I	0.7	0.2	4.6	-6.2	-4.7	-1.3	0.1	-2.6	2.8	-6.2	-4.4	0.0	0.0
Frame Line	Col Line	Seis Right Vert												
7	J	0.0												
7	I	0.0												

NOTES FOR REACTIONS

- All loading conditions are examined and only maximum/minimum H or V and the corresponding H or V are reported.
- Positive reactions are as shown in the sketch. Foundation loads are in opposite directions.
- Bracing reactions are in the plane of the brace with the H pointing away from the braced bay. The vertical reaction is downward.
- Building reactions are based on the following building data:

Width (ft)	=	30.0
Length (ft)	=	100.3
Eave Height (ft)	=	12.5/ 20.0
Roof Slope (Rise/12)	=	3.0
Dead Load (psf)	=	2.0
Collateral Load (psf)	=	1.0
Roof Live Load (psf)	=	20.0
Frame Live Load		
Min (psf)	=	12.0
Max (psf)	=	16.4
Wind Speed (mph)	=	119.0
Wind Code	=	FBC 20 (IBC 18)
Exposure	=	B
Enclosed/Open/Partial	=	PARTIALLY ENCLOSED
Importance Wind	=	1.00
Importance Seismic	=	1.00
Seismic Zone	=	B
Seismic Coeff (F _a S _s)	=	0.14

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frame Line	Col Line	Anc. Bolt Qty	Anc. Bolt Dia	Base Plate (in) Width	Base Plate (in) Length	Base Plate (in) Thick	Grout (in)
6*	J	4	0.750	6.000	8.000	0.625	0.0

6* Frame lines: 6 5 4

RIGID FRAME: ANCHOR BOLTS & BASE PLATES

Frame Line	Col Line	Anc. Bolt Qty	Anc. Bolt Dia	Base Plate (in) Width	Base Plate (in) Length	Base Plate (in) Thick	Grout (in)
3	J	4	0.750	6.000	8.000	0.375	0.0

ENDWALL COLUMN: ANCHOR BOLTS & BASE PLATES

Frame Line	Col Line	Anc. Bolt Qty	Anc. Bolt Dia	Base Plate (in) Width	Base Plate (in) Length	Base Plate (in) Thick	Grout (in)
7	J	4	0.750	8.000	8.000	0.375	0.0
7	I	4	0.750	8.000	8.000	0.250	0.0

ANCHOR BOLT SUMMARY

Qty	Locate	Dia (in)	Type	Projection (in)
Φ 8	Endwall	3/4"	GR36	1.50
Φ 16	Frame	3/4"	GR36	2.50
Φ 4	WindCol	3/4"	GR36	2.50

BUILDING BRACING REACTIONS

Wall Loc	Col Line	± Reactions (k) Wind Horiz	± Reactions (k) Seismic Horiz	Panel Shear (lb/ft) Wind	Panel Shear (lb/ft) Seis	Note
L_EW	7	Bracing Not Used		0	0	(e)
F_SW	H					(f)
R_EW	3					(g)
B_SW	J	5				(g)

(e) Bracing loads must be applied to supporting building
(f) Wind column at column line
(g) Rigid frame at endwall


WIND COLUMN REACTIONS

Wall Loc	Col Line	R/L	Load ID	± Reactions (k) Horiz	± Reactions (k) Vert	Moment (ft-k)	Anc. Bolt Qty	Anc. Bolt Dia	Base Plate (in) Width	Base Plate (in) Length	Base Plate (in) Thick
B_SW	J	5	L Wind Seismic	1.8	21.2	21.2	4	0.750	6.000	8.000	0.375
				0.7	7.9	7.9					



NOTE: THE FRAMING AT BOTH ENDWALLS IS NOT DESIGNED TO ACCOMMODATE FUTURE ADDITIONS. REACTIONS CORRESPONDING TO THESE FRAME LINES REFLECT LOADINGS FOR ACTUAL TRIBUTARY AREA AND ARE NOT INTENDED TO INCLUDE ANY FUTURE MODIFICATIONS UNLESS NOTED OTHERWISE.

ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
VOP NO: 7733		DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING NAME: ANCHOR BOLT REACTIONS				
DRAWING NO: PAGE 1.3	DRAWN BY: DAR		CHECKED BY: SPW	SCALE: NONE

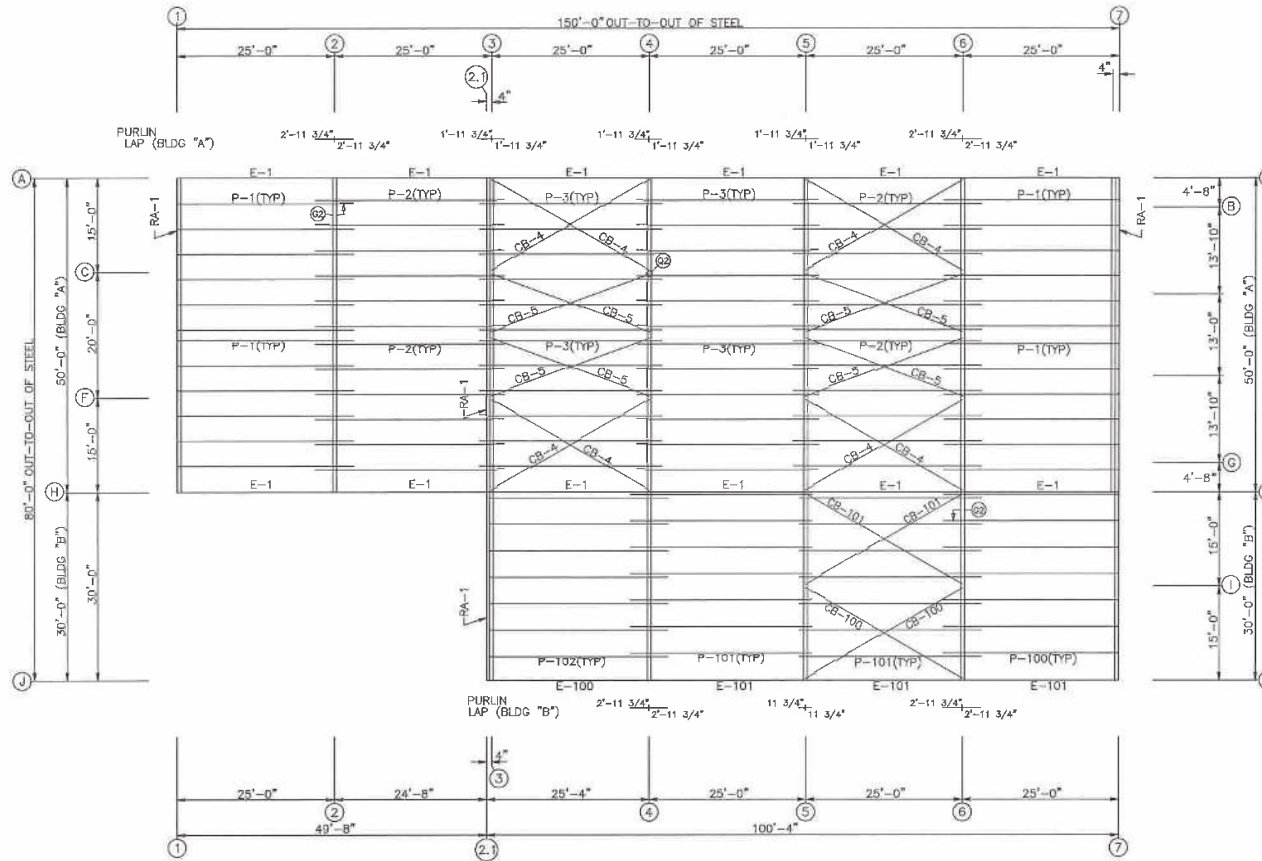

MEMBER TABLE			
ROOF PLAN			
MARK	PART	LENGTH	
7733-A			
P-1	8x25Z14	27'-11"	1/2"
P-2	8x25Z16	29'-11"	1/2"
P-3	8x25Z16	28'-11"	1/2"
E-1	8LE14@3	24'-11"	1/2"
CB-4	1/4 CBL	29'-0"	
CB-5	1/4 CBL	27'-4"	
7733-B			
P-100	8x25Z14	27'-11"	1/2"
P-101	8x25Z14	28'-11"	1/2"
P-102	8x25Z14	28'-3"	1/2"
E-100	8LE14@3	25'-3"	1/2"
E-101	8LE14@3	24'-11"	1/2"
CB-100	1/4 CBL	29'-3"	
CB-101	1/4 CBL	29'-7"	


ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
DESIGNER:				
SPENCER TAYLOR				
JOB NO:	7733	DATE:		11/23/22
LOCATION:				
LAKE CITY, FL 32025				
DRAWING NAME:				
ROOF FRAMING LAYOUT				
DRAWING NO:	PAGE 2	DRAWN BY:	CHECKED BY:	SCALE
		SPW		NONE

SPURCE BOLT TABLE						
MARK	Qty	Top	Bot	int	TYPE	DIA Length
SP-1	4	4	0	A325	5/8"	2"

BASE PLATE TABLE			
COL MARK	PLATE SIZE	Width	THICK Length
BP-1	6"	3/8"	8 1/2"

FLANGE BRACES: (1) One Side; (2) Two Sides
 FBxxA(1): xx=length(in)
 A - L2x2x14

MEMBER TABLE						
MARK	Weight	Web Depth	Web PLATE	Outside Flange	Inside Flange	
		Start/End	THICK Length	W x Thk x Length	W x Thk x Length	W x Thk x Length
RF1-1	495	7.5/10.4	0.188 4'-10 11/16"	6 x 1/4" x 18'-5 1/8"	6 x 1/2" x 17'-10 3/4"	
RF1-2	381	10.4/18.0	0.188 14'-11"	6 x 1/4" x 2'-3"	5 x 1/4" x 20'-0"	
		18.0/10.0	0.135 13'-2 1/2"	5 x 1/4" x 20'-0"	5 x 1/4" x 15'-2 11/16"	
		10.0/10.0	0.135 10'-6 13/16"	5 x 1/4" x 3'-4 11/16"	5 x 1/4" x 10'-4 9/16"	

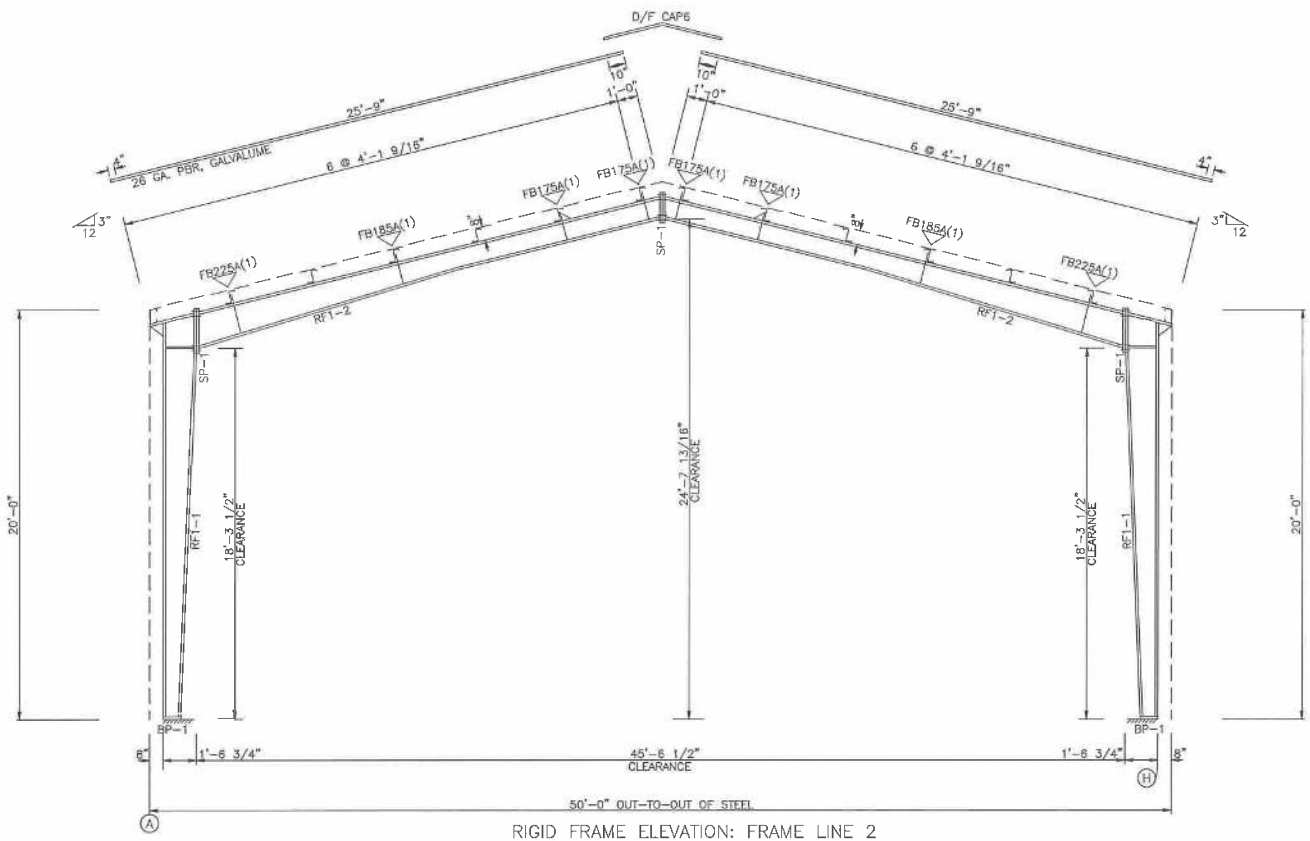

RIGID FRAME ELEVATION: FRAME LINE 2


BUILDING "A"			
BUILDINGS AND MORE			
CUSTOMER: SPENCER TAYLOR			
JOB NO:	7733	DATE:	11/23/22
LOCATION: LAKE CITY, FL 32025			
DRAWING NAME: RIGID FRAME CROSS SECTION			
DRAWING NO:	PAGE 2.1	DRAWN BY:	DAR
CHECKED BY:	SPW	SCALE:	NONE

ISSUE	DET	CHK	DATE

SPICE BOLT TABLE						
MARK	Qty	Top	Bot	Int	TYPE	DIA Length
SP-1	4	4	0	0	A325	5/8" 2"
SP-2	4	0	0	0	A325	5/8" 2"


BASE PLATE TABLE			
COL MARK	PLATE SIZE	Width	THICK Length
BP-0	6" 3/8" 8"		

FLANGE BRACES: (1) One Side; (2) Two Sides
 FBxxM(1); xx=length(in)
 A - L2x2x14

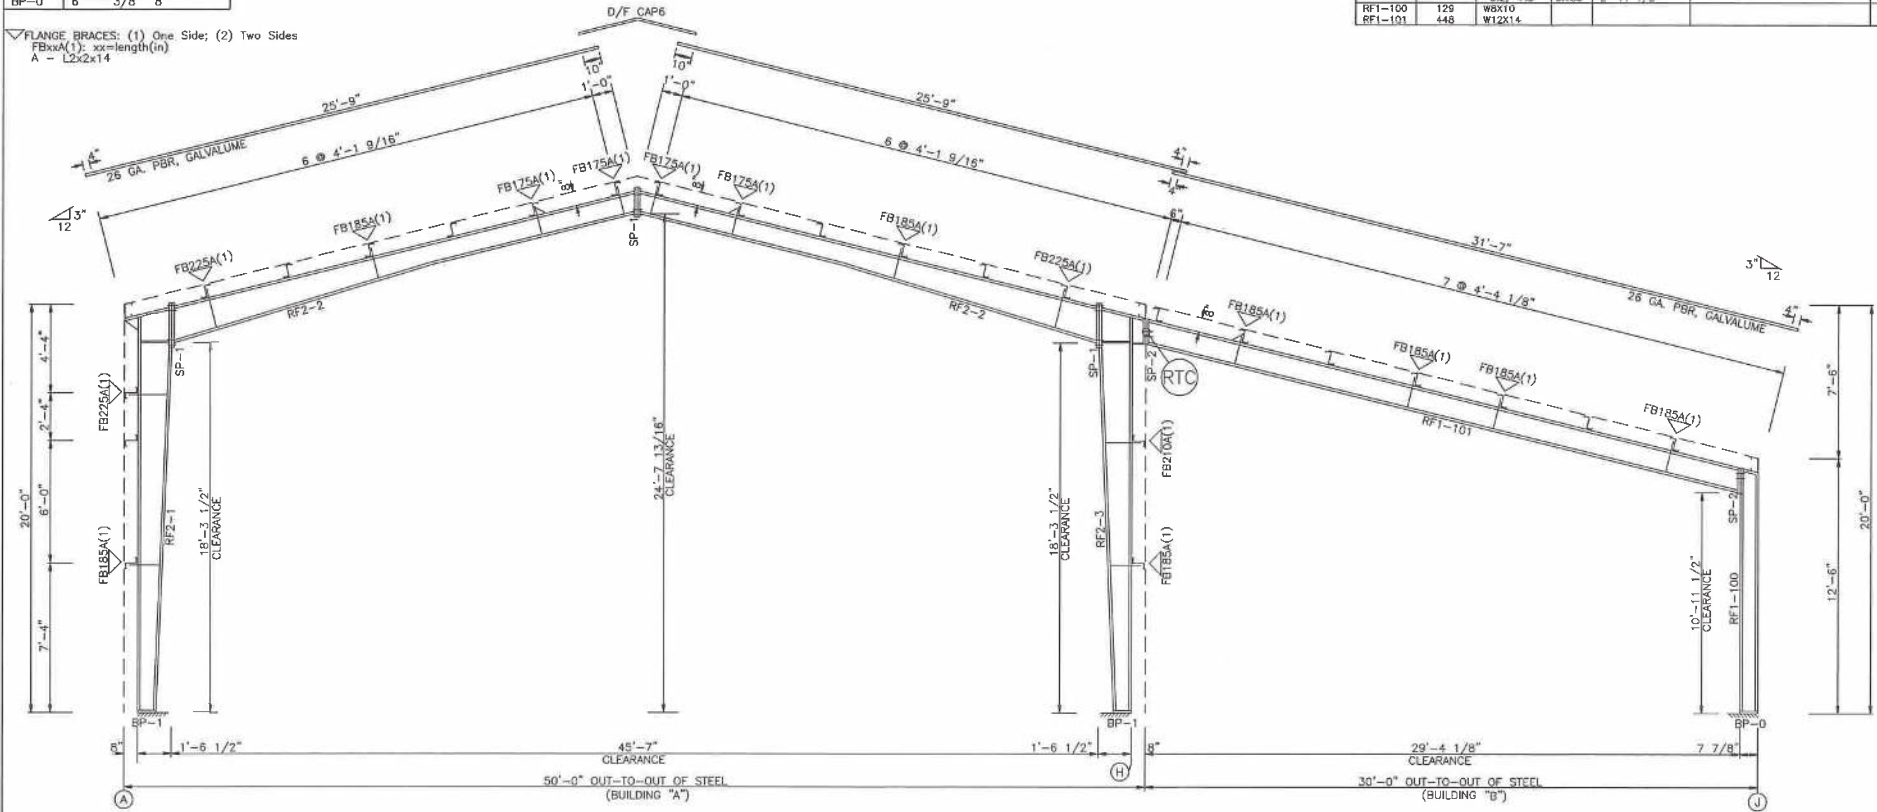

RIGID FRAME ELEVATION: FRAME LINE 3

NOTE: BUILDING "B" FRAMING IS NOT DESIGNED TO ACCOMMODATE ANY FUTURE EXPANSION.

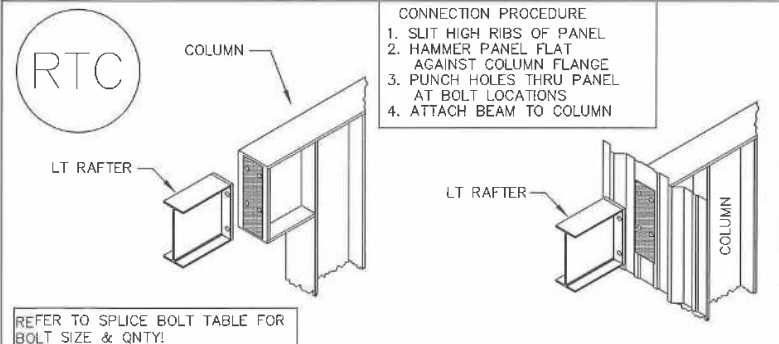

REFER TO SPICE BOLT TABLE FOR BOLT SIZE & QNTY!

MEMBER TABLE						
MARK	Weight	Web Depth	Web THICK	PLATE Length	Outside Flange W x Thk x Length	Inside Flange W x Thk x Length
RF2-1	339	7.5/ 9.2	0.135	2'-11 1/2"	5 x 1/4" x 19'-5 1/8"	5 x 1/4" x 17'-10 3/4"
		9.2/18.0	0.135	14'-11"	5 x 1/4" x 2'-3"	
		18.0/18.0	0.188	1'-11 3/16"		
RF2-2	382	18.0/10.0	0.135	1'-11 3/16"	5 x 1/4" x 20'-0"	5 x 1/4" x 13'-2 11/16"
		18.0/10.0	0.135	1'-11 3/16"	5 x 1/4" x 10'-4 3/16"	5 x 1/4" x 10'-4 3/16"
RF2-3	352	18.0/18.0	0.188	1'-11 3/16"	5 x 1/4" x 2'-2 3/4"	5 x 1/4" x 17'-10 3/4"
		18.0/ 9.2	0.135	14'-11"	5 x 1/4" x 19'-5 1/8"	
		9.2/ 7.5	0.135	7'-11 1/2"		
RF1-100	129	W8x10				
RF1-101	448	W12x14				

ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
JOB NO: 7733		DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING TITLE: RIGID FRAME CROSS SECTION				
DRAWING NO: PAGE 2.2		DESIGNED BY: DAR	CHECKED BY: SPW	SCALE: NONE

BASE PLATE TABLE			
COL MARK	PLATE SIZE		
	Width	THICK	Length
BP-1	6"	1/2"	8"
BP-2	6"	5/8"	8"

▽ FLANGE BRACES: (1) One Side; (2) Two Sides
FBxxA(1): xx=length(in)
A = 12x2x14




ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER:				
SPENCER TAYLOR				
JOB NO.		DATE		
7733		11/23/22		
LOCATION:				
LAKE CITY, FL 32025				
DRAWING NAME:				
RIGID FRACTION CROSS SECTION				
APPROVED BY:	DATE:	DESIGNED BY:	SCALE:	
PAGE 2.3	DAR	SPW	NONE	

BASE PLATE TABLE			
COL MARK	PLATE SIZE		
	Width	THICK	Length
BP-1	6"	3/8"	9 1/2"

WEVER TABLE					
MARK	Weight	Web Depth	Web PLATE	Outside Flange	Inside Flange
		Start/End	HICK	W x Thk x Length	W x Thk x Length
RF4-1	287	9.0/9.0	0.135	5 x 1/4" x 18'-5 1/8"	5 x 1/4" x 18'-5 7/16"
		9.0/9.0	0.135	5 x 1/4" x 1'-5 11/16"	
		9.0/9.0	0.250	1'-2"	
RF4-2	354	9.0/9.0	0.135	5 x 1/4" x 20'-0"	5 x 1/4" x 20'-0"
		9.0/9.0	0.135	5 x 1/4" x 1'-13 1/16"	
		9.0/9.0	0.135	5 x 1/4" x 1'-13 1/16"	


▽ FLANGE BRACES: (1) One Side; (2) Two Sides
FBxxA(1): xx=length(in)
A - L2x2x14

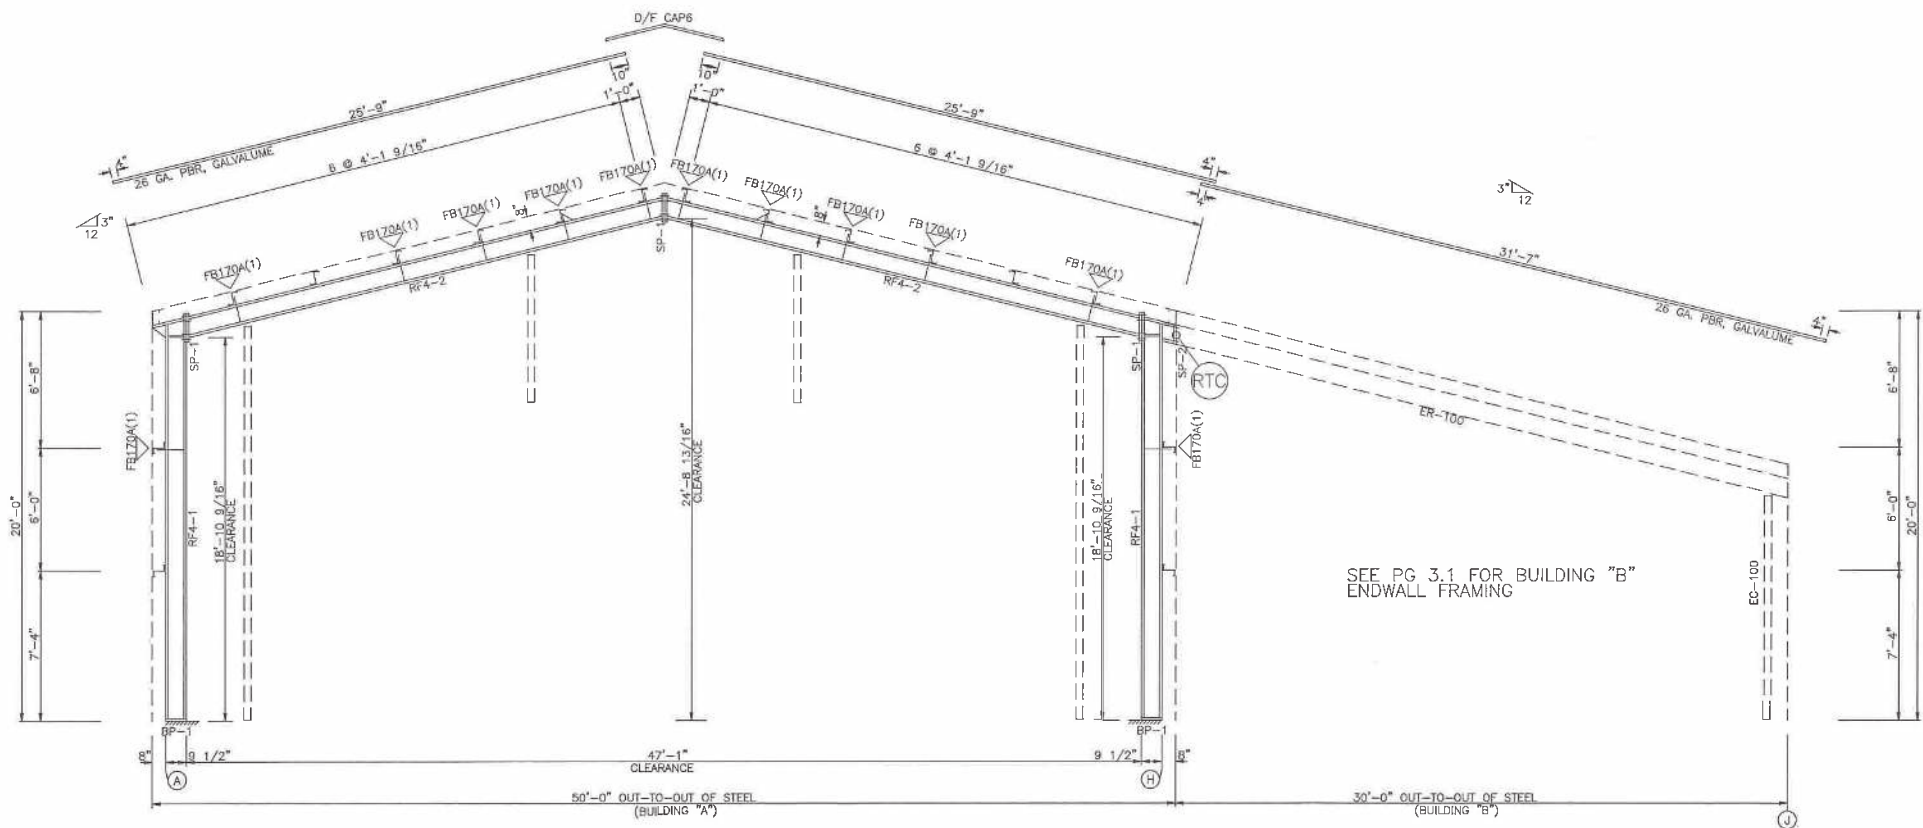


RIGID FRAME ELEVATION: FRAME LINE 7

NOTE: THE FRAMING AS DEPICTED ABOVE IS NOT DESIGNED TO ACCOMMODATE ANY FUTURE EXPANSION.

ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
JOB NO. 7733		DATE 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING NAME: RIGID FRAME CROSS SECTION				
DRAWN BY: PAGE	2.4	CHECKED BY: DAR	SPW	SCALE: NONE

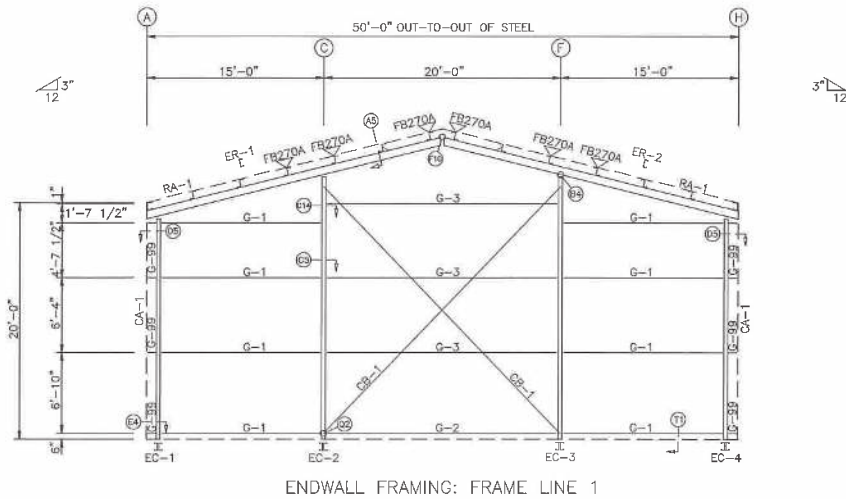


ENDWALL FRAMING: FRAME LINE 1

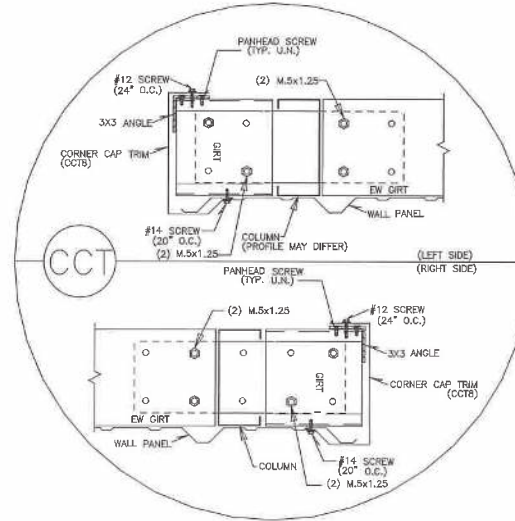

BOLT TABLE				
FRAME LINE 1				
LOCATION	QUAN	TYPE	DIA	LENGTH
ER-1/ER-2	8	A325	5/8"	2"
Columns/Rof	2	A325	5/8"	2"

TRIM TABLE				
FRAME LINE 1				
ID	PART	LENGTH	DETAIL	
1	MOD BASE TRM	20'-3"	TRIM_99	
2	MOD BASE TRM	10'-3"	TRIM_99	
3	CCT8	20'-2"	CCT	
4	RAKE TRM	20'-3"	TRIM_3	
5	RAKE TRM	5'-10"	TRIM_3	
6	PEAK BOX	1'-4"	TRIM_4	

MEMBER TABLE			
FRAME LINE 1			
MARK	PART	LENGTH	
EC-1	8X7DC16	18'-8 1/2"	
EC-2	8X7DC12	22'-2 1/2"	
EC-3	8X7DC12	22'-2 1/2"	
EC-4	8X7DC16	18'-8 1/2"	
ER-1	8X35C12	25'-9"	
ER-2	8X35C12	25'-9"	
G-1	8x25Z16	13'-3 1/2"	
G-2	8x25Z16	19'-3 1/2"	
G-3	8x25Z14	19'-3 1/2"	
G-99	8x25Z16	7 1/2"	
CB-1	1/4 CBL	29'-10"	

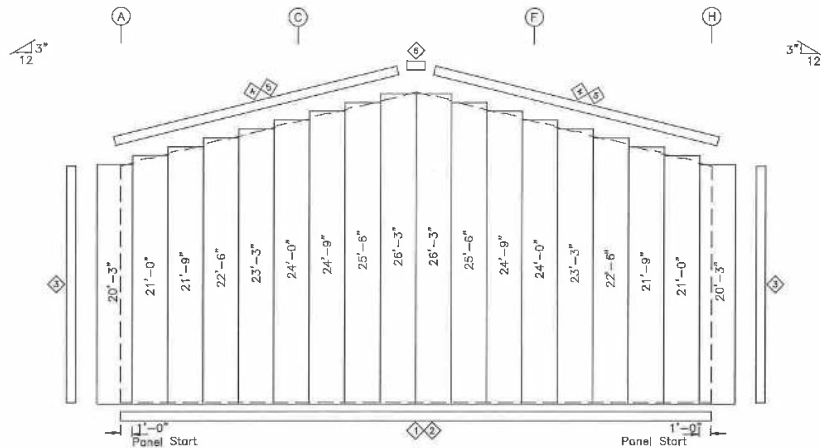


ENDWALL SHEETING & TRIM: FRAME LINE 1

PANELS: 26 Ga. PBR - CHARCOAL GRAY


BUILDING "A"			
BUILDINGS AND MORE			
CUSTOMER:			
SPENCER TAYLOR			
JOB NO:	7733	DATE:	11/23/22
LOCATION:			
LAKE CITY, FL 32025			
DRAWING NAME:			
FRAMING & SHEETING LAYOUT			
DRAWING NO:	PAGE 3	DRAWN BY:	SPW
		DAR	NONE

ISSUE	DET	CHK	DATE


NOTE: THE FRAMING AS DEPICTED ABOVE IS NOT DESIGNED TO ACCOMMODATE ANY FUTURE EXPANSION.

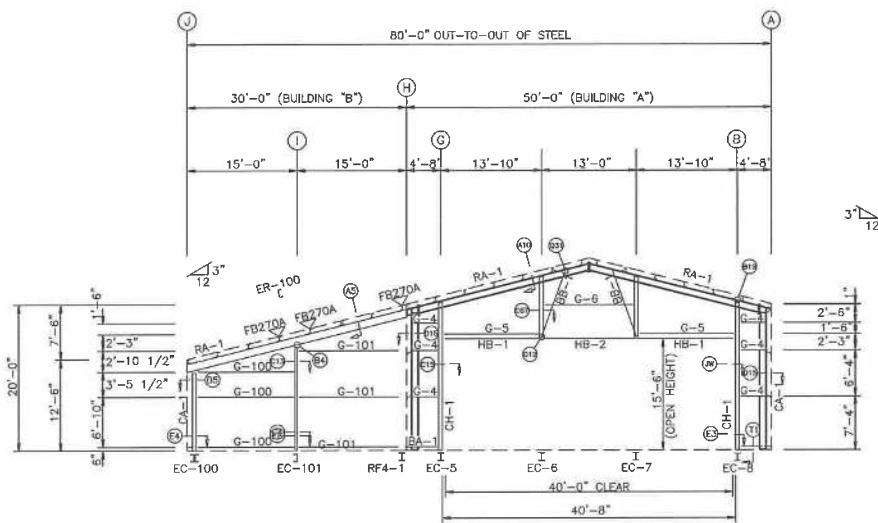

ENDWALL FRAMING: FRAME LINE 7

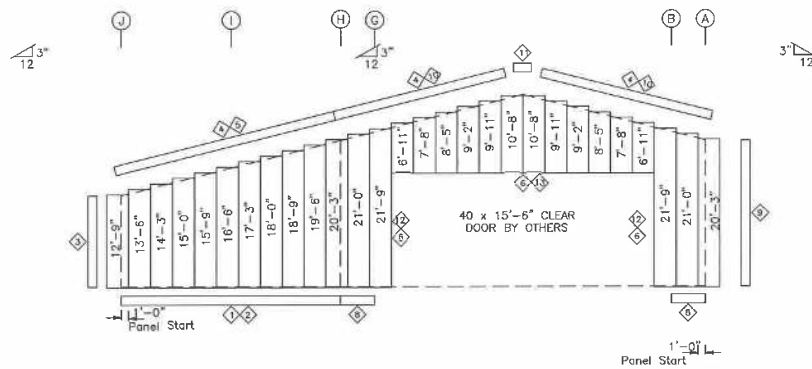

ENDWALL SHEETING & TRIM: FRAME LINE 7
PANELS: 26 Gg. PBR - CHARCOAL GRAY

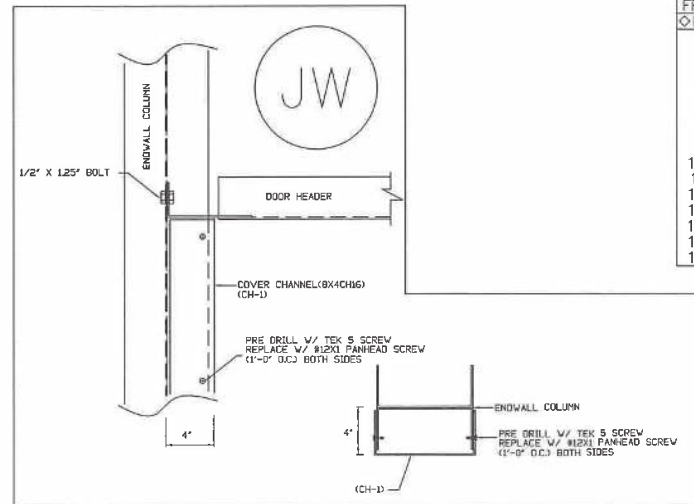

DOOR SHEETING & TRIM
PANELS: 26 Gg. PBR - CHARCOAL GRAY


BOLT TABLE				
FRAME LINE 7				
LOCATION	QUAN	TYPE	DIA	LENGTH
7733-A				
Columns/Raf	2	A325	5/8"	2"
Back Braces	1	A325	5/8"	2"
7733-B				
EC-100/ER-100	2	A325	5/8"	2"
EC-101/ER-100	2	A325	5/8"	2"
ER-100/RF4-1	2	A325	5/8"	2"

TRIM TABLE			
FRAME LINE 7			
QID	PART	LENGTH	DETAIL
1	MOD BASE TRM	20'-3"	TRIM_99
2	MOD BASE TRM	10'-3"	TRIM_99
3	CCT8	12'-8"	TRIM_5
4	RAKE TRM	20'-3"	TRIM_3
5	RAKE TRM	11'-0"	TRIM_3
6	R HEAD	13'-10"	TRIM_6
8	BASE TRM	4'-11"	TRIM_16
9	O/S CORN	20'-2"	TRIM_5
10	RAKE TRM	5'-10"	TRIM_3
11	PEAK BOX	1'-4"	TRIM_4
12	CT8	15'-6"	TRIM_11
13	CT8	13'-10"	TRIM_10
14	R JAMB	15'-8"	
15	R HEAD	20'-3"	
16	DGL DRIP	20'-3"	




MEMBER TABLE		
FRAME LINE 7		
MARK	PART	LENGTH
7733-A		
HB-1	8X35C16	13'-1 1/2"
HB-2	8X35C16	12'-3 1/2"
BB-1	T4x188	25'-3 3/8"
EC-5	W8X18	19'-5 15/16"
EC-6	W8X10	7'-5 7/16"
EC-7	W8X10	7'-5 7/16"
EC-8	W8X18	19'-5 15/16"
CH-1	8X4CH12	15'-6"
G-4	8x25Z16	2'-10"
G-5	8x25Z16	13'-1 1/2"
G-6	8x25Z16	12'-3 1/2"
7733-B		
EC-100	8X7DC16	11'-2 1/2"
EC-101	8X35C12	14'-8 1/2"
ER-100	8X35C12	30'-10 13/16"
G-100	8x25Z16	13'-3 1/2"
G-101	8x25Z16	14'-3 1/2"

NOTE: THE FRAMING AS DEPICTED ABOVE IS NOT DESIGNED TO ACCOMMODATE ANY FUTURE EXPANSION.


ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER:				
SPENCER TAYLOR				
JOB NO.		DATE		
7733		11/23/22		
LOCATION:				
LAKE CITY, FL 32025				
DRAWING NAME:				
FRAMING & SHEETING LAYOUT				
DESIGNED BY:	CHECKED BY:	SCALE:		
PAGE 3.1	DAR	SPW	NONE	

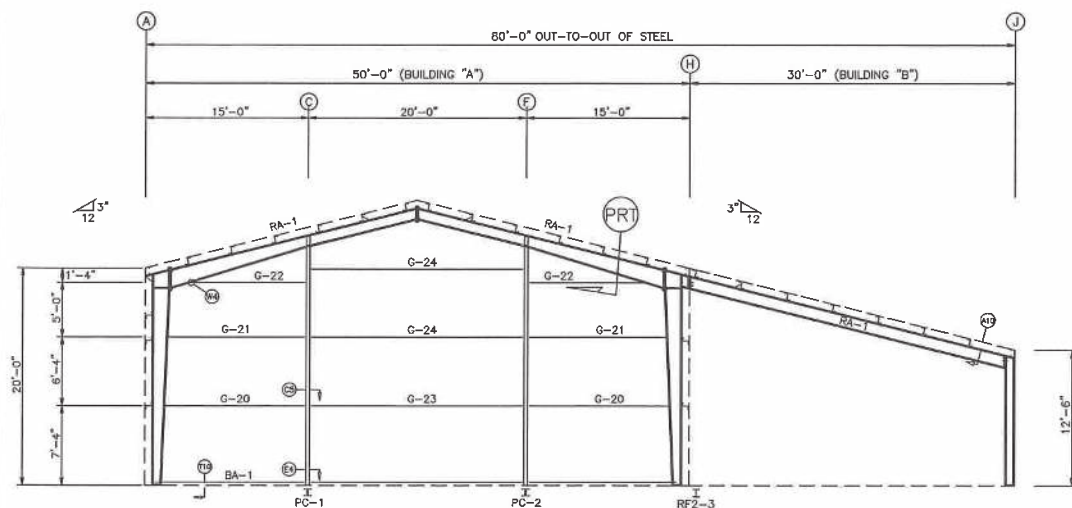

ENDWALL FRAMING: FRAME LINE 3

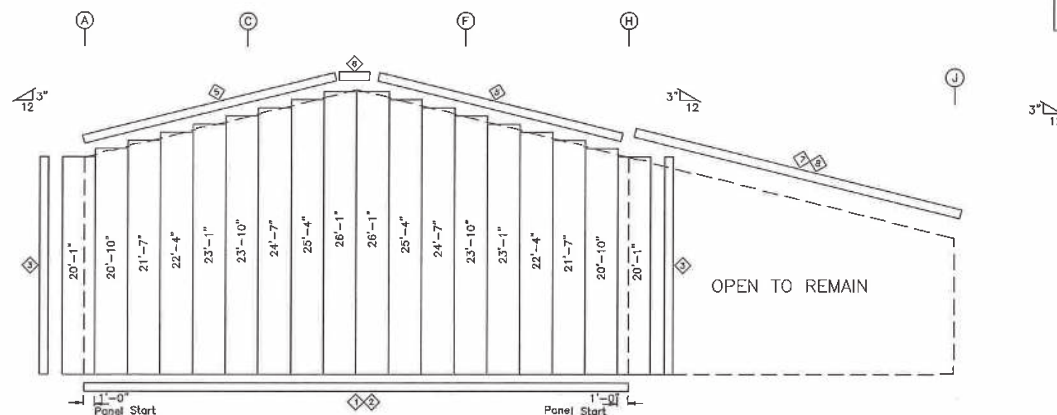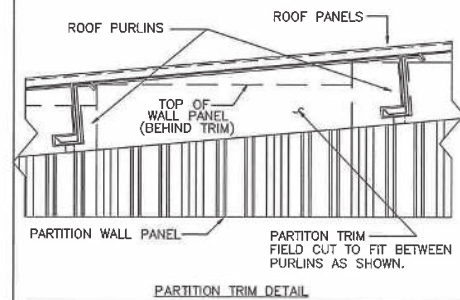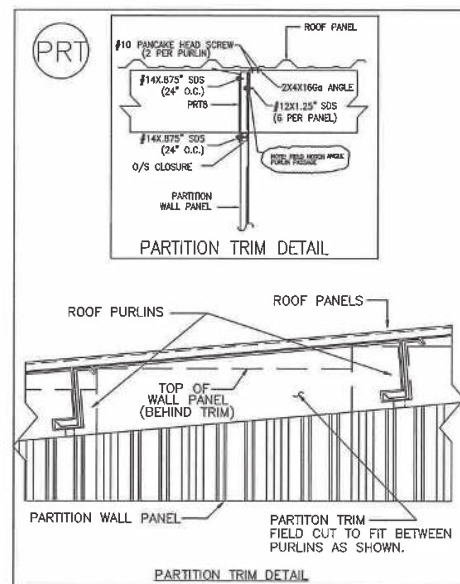


ENDWALL SHEETING & TRIM: FRAME LINE 2.1
PANELS: 26 Ga. PBR - CHARCOAL GRAY

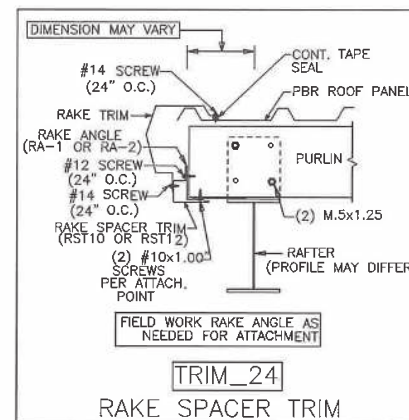

MEMBER TABLE FRAME LINE 3		
MARK	PART	LENGTH
PC-1	8X7DC12	21'-11 15/16"
PC-2	8X7DC12	21'-11 15/16"
G-20	8X25Z16	12'-7 1/2"
G-21	8X25Z16	12'-7 1/2"
G-22	8X25Z16	11'-1 1/2"
G-23	8X25Z12	19'-3 1/2"
G-24	8X25Z14	19'-3 1/2"


TRIM TABLE FRAME LINE 2.1		
ID	PART	LENGTH
1	BASE TRIM	20'-3"
2	BASE TRIM	10'-3"
3	O/S CORN	20'-2"
5	PRT8	5'-0"
6	PRT8	3'-0"
7	RAKE TRM	20'-3"
8	RAKE TRM	11'-0"

ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
CUSTOMER: SPENCER TAYLOR			
JOB NO. 7733	DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025			
DRAWING NAME: FRAMING & SHEETING LAYOUT			
WORKING TITLE: PAGE 3.2	WORK BY: DAR	CHECKED BY: SPW	SCALE: NONE

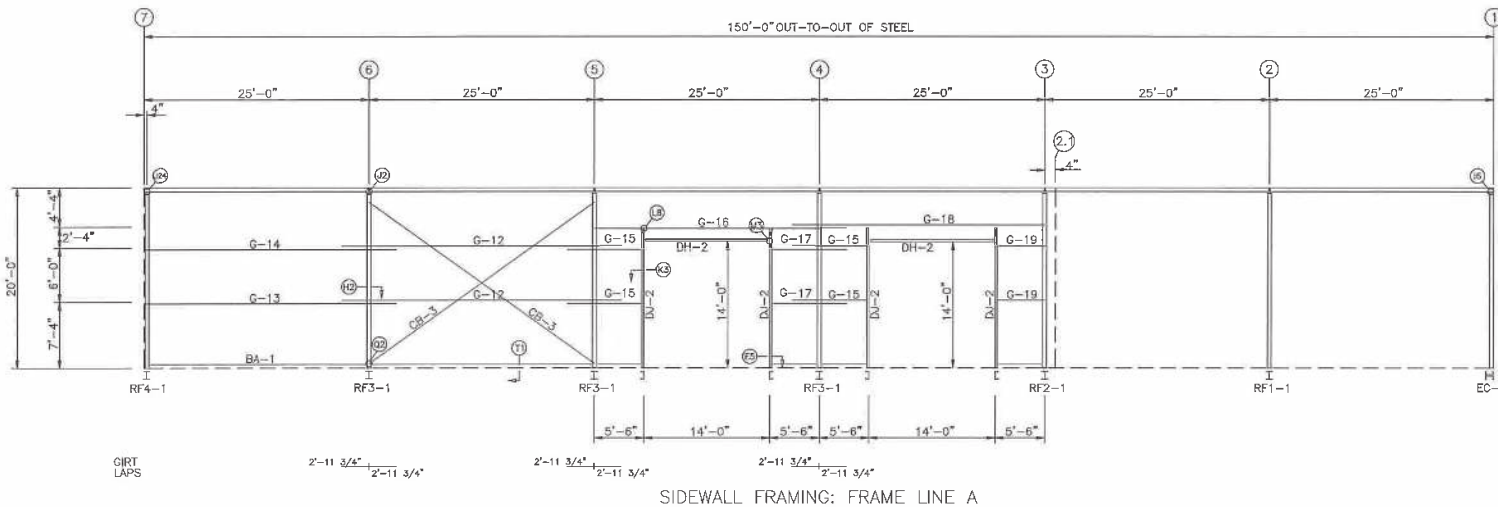

TRIM TABLE FRAME LINE A			
ID	PART	LENGTH	DETAIL
1	BASE TRM	20'-3"	TRIM_16
2	BASE TRM	15'-9"	TRIM_16
3	BASE TRM	11'-9"	TRIM_16
4	BASE TRM	5'-9"	TRIM_16
7	CUTTER	20'-3"	TRIM_1
8	CUTTER	10'-0"	TRIM_1
9	CUTEND L	1'-0"	TRIM_2
10	CORBOX L	1'-0"	TRIM_2
11	CUTEND R	1'-0"	TRIM_2
12	CORBOX R	1'-0"	TRIM_2
13	R JAMB	14'-3"	TRIM_8
14	R HEAD	14'-3"	TRIM_61
15	ECT8	20'-3"	ECT
16	ECT8	10'-3"	ECT

MEMBER TABLE FRAME LINE A		
MARK	PART	LENGTH
DJ-2	8X35C12	15'-8"
DH-2	8X35C16	14'-0"
G-12	8x25Z16	30'-11 1/2"
G-13	8x25Z14	27'-11 1/2"
G-14	8x25Z16	27'-11 1/2"
G-15	8x25Z16	8'-1 1/2"
G-16	8x25Z16	28'-3 1/2"
G-17	8x25Z16	8'-1 1/2"
G-18	8x25Z12	28'-3 1/2"
G-19	8x25Z16	5'-5 1/2"
CB-3	5/16 CBL	31'-10"

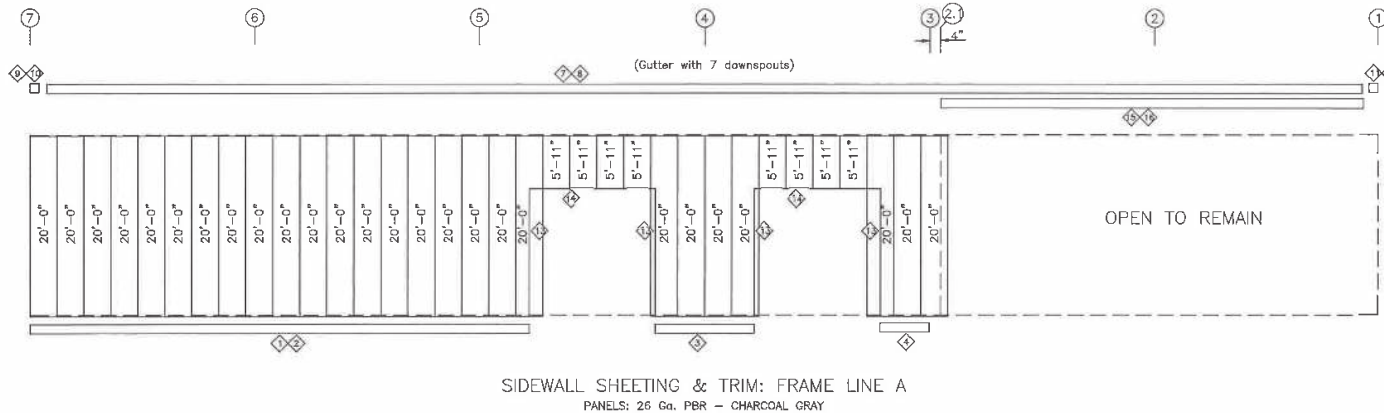

ALL VEHICULAR FRAMED OPENINGS SUPPLIED ON THIS PROJECT HAVE BEEN DESIGNED TO SUPPORT WIND LOADS NORMAL TO A DOOR SYSTEM, BASED ON THE STANDARD BUILDING CODE CRITERIA. THE VEHICULAR FRAMED OPENING HAS NOT BEEN DESIGNED FOR ANY ADDITIONAL MOMENT OR CATENARY FORCE FROM THE DOOR SYSTEM. ANY CHANGES TO THE INFORMATION SHOWN HERE WOULD REQUIRE AN ENGINEERING INVESTIGATION AND POSSIBLE BUILDING REINFORCEMENT.



15

BUILDING "A"			
BUILDINGS AND MORE			
OWNER: SPENCER TAYLOR			
JOB NO:	7733	DATE:	11/23/22
LOCATION: LAKE CITY, FL 32025			
DRAWING NAME: FRAMING & SHEETING LAYOUT			
DRAWING REV:	PAGE 4.1	DRAWN BY: DAR	CHECKED BY: SPW
		SCALE:	NONE

BOLT TABLE				
FRAME LINE J				
LOCATION	QUAN	TYPE	DIA	LENGTH
WF-100 - RF2-100	6	A325	5/8"	2"

TRIM TABLE			
FRAME LINE J			
ID	PART	LENGTH	DETAIL
2	GUTTER	20'-3"	TRIM_1
3	GUTTER	4"	TRIM_1
4	GUTEND L	1"	TRIM_2
5	CORBOX L	1'-0"	TRIM_2
6	GUTEND R	1"	TRIM_2
7	CORBOX R	1'-0"	TRIM_2

MEMBER TABLE		
FRAME LINE J		
MARK	PART	LENGTH
WF-100	B12541	10'-6"

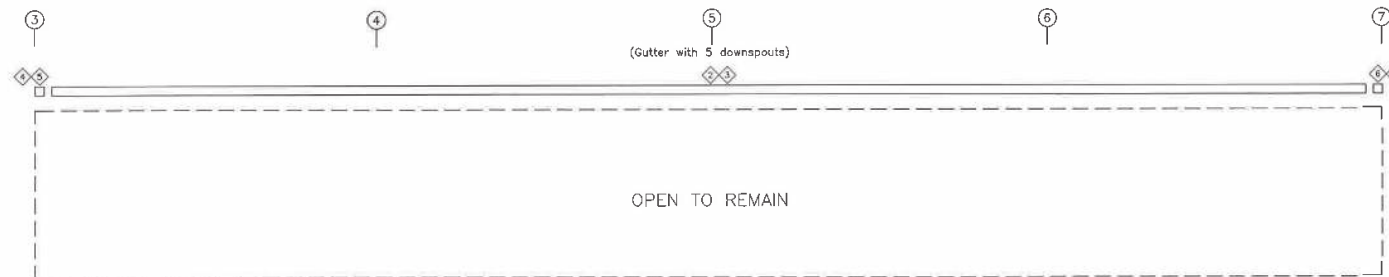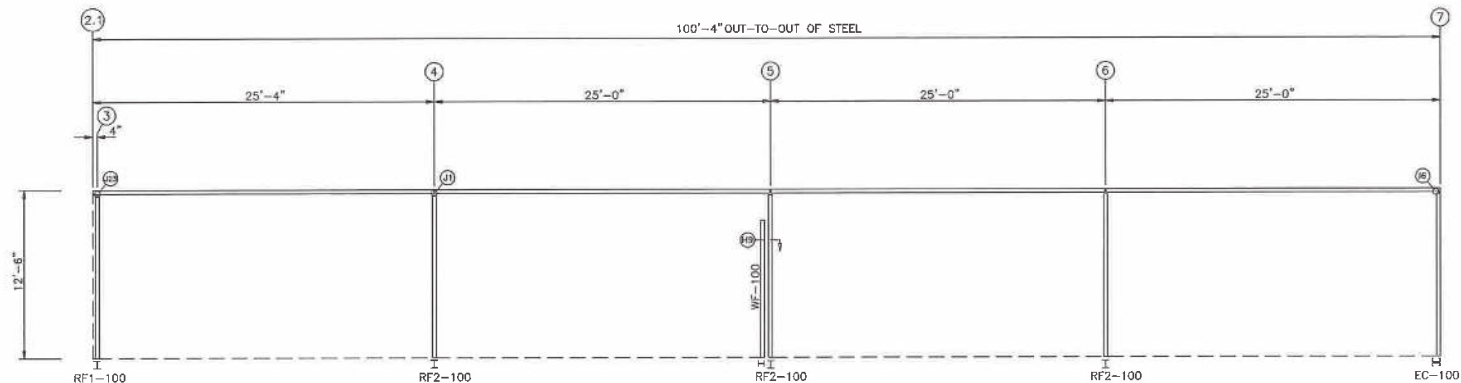


OPEN TO REMAIN

GENERAL NOTES:


MEMBER ID, format is (BABCD) or (BAABCD)
 B = member type (Builtup), A or AA = member depth in inches
 B = flange width in inches, except for (0 = 10 in, 2 = 12 in)
 C = flange thickness in 1/16 inch units
 D = web thickness (1 = 10 ga. Or 0.1345, 2 = 8 ga. or 0.1640, 3 = 3/16)

BUILDING "B"			
BUILDINGS AND MORE			
CUSTOMER:			
SPENCER TAYLOR			
JOB NO:		DATE:	
7733		11/23/22	
LOCATION:			
LAKE CITY, FL 32025			
DRAWING NAME:			
FRAMING & SHEETING LAYOUT			
DRAWN BY:		CHECKED BY:	DESIGNED BY:
PAGE 4.2		DAR	SPW
			SCALE:
			NONE


ISSUE	DET	CHK	DATE

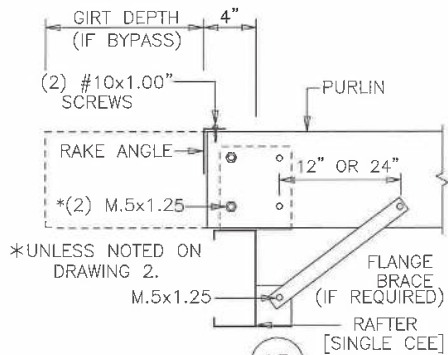


DETAIL A5
PURLIN TO ENDWALL RAFTER
NOTE: REFER TO "TYPICAL WASHER REQUIREMENTS" DETAIL

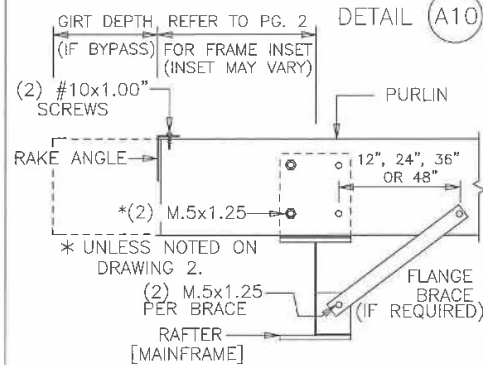


DETAIL A10
PURLIN TO ENDWALL RAFTER
NOTE: REFER TO "TYPICAL WASHER REQUIREMENTS" DETAIL

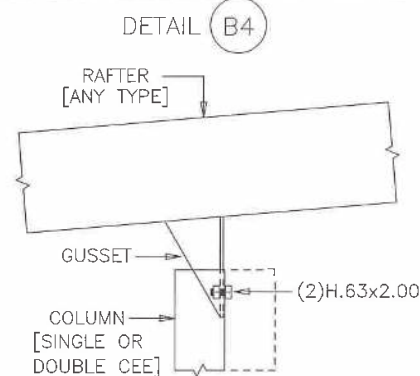


DETAIL B4
CEE COLUMN / RAFTER CONNECTION
*UNLESS NOTED ON EW FRAMING PLAN

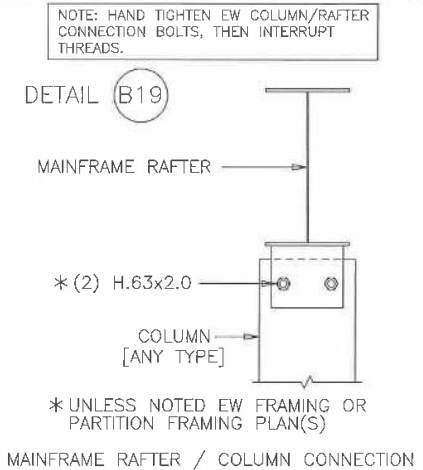


DETAIL B19
MAINFRAME RAFTER / COLUMN CONNECTION
NOTE: HAND TIGHTEN EW COLUMN/RAFTER CONNECTION BOLTS, THEN INTERRUPT THREADS.

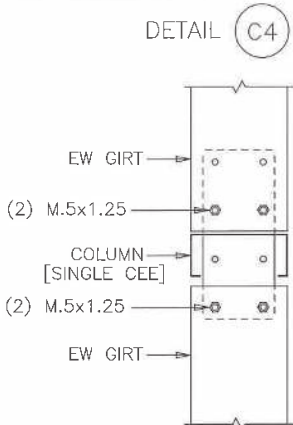


DETAIL C4
ENDWALL GIRTS TO INTERIOR COLUMN

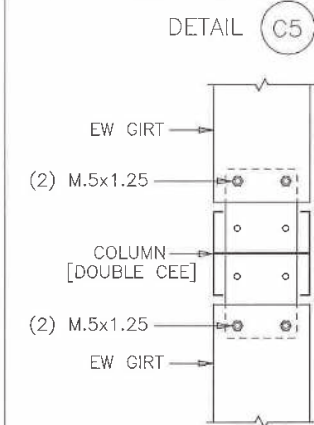

DETAIL C5
ENDWALL GIRTS TO INTERIOR COLUMN

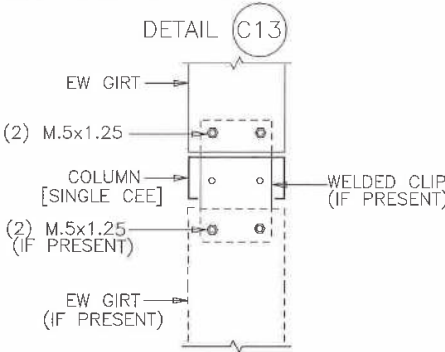


DETAIL C13
ENDWALL GIRT STOPPING AT COLUMN

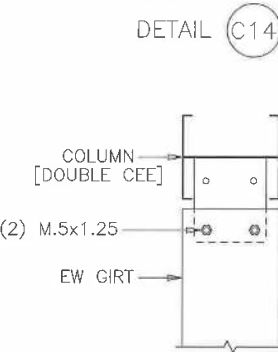

DETAIL C14
ENDWALL GIRT STOPPING AT COLUMN


ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
JOB NO: 7733		DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING NAME: FRAMING DETAILS				
DRAWING NO: PAGE 5		DRAWN BY: DAR	CHECKED BY: SPW	SCALE: NONE

DETAIL C15




ENDWALL GIRT STOPPING AT COLUMN

DETAIL D5

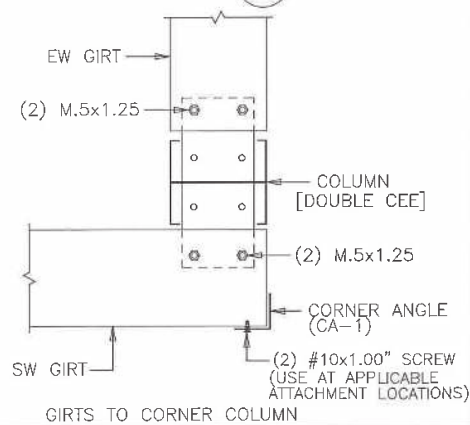


GIRTS TO CORNER COLUMN

DETAIL D15

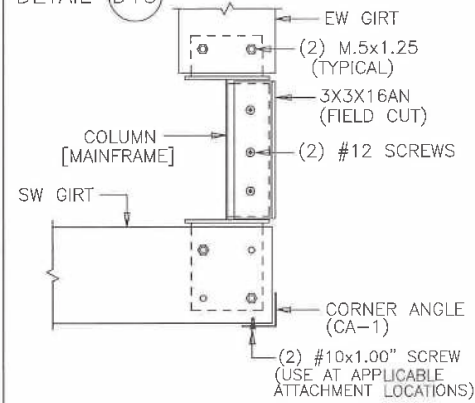


GIRT CONNECTIONS AT RIGID FRAME

DETAIL E3

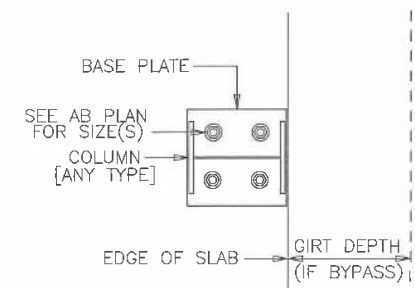


ENDWALL COLUMN BASE DETAIL

DETAIL E4

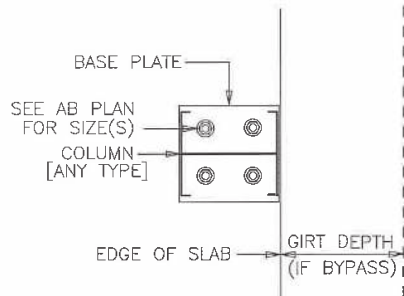


ENDWALL COLUMN BASE DETAIL

DETAIL E5

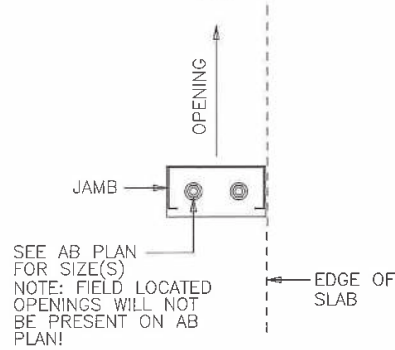


FRAMED OPENING JAMB BASE DETAIL

DETAIL E8

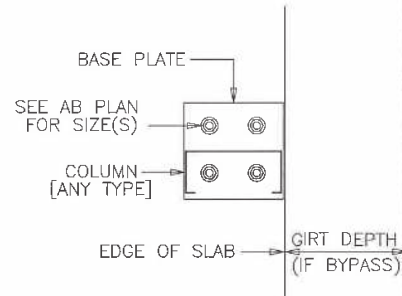









ENDWALL COLUMN BASE DETAIL

DETAIL F10

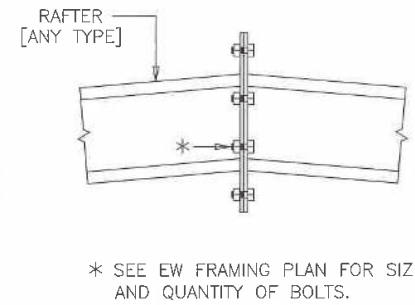


RAFTER DETAIL AT RIDGE

ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMERS				
SPENCER TAYLOR				
JOB NO.	7733	DATE	11/23/22	
LOCATION				
LAKE CITY, FL 32025				
DRAWING NAME:				
FRAMING DETAILS				
DRAWN BY:	PAGE 5.1	DESIGN BY:	CHECKED BY:	SCALE:
		DAR	SPW	NONE

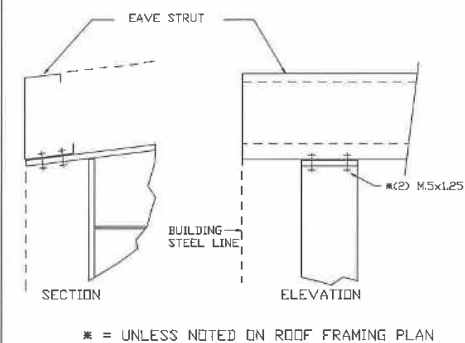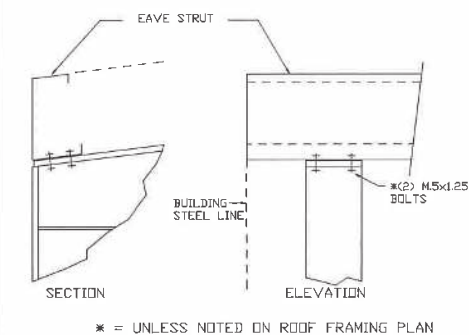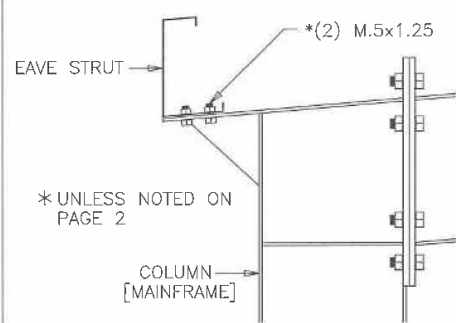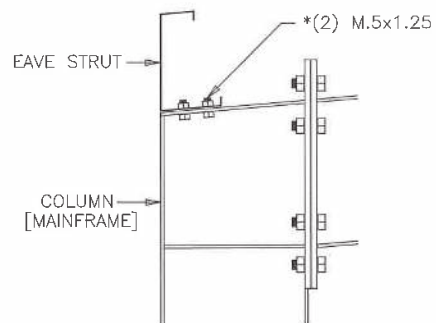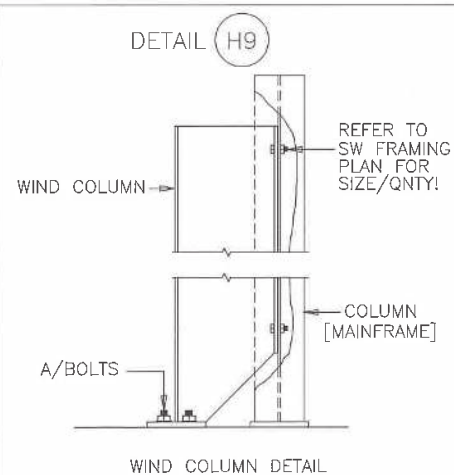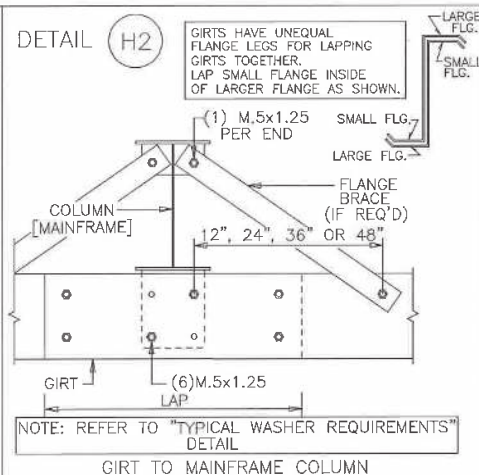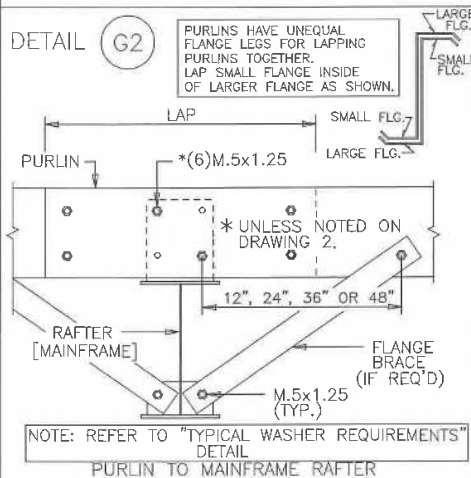


ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
CUSTOMER:			
SPENCER TAYLOR			
JCB NO:	DATE:		
7733	11/23/22		
LOCATION:			
LAKE CITY, FL 32025			
DRAWING NAME:			
FRAMING DETAILS			
DRAWING NO:	DRAWN BY:	CHECKED BY:	SCALE:
PAGE 5.2	DAR	SPW	NONE

DETAIL K3

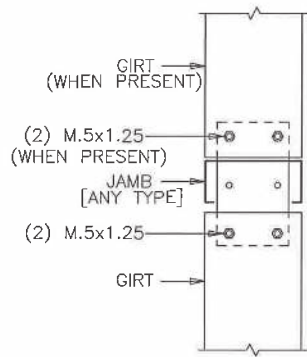


GIRTS TO JAMB

DETAIL L8

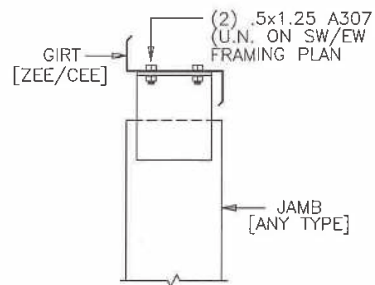


FRAMED OPENING JAMB TO GIRT

DETAIL M3

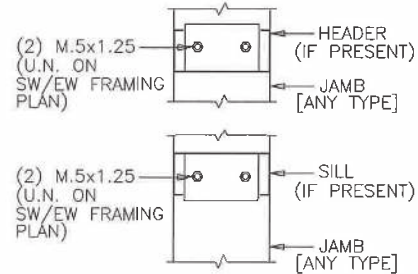


FRAMED OPENING HEADER/SILL TO JAMB

Q2 CABLE INSTALLATION DETAIL

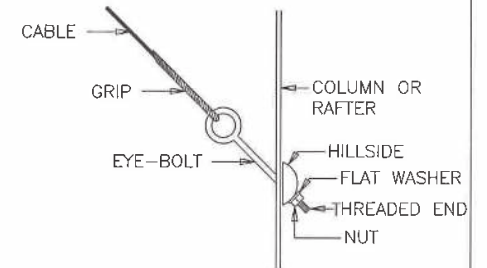

NOTE: WHEN FLUSH GIRTS/PURLINS ARE USED, FIELD SLOT GIRT OR PURLIN AS REQ'D FOR CABLE/ROD PASSAGE THROUGH PURLIN/GIRT.


BACK BRACE W/ WELDED CLIP (PROFILE MAY VARY)

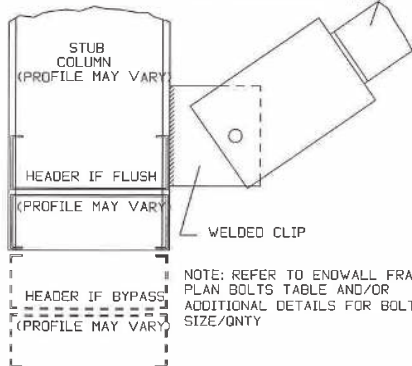

NOTE: REFER TO ENDWALL FRAMING PLAN BOLTS TABLE AND/OR ADDITIONAL DETAILS FOR BOLT SIZE/QNTY

Q12 BACK BRACE TO STUB COLUMN

BACK BRACE W/ WELDED CLIP (PROFILE MAY VARY)




NOTE: REFER TO ENDWALL FRAMING PLAN DRAWING FOR BOLTS TABLE AND/OR ADDITIONAL DETAILS FOR BOLT SIZE/QNTY

Q31 BACK BRACE TO RIGID FRAME RAFTER









DETAIL T1

1/4" x 1 1/4" ZINC HAMMER DRIVES ZAMAK ALLOY (ASTM B633, SC1, TYPE III) (24" ON CENTER)




BASE ANGLE DETAIL

ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
CUSTOMER: SPENCER TAYLOR			
JOB NO: 7733	DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025			
DRAWING NAME: FRAMING DETAILS			
DRAWING BY: PAGE 5.3	ISSUED BY: DAR	CHECKED BY: SPW	SCALE: NONE

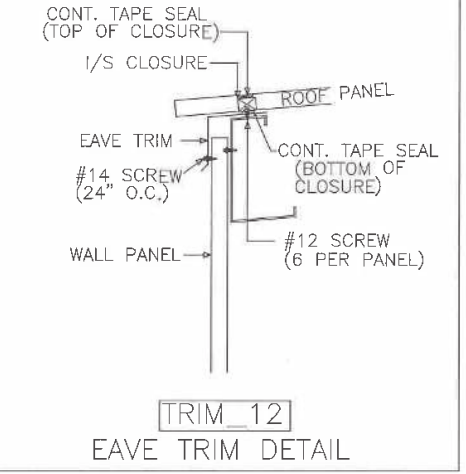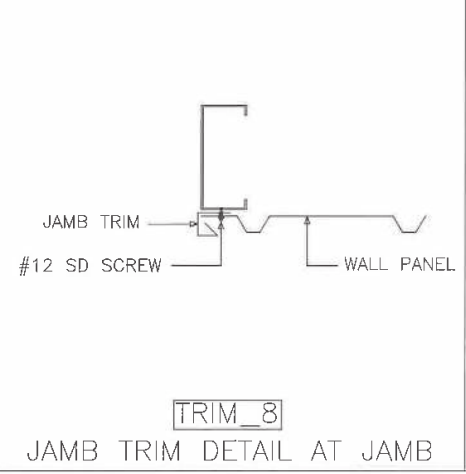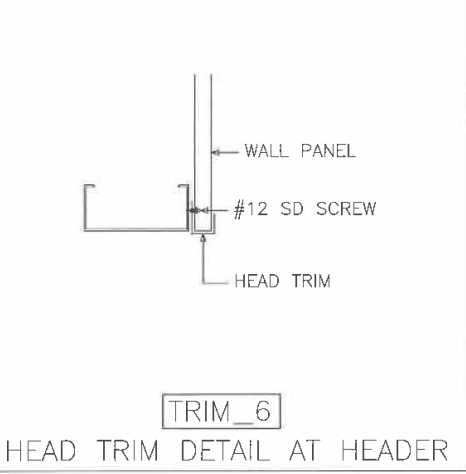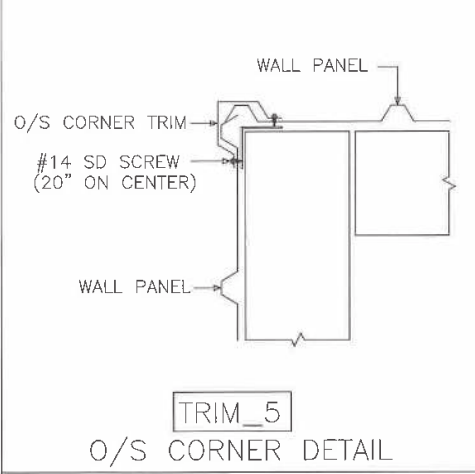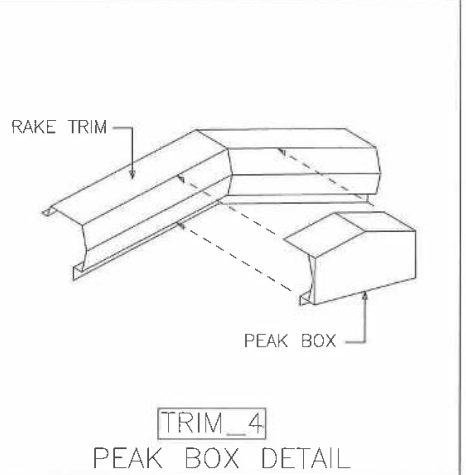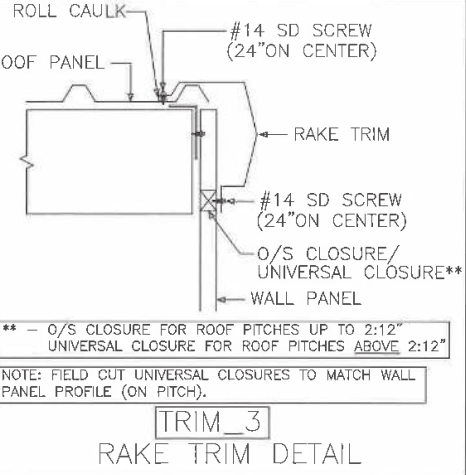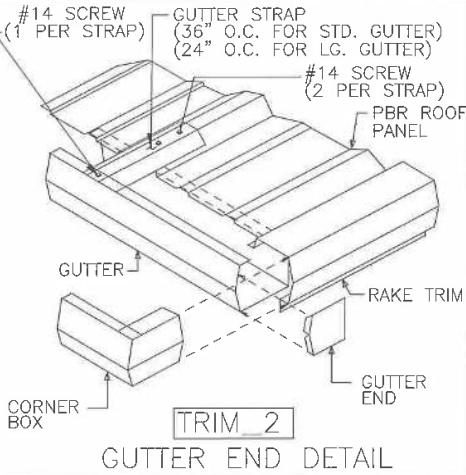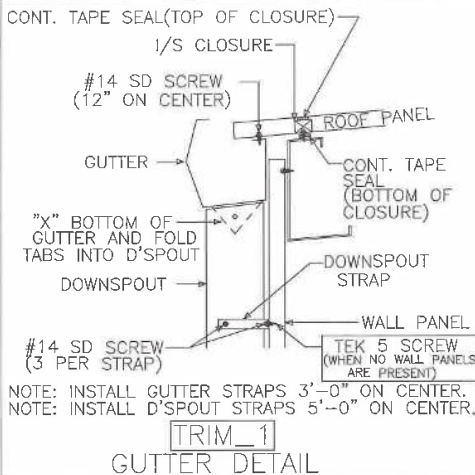


ISSUE		DET	CHK	DATE
BUILDINGS AND MORE				
CUSTOMER: SPENCER TAYLOR				
JOB NO: 7733		DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025				
DRAWING NAME: FRAMING DETAILS				
DRAWING NO: PAGE 5.4	DRAWN BY: DAR	CHECKED BY: SPW	SCALE: NONE	




TRIM_13

RAKE END DETAIL

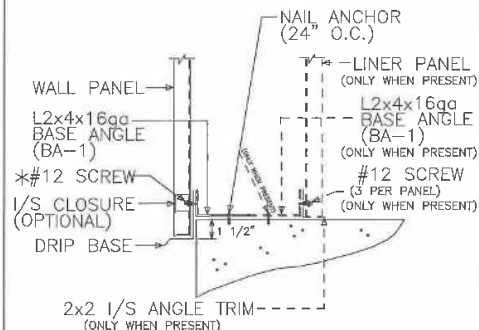


* = 6 PER PANEL FOR STANDARD PBR
3 PER PANEL FOR REV. ROLLED PBR

TRIM_16 BASE TRIM DETAIL

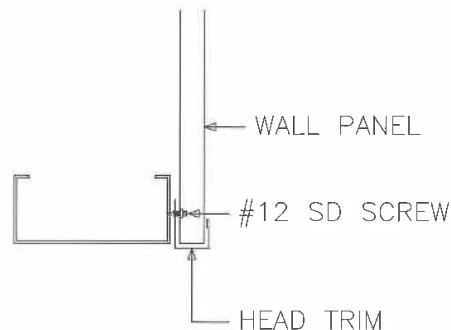


TRIM_61

HEAD TRIM DETAIL AT HEADER

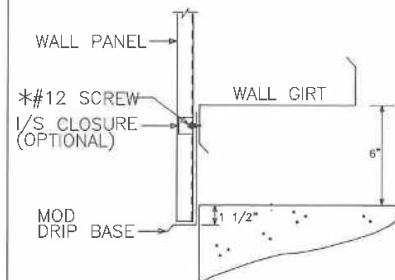

* = 6 PER PANEL FOR STANDARD PBR
3 PER PANEL FOR REV. ROLLED PBR


TRIM_99 BASE TRIM DETAIL



BOLTED END PLATE CONNECTION


TYPICAL WASHER REQUIREMENTS
(UNLESS NOTED OTHERWISE ON DRAWINGS)

SLOT TO HOLE CONN.
WASHER REQUIRED ON SLOTTED SIDE



HOLE TO HOLE CONN.
NO WASHERS REQ'D.

SLOT TO SLOT CONN.
WASHERS ARE REQUIRED ON EACH SLOTTED SIDE.
(**WASHER(S) NOT REQ'D WITHIN LAPPED ZEE PURLIN/GIRT AREAS**)



STRUCTURAL BOLTED CONNECTIONS

REFER TO COVER PAGE "GENERAL NOTES" PARAGRAPH "C", SECTION "9" FOR INSTRUCTIONS ON TIGHTENING ALL A325 AND A490 CONNECTION BOLTS.

TRIM NOTES:

- [1] SEAL TRIM SPLICES WITH TUBE CAULK.
- [2] SECURE GUTTER SPLICES AND END PLUGS WITH RIVETS.
- [3] SECURE ALL OTHER ROOF TRIM SPLICES WITH TRIM SCREWS UNLESS NOTED OTHERWISE.
- [4] TRIM SCREWS ARE LOCATED 24" ON CENTER UNLESS NOTED OTHERWISE.
- [5] STD. TRIM SPLICES ARE 3" TOTAL UNLESS NOTED OTHERWISE.

MORTISE PREPPED PERSONNEL DOORS


ALL MORTISE PREPPED PERSONNEL DOORS COME AS RIGHTHAND REVERSED SWING.

(i.e. STANDING ON THE OUTSIDE OF THE BUILDING FACING THE DOOR, THE LOCK WILL BE ON THE LEFTHAND SIDE OF THE DOOR AND THE DOOR WILL SWING OUTWARD FROM THE BUILDING.)

ANY FIELD MODIFICATIONS ARE THE RESPONSIBILITY OF THE ERECTOR AND MBM IS NOT LIABLE FOR LABOR CHARGES NOR DAMAGES DUE TO ERROR.



ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
CUSTOMER:			
SPENCER TAYLOR			
JOB NO:	DATE:		
7733	11/23/22		
LOCATION:			
LAKE CITY, FL 32025			
DRAWING NAME:			
FRAMING DETAILS			
DRAWING BY:	DRAWN BY:	CHECKED BY:	SCALE:
SPW 5.5	DAR	SPW	NONE

TRIM TABLE		
ROOF PLAN		
OID	PART	LENGTH
1	D/F CAP6	3'-0"

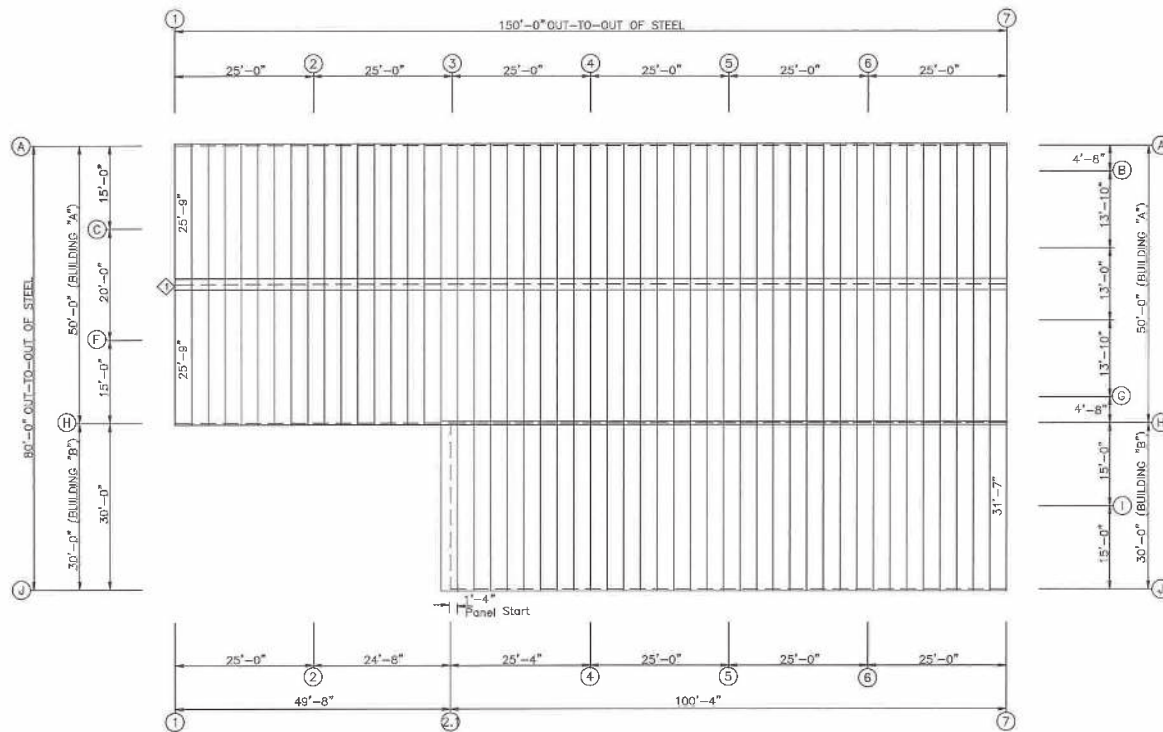


ROOF SHEETING PLAN
PANELS: 26 GA. PBR - GALVALUME

ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
CUSTOMER: SPENCER TAYLOR			
JOB NO:	7733	AND:	11/23/22
LOCATION: LAKE CITY, FL 32025			
DRAWING NAME: ROOF PANELS & TRIM			
DRAWING NO:	PAGE 6	SHEET OF: DAR	SPEAKER OF: SPW
			SCALE: NONE

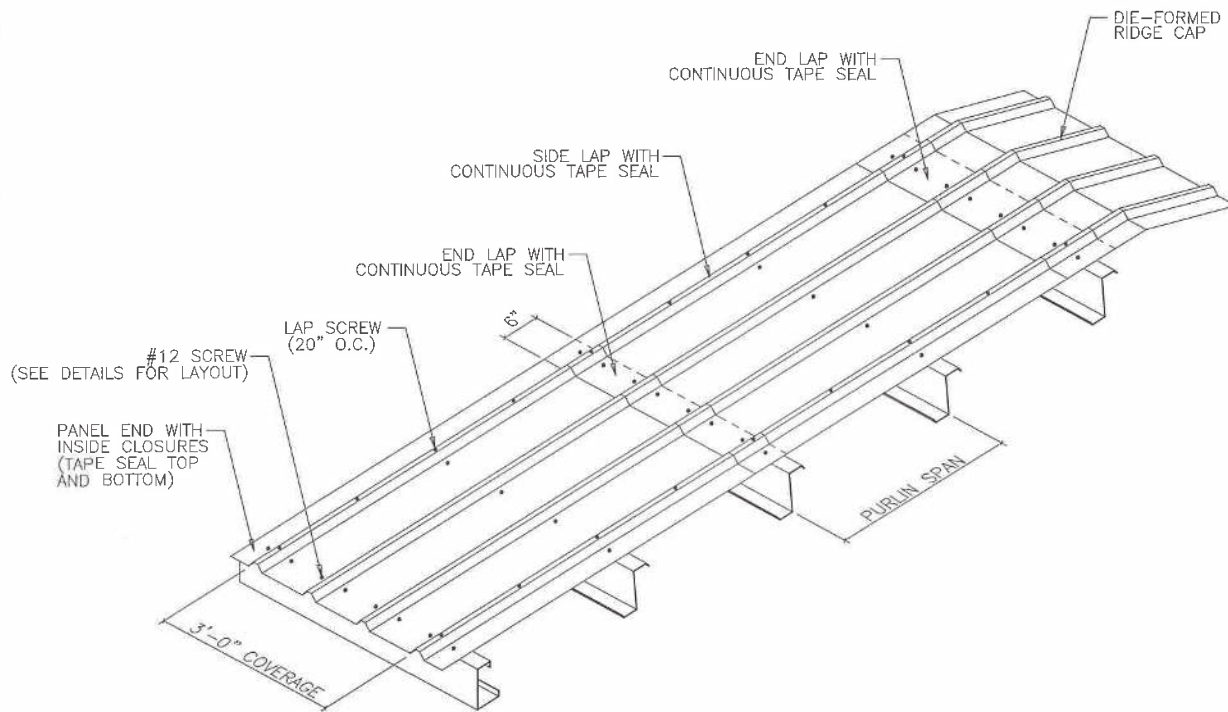

PANEL ATTACHMENT AT PANEL END
(PEAK PURLIN, EAVE STRUT, AND PANEL END LAPS)





PANEL ATTACHMENT AT INTERMEDIATE MEMBERS


NOTES:

- [1] ALL END LAPS MUST BE A MINIMUM OF 6".
- [2] METAL SHAVINGS MUST BE SWEEPED FROM THE ROOF EACH DAY DURING ERECTION TO PREVENT SURFACE RUSTING.
- [3] TAPE SEAL MUST BE APPLIED WITH NO GAPS OR BREAKS.
- [4] #12 SCREWS ARE USED TO ATTACH THE PANEL TO THE PURLINS. #14 LAP SCREWS ARE USED AT THE PANEL-TO-PANEL ATTACHMENTS. ALL FASTENERS ARE SELF-DRILLING.

ISSUE				BUILDINGS AND MORE			
DESIGNED BY	DET	CHK	DATE	SPENCER TAYLOR			
JOB NO.	7733	DATE	11/23/22	LOCATION			
				LAKE CITY, FL 32025			
				DRAWING NAME		SCALE	
				ROOF PANEL DETAILS		NONE	
APPROVED BY	PAGE 6.1	DESIGNED BY	DAR	APPROVED BY	SPW	DATE	

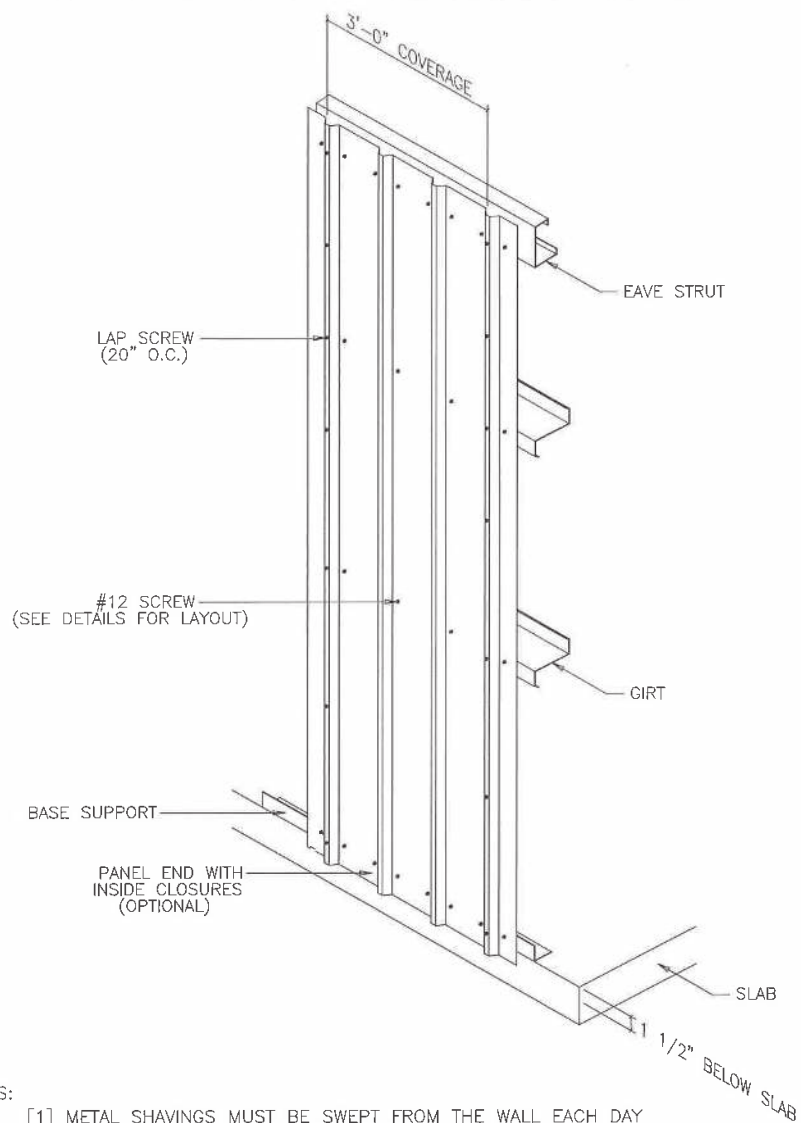

PANEL ATTACHMENT AT PANEL END
(BASE, EAVE STRUT, HEADER, SILL, AND PANEL END LAPS)




PANEL ATTACHMENT AT INTERMEDIATE MEMBERS

NOTES:

- [1] METAL SHAVINGS MUST BE SWEEPED FROM THE WALL EACH DAY DURING ERECTION TO PREVENT SURFACE RUSTING.
- [2] #12 SCREWS ARE USED TO ATTACH THE PANEL TO THE GIRTS. #14 LAP SCREWS ARE USED AT THE PANEL-TO-PANEL ATTACHMENTS. ALL FASTENERS ARE SELF-DRILLING.


ISSUE	DET	CHK	DATE

BUILDINGS AND MORE			
CUSTOMER SPENCER TAYLOR			
JOB NO: 7733		DATE 11/23/22	
LOCATION LAKE CITY, FL 32025			
DRAWING NAME SIDEWALL PANEL DETAILS			SCALE NONE
DRAWN BY DAR	CHECKED BY SPW	PAGE 7	FIG: 1

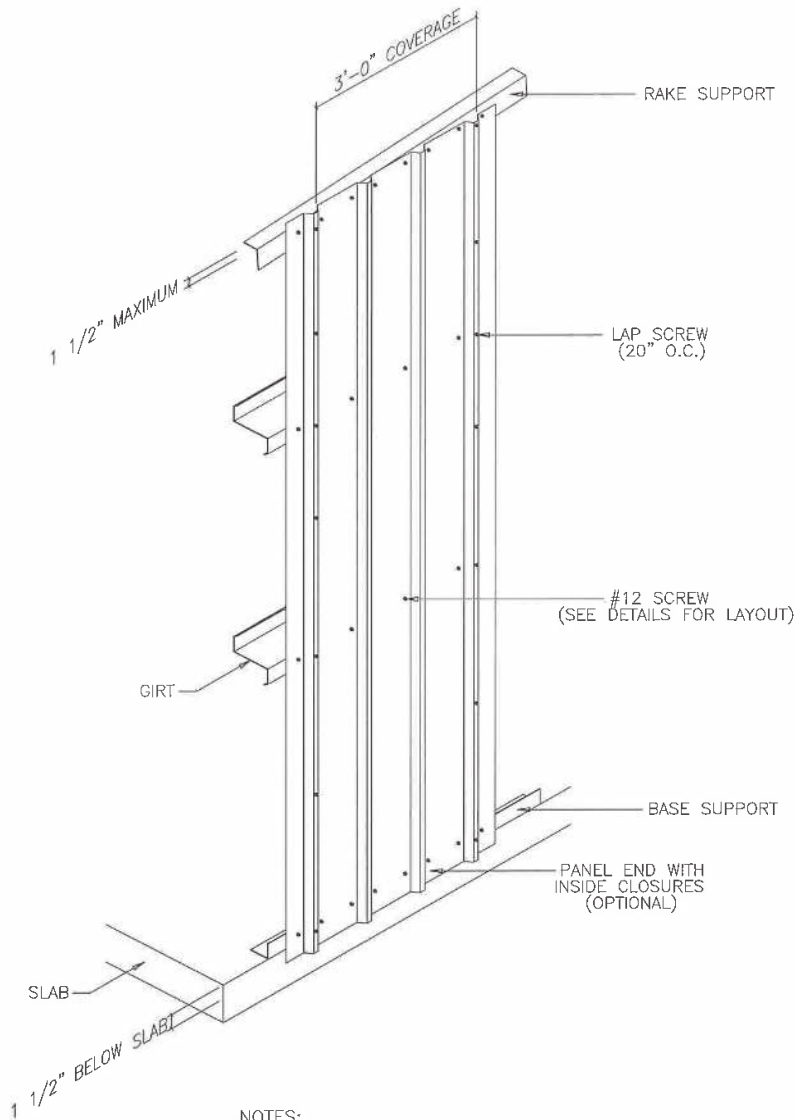


NOTES:

- [1] METAL SHAVINGS MUST BE SWEEPED FROM THE WALL EACH DAY DURING ERECTION TO PREVENT SURFACE RUSTING.
- [2] #12 SCREWS ARE USED TO ATTACH THE PANEL TO THE GIRTS. #14 LAP SCREWS ARE USED AT THE PANEL-TO-PANEL ATTACHMENTS. ALL FASTENERS ARE SELF-DRILLING.




PANEL ATTACHMENT AT PANEL END
(BASE, EAVE STRUT, HEADER, SILL, AND PANEL END LAPS)



PANEL ATTACHMENT AT INTERMEDIATE MEMBERS

ISSUE	DET	CHK	DATE

BUILDINGS AND MORE			
CUSTOMER SPENCER TAYLOR			
JOB NO: 7733	DATE: 11/23/22		
LOCATION LAKE CITY, FL 32025			
DRAWING NAME ENDWALL PANEL DETAILS			SCALE NONE
CREATED BY JAC	DRAWN BY DAP	CHECKED BY SPW	DATE ENR
PAGE 8			

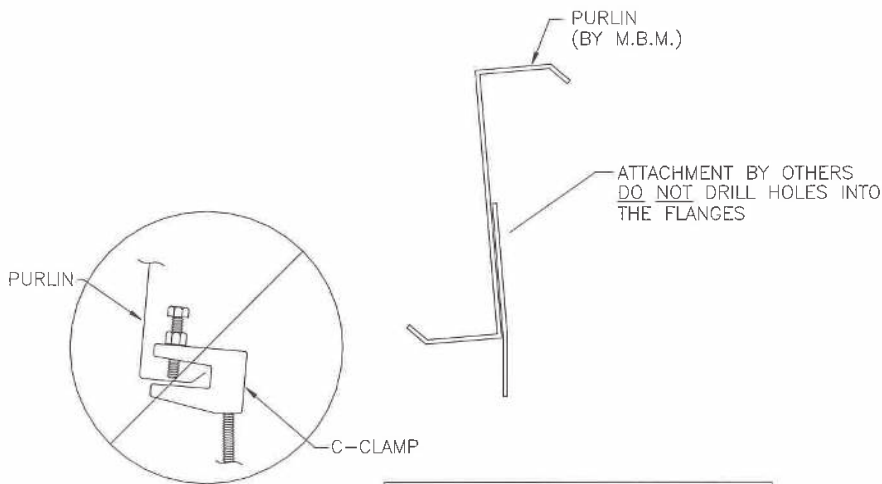

Flange C-Clamp is not an acceptable connection

NOTE: M.B.M. only provides the roof purlin. All other material and hardware is by others.

Recommended Connection Detail


NOTE

MANY FACTORS BEYOND THE CONTROL OF THE METAL BUILDING SUPPLIER AFFECT THE ABILITY OF A PURLIN TO SAFELY SUPPORT HANGING LOADS COMBINED WITH OTHER REQUIRED ROOF LOADS. DUE TO THE VARIABLES INVOLVED IN HANGING LOADS AND THEIR ATTACHMENTS TO THE PURLINS, THE METAL BUILDING SUPPLIER CANNOT ASSURE THAT THE PURLINS FOR A PARTICULAR BUILDING PROJECT CAN SAFELY SUPPORT THE MAXIMUM ALLOWABLE HANGING LOADS IN COMBINATION WITH OTHER ROOF LOADS.


IT IS THE RESPONSIBILITY OF THE HANGER SYSTEM INSTALLER TO COORDINATE WITH THE ENGINEER OF RECORD FOR THE OVERALL PROJECT TO ENSURE A SAFE HANGING LOAD INSTALLATION. THE METAL BUILDING ENGINEER IS NOT THE ENGINEER OF RECORD FOR THE OVERALL PROJECT. WITHOUT SPECIFIC CERTIFICATION FOR INDIVIDUAL HANGING LOADS, THE NET EFFECTS OF APPLIED HANGER LOADS INSTALLED ON A PARTICULAR PURLIN SHALL NOT EXCEED THE NET EFFECTS OF THE CERTIFIED UNIFORMLY APPLIED DESIGN COLLATERAL LOAD.

HANGING LOADS SHOULD NOT BE APPLIED TO THE PURLIN LIP. WHERE PERMISSIBLE, THE BEST PRACTICE FOR HANGING LOADS IS TO ATTACH TO THE PURLIN WEB USING A BOLT AND NUT, OR SELF-DRILLING SCREWS.

HANGING UNIFORM LOADS SUCH AS SPRINKLER MAINS OR HVAC EQUIPMENT SHOULD BE DISTRIBUTED OVER SEVERAL PURLINS, AND SHOULD NEVER EXCEED THE COLLATERAL LOAD ALLOWANCE FOR THE ROOF SYSTEM. FOR UNIFORM LOADS THAT RUN PARALLEL TO THE PURLINS, IT MAY BE NECESSARY TO USE TRANSVERSE SUPPORT CHANNELS(A.K.A. TRAPEZE BEAMS) ATTACHED TO THE WEBS OR FLANGES OF ADJACENT PURLINS TO SPREAD THE LOAD BETWEEN TWO OR MORE PURLINS. IN SUCH CASES, CONTACT THE BUILDING MANUFACTURER OR A LOCAL PROFESSIONAL ENGINEER PRIOR TO ATTEMPTING TO HANG LOADS FROM THE PURLINS

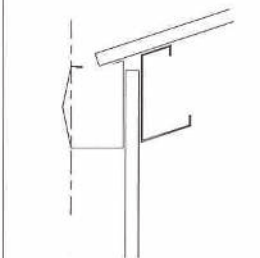


DO NOT INSTALL GUTTER WITH OUTSIDE FACE PERPENDICULAR TO THE GROUND.

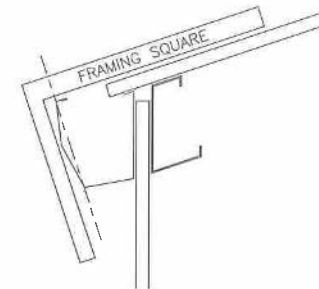

INSTALL GUTTER WITH OUTSIDE FACE PERPENDICULAR TO THE ROOF.

GUTTER INSTALLATION DETAIL
(ONLY IF PROVIDED)

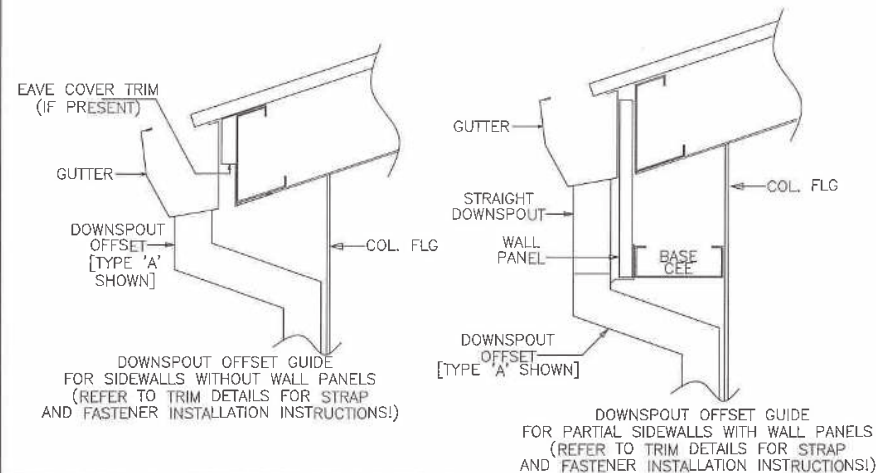

ISSUE	DET	CHK	DATE
BUILDINGS AND MORE			
DESIGNER: SPENCER TAYLOR			
JOB NO: 7733	DATE: 11/23/22		
LOCATION: LAKE CITY, FL 32025			
SPECIAL DETAILS			
DRAWING NO: PAGE 9	DESIGN BY: DAF	CHECKED BY: SPW	SCALE: NONE
