FLORIDA ENERGY EFFICIENCY CODE FOR BUILDING CONSTRUCTION

Florida Department of Business and Professional Regulation - Residential Performance Method

Project Name: 1724 SW Herlong St-Blanchard-N Street: 1724 SW Herlong St City, State, Zip: Fort White, FL 32038, FL, 32038 Owner: Stephanie Blanchard Design Location: FL, Gainesville	Builder Name: . Permit Office: Permit Number: Jurisdiction: County: Columbia(Florida Climate Zone 2)
1. New construction or existing 2. Single family or multiple family 3. Number of units, if multiple family 4. Number of Bedrooms 5. Is this a worst case? 6. Conditioned floor area above grade (ft²) Conditioned floor area below grade (ft²) 7. Windows(39.0 sqft.) 844 Conditioned floor area below grade (ft²) 845 Conditioned floor area below grade (ft²) 846 Conditioned floor area below grade (ft²) 847 Conditioned floor area below grade (ft²) 848 Conditioned floor area below grade (ft²) 849 Conditioned floor area below grade (ft²) 840 Conditioned floor area above grade (ft²) 841 Conditioned floor area above grade (ft²) 842 Conditioned floor area above grade (ft²) 844 Conditioned floor area below grade (ft²) 844 Conditioned floor area be	10. Wall Types(2152.5 sqft.) a. Frame - Wood, Exterior b. Frame - Wood, Adjacent c. N/A d. N/A 11. Ceiling Types(844.0 sqft.) b. N/A c. N/A 12. Roof(Metal, Vented) c. N/A 13. Ducts, location & insulation level a. Central Unit 15. Heating Systems a. Electric Heat Pump 16. Hot Water Systems a. Electric b. Conservation features None 17. Credits R=13.0 1312.50 ft² R=13.0 1312.50 ft² R=13.0 844.00 ft² R=30.0 844.00 ft² R=13.0 R=13.0 840.00 ft² R=30.0 844.00 ft² R=13.0 840.00 ft² R=13.0 840.00 ft² R=30.0 844.00 ft² R=13.0 840.00 ft² R=30.0 844.00 ft² R=13.0 840.00 ft² R=30.0 844.00 ft² R=13.0 840.00 ft² R=30.0 844.00 ft² R=30.0 914 ft² 13. Ducts, location & locat
Glass/Floor Area: 0.046 Total Proposed Modifie Total Baselin	TA CC
I hereby certify that the plans and specifications covered by this calculation are in compliance with the Florida Energy Code. PREPARED BY: Robin Goodwell DATE: March 24, 2023 I hereby certify that this building, as designed, is in compliance with the Florida Energy Code. OWNER/AGENT: DATE:	Review of the plans and specifications covered by this calculation indicates compliance with the Florida Energy Code. Before construction is completed this building will be inspected for compliance with Section 553.908 Florida Statutes. BUILDING OFFICIAL: DATE:

- Compliance requires certification by the air handler unit manufacturer that the air handler enclosure qualifies as certified factory-sealed in accordance with R403.3.2.1.
- Proposed Qn of NAN exceeds the performance method default limit of 0.08 and therefore does not require duct testing. R405 .2.3
- Compliance requires an Air Barrier and Insulation Inspection Checklist in accordance with R402.4.1.1 and this project requires a PERFORMANCE envelope leakage test report with envelope leakage no greater than 7.00 ACH50 (R402.4.1.2).

FORM R405-2022S

INPUT SUMMARY CHECKLIST REPORT

					PRO.	JECT						
Own Build Pern Juris Fam New Year	ding Type: er: der Name: nit Office: diction: ily Type:	1724 SW Herlong St- User Stephanie Blanchard Detached New (From Plans)	Blanchard-N	Bedrooms Condition Total Stor Worst Ca Rotate Ar Cross Ver Whole Ho Terrain: Shielding:	ed Area: ries: se: ngle: ntilation: buse Fan	1 844 1 No 0 No : No : No Suburban Suburban	Lot # Bloc PlatE Stree Cour	k/SubDivisio Book: et:	Street Add on: 1724 SW I Columbia Fort White FL, 32038	Herlong St		
					CLIN	IATE						
V Des	sign ation		Tmy Site		Des 97.5%	ign Temp 2.5%	Int Desig Winter		Heating Degree Days	Desigi Moisture		ly temp nge
FL	., Gainesville	FL	_GAINESVILLE	_REGIONA	32	92	70	75	1305.5	51	Medi	um
					BLO	CKS						
√ Nur	mber	Name	Area	Vol	ume							
1		Block1	844	118	16 cu ft							
					SPA	CES						
√ Nur	mber	Name	Area	Volume	Kitchen	Occupants	Bedr	ooms	Finished	Coo	led F	leated
1		Main	844	11816	Yes	2	,		Yes	Υe	es	Yes
					FLO	ORS		(Total E	xposed A	rea = 8	344 sq	.ft.)
V #	Floor Type	e	Space	Exposed	Perim	Perimeter R-Va	alue Area	U-Facto	r Joist R-Value	e Tile	Wood	Carpet
1	Slab-On-Gr	ade Edge Ins	Main	160)	0	844	ft 0.518		0.20	0.00	0.80
					RO	OF						
/ #	Туре		Materials		oof ea	Gable Roof Area Color		Solar Absor.	SA Emitt Tested	Emitt Tested	Deck Insul.	Pitch (deg)
1	Gable or Sh	ned	Metal	91	14 ft²	176 ft ² Mediur	m N	0.75	N 0.9	No	0	22.62
					ΑТ	TIC						
/ #	Туре		Ventilation	1	Vent F	Ratio (1 in)	Area	RBS	IRCC			
1	Full attic		Vented			300	844 ft ²	N	N			
					CEIL	ING		(Total E	xposed A	rea = 8	344 sq	.ft.)
V #	Ceiling Ty	/pe		Space	R-Va	alue Ins. Typ	oe Are	a U-Fa	actor Framino	g Frac.	Trus	s Type
1	Sloped ceili	ng under attic(Vented)	Main	30	.0 Blowr	n 844.	Oft² 0.0	0.1	0	W	ood

FORM R405-2022S INPUT SUMMARY CHECKLIST REPORT

								WA	LLS	;		(To	otal	Ехр	osed	Area	a = 2	153	sq.f	t.)
\ #	Ornt	Adjac To		Wall Type		Space		Cav R-V	vity /alue	Width Ft Ir		Heigh Ft In		Area sq.ft.	U- Facto	She r R-V		rm. S		Below Grade
1 2 3 4	E S	E	Exterior Exterior Garage Exterior	Frame - Woo Frame - Woo Frame - Woo Frame - Woo	od od	N N	lain lain lain lain	1; 1;	3.0 3.0 3.0 3.0	60.0 (13.0 (60.0 (20.0 (5 1) 1	4.0 4.0 4.0 4.0	0 0 0 0	840.0 189.0 840.0 283.5	0.09	5 (5 (0. 0 0.	25 25	0.80 0.80 0.80 0.80	0 % 0 % 0 % 0 %
								DO	ORS	3			(Tot	al E	xpos	ed A	rea :	= 75	sq.f	t.)
\ #	Ornt	P	Adjacent	To Door Type	e	Space			Stori	ms	ι	J-Valu	e		/idth ⁻ t In		Heigh Ft Ir		Are	a
1 2	N S		Exterior Garage			Mair Mair				one		0.40 0.40		5.00 5.00		7.0 7.0		0 0	37.9 37.3	
							W	/INE	OOW	/S			(Tot	al E	xpos	ed A	rea :	= 39	sq.f	t.)
\sqrt #	Ornt	Wall ID	Frame	Panes	NFR	C U-Factor	SHGC	Imp :	Storm	Total Area (ft²)	Same Units	Wid (ft)		eight (ft)	Over Depth (ft)			rior Sł	nade	Screen
1 2 3	n	1 1 2	Vinyl Vinyl Vinyl	Low-E Double Low-E Double Low-E Double	Y Y Y	0.40	0.25 0.25 0.25	N N N	N N N	6.0 18.0 15.0	1 2 1	2.0 3.0 3.0	0 3	3.00 3.00 5.00	0.5 0.5 0.5	5.0 5.0 5.0		None None None	:	None None None
							INF	ILT	RAT	ION										
V #	Scope	Э	Ме	thod		SLA (CFM50	E	LA	EqL	A	ACH	,	ACH50	0 Spa	ce(s)	Inf	Itratio	n Test	Volume
1	Who	olehous	se Prop	osed ACH(50)	0.	00062	1379	75	5.63	141.9	9	0.1716	6	7.0	P	All	11	816 cı	u ft	
							(SAR	RAG	E										
V #		Fle	oor Area		Roof A	rea	Exp	osed	Wall P	erimeter		А	vg. W	all He	ight	E	kposed	Wall	Insulat	ion
1		2	2340 ft²		2340	ft²			216 ft				1	4 ft				1		
								MA	ASS											
V #	Mas	ss Type				Area		Th	icknes	ss	Fur	niture	Fraction	on		Space	;			
1	Defa	ault(8 lb	os/sq.ft.)			0 ft²			0 ft			0.3	0			Mair	1			
							HEAT	ING	SY	STE	VI									
\sqrt	Sys	tem Ty _l	pe		Subtype	e/Speed	AHRI	#	Effici	iency	Capa kBtu		 Entry		ermal H ower		mp Curre		cts I	Block
1	Elec	ctric He	at Pump		Split/s	Single			HSPF	9.10	21.	.0		C	0.00	0.00	0.00) sys	#0	1
						(COOL	INC	SY	STE	M									
#	Sys	tem Ty _l	 _		Subtype	e/Speed	AHRI	- -	Eff	ficiency		Capa kBtu			Air Flow cfm	, 	SHR	Du	ct I	Block

FORM R405-2022S

INPUT SUMMARY CHECKLIST REPORT

				COC	DLIN	G SYS	TEM(C	ontinu	ued)					
1	Central Unit			Split/Singl	e		SEER:	18.0 21	1.0		0	0.75	Ductles	s 1
					НОТ	T WATI	ER SY	STEM						
/ #	System Type	Subtype		Location		EF(UEF)	Сар	Use	SetPnt	Fixture	Flow	Pipe Ins.	. Pipe	elength
1	Electric	None		Main		0.92 (0.92)) 40.00 gal	40 gal	120 deg	Stan	dard	None		99
	Recirculation System		с Control Гуре		Loop length	Branch length	Pump power	DWHR	Facilitie Connect	-		DWHR Eff	Othe	r Credits
1	No				NA	NA	NA	No	NA	N	A	NA	Non	ie
						DU	CTS							
Duct #		ply R-Value A		Ret			Leakage T	ype	Air Handler	CFM 25 TOT	CFM 2 OUT	-	RLF H	HVAC # eat Cool
					T	EMPER	RATUR	ES						
Progr Cooli Heati Venti	ing [X] Jan	ostat: Y [] Feb [X] Feb [] Feb	[] Mar [X] Mar [X] Mar	[] Apr [] Apr [X] Apr	[]	Ceiling Far May [X] May []	ns: N] Jun [Jun	X] Jul	[X] Aug [] Aug [] Aug	[X] Sep [] Sep [] Sep	[X] ([] (Oct [X] Nov (] Nov (] Nov	[] Dec [X] Dec [] Dec
Cooli Heati Venti	ing [] Jan ing [X] Jan	[] Feb [X] Feb [] Feb	[X] Mar [X] Mar	[] Apr [X] Apr	[] N[]	Ceiling Far May [X] May []	ns: N] Jun [Jun	X] Jul [] Jul	[] Aug [] Aug	[]Sep	[] [Oct [X	(] Nov	[X] Dec
Cooli Heati Venti	ing [] Jan ing [X] Jan ing [] Jan ermostat Sched	[] Feb [X] Feb [] Feb	[X] Mar [X] Mar 2006 Refere	[] Apr [X] Apr	[] N[] N[]	Ceiling Far May [X] May [] May []	ns: N Jun	X] Jul [] Jul [] Jul Hou	[] Aug [] Aug irs	[]Sep []Sep	[X] (Oct [X Oct [X	(] Nov (] Nov	[X] Dec [] Dec
Cooli Heati Venti The Scl	ing [] Jan ing [X] Jan ing [] Jan ermostat Sched hedule Type	[] Feb [X] Feb [] Feb ule: HERS 2	[X] Mar [X] Mar 2006 Refere	[] Apr [X] Apr ence 2	[] [] [] 3	Ceiling Far May [X] May [] May []	ns: N] Jun [Jun Jun 5	X] Jul [] Jul [] Jul Hou 6	[] Aug [] Aug Irs 7	[] Sep [] Sep	9 [X] (Oct [X Oct [X	(] Nov (] Nov 11	[X] Dec [] Dec
Cooli Heati Venti The Scl Co Co	ing [] Jan ing [X] Jan ing [] Jan ermostat Sched hedule Type poling (WD)	[] Feb [X] Feb [] Feb ule: HERS 2	[X] Mar [X] Mar 2006 Refere 1 78 80	[] Apr [X] Apr ence 2 78 80	[]N []N 3	Ceiling Far May [X May [] May [] 4	ns: N Jun [Jun Jun 5 78	X] Jul [] Jul [] Jul Hou 6 78	[] Aug [] Aug Irs 7 78 78	[] Sep [] Sep 8	9 80 78	Oct [X Oct [X 10 80 78	1] Nov 1] Nov 11 80 78	[X] Dec [] Dec 12 80 78

Florida Building Code, Energy Conservation, 7th Edition (2020) Mandatory Requirements for Residential Performance, Prescriptive and ERI Methods

ADDRESS:	1724 SW Herlong St	Permit Number:	
	Fort White, FL 32038, FL 32038		

MANDATORY REQUIREMENTS - See individual code sections for full details.

SECTION R401 GENERAL
R401.3 Energy Performance Level (EPL) display card - (Mandatory). The building official shall require that an energy performance level (EPL) display card be completed and certified by the builder to be accurate and correct before final approval of the building for occupancy. Florida law (Section 553.9085, Florida Statutes) requires the EPL display card to be included as an addendum to each sales contract for both presold and nonpresold residential buildings. The EPL display card contains information indicating the energy performance level and efficiencies of components installed in a dwelling unit. The building official shall verify that the EPL display card completed and signed by the builder accurately reflects the plans and specifications submitted to demonstrate code compliance for the building. A copy of the EPL display card can be found in Appendix RD.
SECTION R402 BUILDING THERMAL ENVELOPE
R402.4 Air leakage (Mandatory). The building thermal envelope shall be constructed to limit air leakage in accordance with the requirements of Sections R402.4.1 through R402.4.5.
Exception: Dwelling units of R-2 Occupancies and multiple attached single family dwellings shall be permitted to comply with Section C402.5.
R402.4.1 Building thermal envelope. The building thermal envelope shall comply with Sections R402.4.1.1 and R402.4.1.2. The sealing methods between dissimilar materials shall allow for differential expansion and contraction.
R402.4.1.1 Installation. The components of the building thermal envelope as listed in Table R402.4.1.1 shall be installed in accordance with the manufacturer's instructions and the criteria listed in Table R402.4.1.1, as applicable to the method of construction. Where required by the code official, an approved third party shall inspect all components and verify compliance.
R402.4.1.2 Testing. The building or dwelling unit shall be tested and verified as having an air leakage rate not exceeding seven air changes per hour in Climate Zones 1 and 2, and three air changes per hour in Climate Zones 3 through 8. Testing shall be conducted in accordance with ANSI/RESNET/ICC 380 and reported at a pressure of 0.2 inch w.g. (50 pascals). Testing shall be conducted by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i) or an approved third party. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official. Testing shall be performed at any time after creation of all penetrations of the building thermal envelope.
Exception: Testing is not required for additions, alterations, renovations, or repairs, of the building thermal envelope of existing buildings in which the new construction is less than 85 percent of the building thermal envelope.
During testing: 1. Exterior windows and doors, fireplace and stove doors shall be closed, but not sealed, beyond the intended weatherstripping or other infiltration control measures. 2. Dampers including exhaust, intake, makeup air, backdraft and flue dampers shall be closed, but not sealed beyond intended infiltration control measures. 3. Interior doors, if installed at the time of the test, shall be open. 4. Exterior doors for continuous ventilation systems and heat recovery ventilators shall be closed and sealed. 5. Heating and cooling systems, if installed at the time of the test, shall be turned off. 6. Supply and return registers, if installed at the time of the test, shall be fully open.
R402.4.2 Fireplaces. New wood-burning fireplaces shall have tight-fitting flue dampers or doors, and outdoor combustion air. Where using tight-fitting doors on factory-built fireplaces listed and labeled in accordance with UL 127, the doors shall be tested and listed for the fireplace. Where using tight-fitting doors on masonry fireplaces, the doors shall be listed and labeled in accordance with UL 907.
R402.4.3 Fenestration air leakage. Windows, skylights and sliding glass doors shall have an air infiltration rate of no more than 0.3 cfm per square foot (1.5 L/s/m2), and swinging doors no more than 0.5 cfm per square foot (2.6 L/s/m2), when tested according to NFRC 400 or AAMA/ WDMA/CSA 101/I.S.2/A440 by an accredited, independent laboratory and listed and labeled by the manufacturer.

Exception: Site-built windows, skylights and doors.

R402.4.4 Rooms containing fuel - burning appliances. In Climate Zones 3 through 8, where open combustion air ducts provide combustion air to open combustion fuel burning appliances, the appliances and combustion air opening shall be located outside the building thermal envelope or enclosed in a room, isolated from inside the thermal envelope. Such rooms shall be sealed and insulated in accordance with the envelope requirements of Table R402.1.2, where the walls, floors and ceilings shall meet not less than the basement wall R-value requirement. The door into the room shall be fully gasketed and any water lines and ducts in the room insulated in accordance with Section R403. The combustion air duct shall be insulated where it passes through conditioned space to a minimum of R-8.

Exceptions:

- 1. Direct vent appliances with both intake and exhaust pipes installed continuous to the outside.
- 2. Fireplaces and stoves complying with Section R402.4.2 and Section R1006 of the Florida Building Code, Residential.

MANDATORY REQUIREMENTS (Continued)

not more than 2.0 cfm (0.944 L/s) when tested in accordance with ASTM E283 at a 1.57 psf (75 Pa) pressure differential. All recessed luminaires shall be sealed with a gasket or caulk between the housing and the interior wall or ceiling covering.
SECTION R403 SYSTEMS
R403.1 Controls R403.1.1 Thermostat provision (Mandatory). At least one thermostat shall be provided for each separate heating and cooling system
R403.1.3 Heat pump supplementary heat (Mandatory). Heat pumps having supplementary electric-resistance heat shall have controls that, except during defrost, prevent supplemental heat operation when the heat pump compressor can meet the heating load.
R403.3.2 Sealing (Mandatory). All ducts, air handlers, filter boxes and building cavities that form the primary air containment passageways for air distribution systems shall be considered ducts or plenum chambers, shall be constructed and sealed in accordance with Section C403.2.9.2 of the Commercial Provisions of this code and shall be shown to meet duct tightness criteria below.
Duct tightness shall be verified by testing in accordance with ANSI/RESNET/ICC 380 by either individuals as defined in Section 553.993(5) or (7), Florida Statutes, or individuals licensed as set forth in Section 489.105(3)(f), (g) or (i), Florida Statutes, to be "substantially leak free" in accordance with Section R403.3.3.
R403.3.2.1 Sealed air handler. Air handlers shall have a manufacturer's designation for an air leakage of no more than 2 percent of the design airflow rate when tested in accordance with ASHRAE 193.
 R403.3.3 Duct testing (Mandatory). Ducts shall be pressure tested to determine air leakage by one of the following methods: 1. Rough-in test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the system, including the manufacturer's air handler enclosure if installed at the time of the test. All registers shall be taped or otherwise sealed during the test. 2 Postconstruction test: Total leakage shall be measured with a pressure differential of 0.1 inch w.g. (25 Pa) across the entire system, including the manufacturer's air handler enclosure. Registers shall be taped or otherwise sealed during the test.
 Exceptions; A duct air leakage test shall not be required where the ducts and air handlers are located entirely within the building thermal envelope. Duct testing is not mandatory for buildings complying by Section 405 of this code. Duct leakage testing is required for Section R405 compliance where credit is taken for leakage, and a duct air leakage Qn to the outside of less than 0.080 (where Qn = duct leakage to the outside in cfm per 100 square feet of conditioned floor area tested at 25 Pascals) is indicated in the compliance report for the proposed design. A written report of the results of the test shall be signed by the party conducting the test and provided to the code official
R403.3.5 Building cavities (Mandatory). Building framing cavities shall not be used as ducts or plenums
R403.4 Mechanical system piping insulation (Mandatory). Mechanical system piping capable of carrying fluids above 105°F (41°C) or below 55°F (13°C) shall be insulated to a minimum of R-3.
R403.4.1 Protection of piping insulation. Piping insulation exposed to weather shall be protected from damage, including that caused by sunlight, moisture, equipment maintenance and wind, and shall provide shielding from solar radiation that can cause degradation of the material. Adhesive tape shall not be permitted.
R403.5.1 Heated water circulation and temperature maintenance systems (Mandatory). If heated water circulation systems are installed, they shall be in accordance with Section R403.5.1.1. Heat trace temperature maintenance systems shall be in accordance with Section R403.5.1.2. Automatic controls, temperature sensors and pumps shall be accessible. Manual controls shall be readily accessible.
R403.5.1.1 Circulation systems. Heated water circulation systems shall be provided with a circulation pump. The system return pipe shall be a dedicated return pipe or a cold water supply pipe. Gravity and thermosiphon circulation systems sha be prohibited. Controls for circulating hot water system pumps shall start the pump based on the identification of a deman for hot water within the occupancy. The controls shall automatically turn off the pump when the water in the circulation loop is at the desired temperature and when there is no demand for hot water.
R403.5.1.2 Heat trace systems. Electric heat trace systems shall comply with IEEE 515.1 or UL 515. Controls for such systems shall automatically adjust the energy input to the heat tracing to maintain the desired water temperature in the piping in accordance with the times when heated water is used in the occupancy.

R402.4.5 Recessed lighting. Recessed luminaires installed in the building thermal envelope shall be sealed to limit air leakage between conditioned and unconditioned spaces. All recessed luminaires shall be IC-rated and labeled as having an air leakage rate

MANDATORY REQUIREMENTS (Continued)

R403.5.5 Heat traps (Mandatory). Storage water heaters not equipped with integral heat traps and having vertical pipe risers shall have heat traps installed on both the inlets and outlets. External heat traps shall consist of either a commercially available heat trap or a downward and upward bend of at least 3 ½ inches (89 mm) in the hot water distribution line and cold water line located as close as possible to the storage tank.
R403.5.6 Water heater efficiencies (Mandatory). R403.5.6.1.1 Automatic controls. Service water-heating systems shall be equipped with automatic temperature controls capable of adjustment from the lowest to the highest acceptable temperature settings for the intended use. The minimum temperature setting range shall be from 100°F to 140°F (38°C to 60°C).
R403.5.6.1.2 Shut down. A separate switch or a clearly marked circuit breaker shall be provided to permit the power supplied to electric service systems to be turned off. A separate valve shall be provided to permit the energy supplied to the main burner(s) of combustion types of service water-heating systems to be turned off.
R403.5.6.2 Water-heating equipment. Water-heating equipment installed in residential units shall meet the minimum efficiencies of Table C404.2 in Chapter 4 of the Florida Building Code, Energy Conservation, Commercial Provisions, for the type of equipment installed. Equipment used to provide heating functions as part of a combination system shall satisfy all stated requirements for the appropriate water-heating category. Solar water heaters shall meet the criteria of Section R403.5.6.2.1.
R403.5.6.2.1 Solar water-heating systems. Solar systems for domestic hot water production are rated by the annual solar energy factor of the system. The solar energy factor of a system shall be determined from the Florida Solar Energy Center Directory of Certified Solar Systems. Solar collectors shall be tested in accordance with ISO Standard 9806, Test Methods for Solar Collectors, and SRCC Standard TM-1, Solar Domestic Hot Water System and Component Test Protocol. Collectors in installed solar water-heating systems should meet the following criteria: 1. Be installed with a tilt angle between 10 degrees and 40 degrees of the horizontal; and 2. Be installed at an orientation within 45 degrees of true south.
R403.6 Mechanical ventilation (Mandatory). The building shall be provided with ventilation that meets the requirements of the Florida Building Code, Residential, or Florida Building Code, Mechanical, as applicable, or with other approved means of ventilation including: Natural, Infiltration or Mechanical means. Outdoor air intakes and exhausts shall have automatic or gravity dampers that close when the ventilation system is not operating.
R403.6.1 Whole-house mechanical ventilation system fan efficacy. When installed to function as a whole-house mechanical ventilation system, fans shall meet the efficacy requirements of Table R403.6.1.
Exception: Where an air handler that is integral to tested and listed HVAC equipment is used to provide whole-house mechanical ventilation, the air handler shall be powered by an electronically commutated motor.
R403.6.2 Ventilation Air. Residential buildings designed to be operated at a positive indoor pressure or for mechanical ventilation shall meet the following criteria:
 The design air change per hour minimums for residential buildings in ASHRAE 62.2, Ventilation for Acceptable Indoor Air Quality, shall be the maximum rates allowed for residential applications.
No ventilation or air-conditioning system make-up air shall be provided to conditioned space from attics, crawlspaces, attached enclosed garages or outdoor spaces adjacent to swimming pools or spas.
3. If ventilation air is drawn from enclosed space(s), then the walls of the space(s) from which air is drawn shall be insulated to a minimum of R-11 and the ceiling shall be insulated to a minimum of R-19, space permitting, or R-10 otherwise.
R403.7 Heating and cooling equipment. R403.7.1 Equipment sizing (Mandatory). Heating and cooling equipment shall be sized in accordance with ACCA Manual S based on the equipment loads calculated in accordance with ACCA Manual J or other approved heating and cooling calculation methodologies, based on building loads for the directional orientation of the building. The manufacturer and model number of the outdoor and indoor units (if split system) shall be submitted along with the sensible and total cooling capacities at the design conditions described in Section R302.1. This Code does not allow designer safety factors, provisions for future expansion or other factors that affect equipment sizing. System sizing calculations shall not include loads created by local intermittent mechanical ventilation such as standard kitchen and bathroom exhaust systems. New or replacement heating and cooling equipment shall have an efficiency rating equal to or greater than the minimum required by federal law for the geographic location where the equipment is installed.

MANDATORY REQUIREMENTS (Continued)

TABLE R403.6.1 WHOLE-HOUSE MECHANICAL VENTILATION SYSTEM FAN EFFICACY

FAN LOCATION	AIRFLOW RATE MINIMUM (CFM)	MINIMUM EFFICACY ^a (CFM/WATT)	AIRFLOW RATE MAXIMUM (CFM)
HRV or ERV	Any	1.2 cfm/watt	Any
Range hoods	Any	2.8 cfm/watt	Any
In-line fan	Any	2.8 cfm/watt	Any
Bathroom, utility room	10	1.4 cfm/watt	<90
Bathroom, utility room	90	2.8 cfm/watt	Any

For SI: 1 cfm = 28.3 L/min.

R403.7.1.1 Cooling equipment capacity. Cooling only equipment shall be selected so that its total capacity is not less than the calculated total load but not more than 1.15 times greater than the total load calculated according to the procedure selected in Section R403.7, or the closest available size provided by the manufacturer's product lines. The corresponding latent capacity of the equipment shall not be less than the calculated latent load.

The published value for AHRI total capacity is a nominal, rating-test value and shall not be used for equipment sizing. Manufacturer's expanded performance data shall be used to select cooling-only equipment. This selection shall be based on the outdoor design dry-bulb temperature for the load calculation (or entering water temperature for water-source equipment), the blower CFM provided by the expanded performance data, the design value for entering wet-bulb temperature and the design value for entering dry-bulb temperature.

Design values for entering wet-bulb and dry-bulb temperatures shall be for the indoor dry bulb and relative humidity used for the load calculation and shall be adjusted for return side gains if the return duct(s) is installed in an unconditioned space.

Exceptions:

- 1. Attached single- and multiple-family residential equipment sizing may be selected so that its cooling capacity is less than the calculated total sensible load but not less than 80 percent of that load.
- 2. When signed and sealed by a Florida-registered engineer, in attached single- and multiple-family units, the capacity of equipment may be sized in accordance with good design practice.

R403.7.1.2 Heating equipment capacity.

R403.7.1.2.1 Heat pumps. Heat pump sizing shall be based on the cooling requirements as calculated according to Section R403.7.1.1, and the heat pump total cooling capacity shall not be more than 1.15 times greater than the design cooling load even if the design heating load is 1.15 times greater than the design cooling load.
R403.7.1.2.2 Electric resistance furnaces. Electric resistance furnaces shall be sized within 4 kW of the design requirements calculated according to the procedure selected in Section R403.7.1.
R403.7.1.2.3 Fossil fuel heating equipment. The capacity of fossil fuel heating equipment with natural draft atmospheric burners shall not be less than the design load calculated in accordance with Section R403.7.1.
 R403.7.1.3 Extra capacity required for special occasions. Residences requiring excess cooling or heating equipment capacity on an intermittent basis, such as anticipated additional loads caused by major entertainment events, shall have equipment sized or controlled to prevent continuous space cooling or heating within that space by one or more of the following options: A separate cooling or heating system is utilized to provide cooling or heating to the major entertainment areas. A variable capacity system sized for optimum performance during base load periods is utilized.
R403.8 Systems serving multiple dwelling units (Mandatory). Systems serving multiple dwelling units shall comply with Sections C403 and C404 of the Florida Building Code, Energy Conservation—Commercial Provisions in lieu of Section R403.
R403.9 Snow melt and ice system controls (Mandatory). Snow- and ice-melting systems, supplied through energy service to the building, shall include automatic controls capable of shutting off the system when the pavement temperature is above 50°F (10°C), and no precipitation is falling and an automatic or manual control that will allow shutoff when the outdoor temperature is above 40°F (4.8°C).
403.10 Pools and permanent spa energy consumption (Mandatory). The energy consumption of pools and permanent spas shall be in accordance with Sections R403.10.1 through R403.10.5.
R403.10.1 Heaters. The electric power to heaters shall be controlled by a readily accessible on-off switch that is an integral part of the heater mounted on the exterior of the heater, or external to and within 3 feet (914 mm) of the heater. Operation of such switch shall not change the setting of the heater thermostat. Such switches shall be in addition

to a circuit breaker for the power to the heater.

Gas-fired heaters shall not be equipped with continuously burning ignition pilots.

a. When tested in accordance with HVI Standard 916

MANDATORY REQUIREMENTS (Continued) ☐ R403.10.2 Time switches. Time switches or other control methods that can automatically turn off and on according to a preset schedule shall be installed for heaters and pump motors. Heaters and pump motors that have built-in time switches shall be in compliance with this section.

Exceptions:

- 1. Where public health standards require 24-hour pump operation.
- 2. Pumps that operate solar- and waste-heat-recovery pool heating systems
- 3. Where pumps are powered exclusively from on-site renewable generation.

R403.10.3 Covers. Outdoor heated swimming pools and outdoor permanent spas shall be equipped with a vapor-retardant cover on or at the water surface or a liquid cover or other means proven to reduce heat loss.

Exception:Where more than 70 percent of the energy for heating, computed over an operation season, is from site-recovered energy, such as from a heat pump or solar energy source, covers or other vapor-retardant means shall not be required

- R403.10.4 Gas- and oil-fired pool and spa heaters. All gas- and oil-fired pool and spa heaters shall have a minimum thermal efficiency of 82 percent for heaters manufactured on or after April 16, 2013, when tested in accordance with ANSI Z 21.56. Pool heaters fired by natural or LP gas shall not have continuously burning pilot lights.
- R403.10.5 Heat pump pool heaters. Heat pump pool heaters shall have a minimum COP of 4.0 when tested in accordance with AHRI 1160, Table 2, Standard Rating Conditions-Low Air Temperature. A test report from an independent laboratory is required to verify procedure compliance. Geothermal swimming pool heat pumps are not required to meet this standard.
- R403.11 Portable spas (Mandatory). The energy consumption of electric-powered portable spas shall be controlled by the requirements of APSP-14
- R403.13 Dehumidifiers (Mandatory). If installed, a dehumidifier shall conform to the following requirements:
 - 1. The minimum rated efficiency of the dehumidifier shall be greater than 1.7 liters/ kWh if the total dehumidifier capacity for the house is less than 75 pints/day and greater than 2.38 liters/kWh if the total dehumidifier capacity for the house is greater than or equal to 75 pints/day.
 - 2. The dehumidifier shall be controlled by a sensor that is installed in a location where it is exposed to mixed house air.
 - 3. Any dehumidifier unit located in unconditioned space that treats air from conditioned space shall be insulated to a minimum of R-2.
 - 4. Condensate disposal shall be in accordance with Section M1411.3.1 of the Florida Building Code, Residential.
- R403.13.1 Ducted dehumidifiers. Ducted dehumidifiers shall, in addition to conforming to the requirements of Section R403.13, conform to the following requirements:
 - 1. If a ducted dehumidifier is configured with return and supply ducts both connected into the supply side of the cooling system, a backdraft damper shall be installed in the supply air duct between the dehumidifier inlet and outlet duct.
 - 2. If a ducted dehumidifier is configured with only its supply duct connected into the supply side of the central heating and cooling system, a backdraft damper shall be installed in the dehumidifier supply duct between the dehumidifier and central supply duct.
 - 3. A ducted dehumidifier shall not be ducted to or from a central ducted cooling system on the return duct side upstream from the central cooling evaporator coil.
 - 4. Ductwork associated with a dehumidifier located in unconditioned space shall be insulated to a minimum of R-6.

SECTION R404 ELECTRICAL POWER AND LIGHTING SYSTEMS

R404.1 Lighting equipment (Mandatory). Not less than 90 percent of the lamps in permanently installed luminaires shall have an efficacy of at least 45 lumens-per-watt or shall utilize lamps with an efficacy of not less than 65 lumens-per-watt.

R404.1.1 Lighting equipment (Mandatory). uel gas lighting systems shall not have continuously burning pilot lights.

ENERGY PERFORMANCE LEVEL (EPL) DISPLAY CARD ESTIMATED ENERGY PERFORMANCE INDEX* = 94

The lower the EnergyPerformance Index, the more efficient the home.

1724 SW Herlong St, Fort White, FL 32038, FL, 32038

1. New construction or e	existing	New (From Plans)	10.	Wall Types(2152.5 sqft.)	Insulation	Area
2. Single family or multip	ole family	Detached		. Frame - Wood, Exterior	R=13.0	1312.50 ft ²
3. Number of units, if mu	ultiple family	1		. Frame - Wood, Adjacent . N/A	R=13.0	840.00 ft ²
4. Number of Bedrooms		1		. N/A		
5. Is this a worst case?		No		Ceiling Types(844.0 sqft.)	Insulation	
Conditioned floor area Conditioned floor area			b	. Sloped ceiling under a (Vented) . N/A . N/A	R=30.0	844.00 ft ²
7. Windows** a. U-Factor: SHGC:	Description Dbl, U=0.40 SHGC=0.25	Area 39.00 ft	² 13. a	Ducts, location & insulation level	Deck R=0.0	914 ft ² R ft ²
b. U-Factor: SHGC:	N/A	ft	c			
c. U-Factor: SHGC:	N/A	ft	а	Cooling Systems . Central Unit	kBtu/hr 21.0 S	Efficiency SEER:18.00
Area Weighted Average Area Weighted Average		h: 0.500 ft 0.250				
Skylights U-Factor:(AVG) SHGC(AVG):	Description N/A N/A	Area N/A ft	_	Heating Systems . Electric Heat Pump	kBtu/hr 21.0	Efficiency HSPF:9.10
 Floor Types Slab-On-Grade Edg N/A 	e Insulation R= R=	sulation Area : 0.0 844.00 f :	ft ² a	Hot Water Systems . Electric	Cap	: 40 gallons EF: 0.920
c. N/A	R=	: 1	ft ² b	. Conservation features		
			17.	Credits		None Pstat

I certify that this home has complied with the Florida Energy Efficiency Code for Building Construction through the above energy saving features which will be installed (or exceeded) in this home before final inspection. Otherwise, a new EPL Display Card will be completed based on installed Code compliant features.

Builder Signature: _____ Date: _____

Address of New Home: 1724 SW Herlong St City/FL Zip: Fort White, FL 32038,FL,320

*Note: This is not a Building Energy Rating. If your Index is below 70, your home may qualify for energy efficient mortgage (EEM) incentives if you obtain a Florida Energy Rating. For information about the Florida Building Code, Energy Conservation, contact the Florida Building Commission's support staff.

**Label required by Section R303.1.3 of the Florida Building Code, Energy Conservation, if not DEFAULT.



2020 - AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIA TABLE 402.4.1.1

AIR BARRIER AND INSULATION INSPECTION COMPONENT CRITERIAª

Project Name: Street: City, State, Zip: Owner: Design Location:	1724 SW Herlong St Permit	Number: ction:	CHECK
COMPONENT	AIR BARRIER CRITERIA	INSULATION INSTALLATION CRITERIA	
General requirements	A continuous air barrier shall be installed in the building envelope. The exterior thermal envelope contains a continuous air barrier. Breaks or joints in the air barrier shall be sealed.	Air-permeable insulation shall not be used as a sealing material.	
Ceiling/attic	The air barrier in any dropped ceiling/soffit shall be aligned with the insulation and any gaps in the air barrier shall be sealed. Access openings, drop down stairs or knee wall doors to unconditioned attic spaces shall be sealed.	The insulation in any dropped ceiling/soffit shall be aligned with the air barrier.	
Walls	The junction of the foundation and sill plate shall be sealed. The junction of the top plate and the top of exterior walls shall be sealed. Knee walls shall be sealed.	Cavities within corners and headers of frame walls shall be insulated by completely filling the cavity with a material having a thermal resistance of R-3 per inch minimum Exterior thermal envelope insulation for framed walls shall be installed in substantial contact and continuous alignment with the air barrier.	
Windows, skylights and doors	The space between window/door jambs and framing, and skylights and framing shall be sealed.		
Rim joists	Rim joists shall include the air barrier.	Rim joists shall be insulated.	
Floors (including above-garage and cantilevered floors)	The air barrier shall be installed at any exposed edge of insulation.	Floor framing cavity insulation shall be installed to maintain permanent contact with the underside of subfloor decking, or floor framing cavity insulation shall be permitted to be in contact with the top side of sheathing, or continuous insulation installed on the underside of floor framing and extends from the bottom to the top of all perimeter floor framing members.	
Crawl space walls	Exposed earth in unvented crawl spaces shall be covered with a Class I vapor retarder with overlapping joints taped.	Where provided instead of floor insulation, insulation shall be permanently attached to the crawlspace walls.	
Shafts, penetrations	Duct shafts, utility penetrations, and flue shafts opening to exterior or unconditioned space shall be sealed.		
Narrow cavities		Batts in narrow cavities shall be cut to fit, or narrow cavities shall be filled by insulation that on installation readily conforms to the available cavity spaces.	
Garage separation	Air sealing shall be provided between the garage and conditioned spaces.		
Recessed lighting	Recessed light fixtures installed in the building thermal envelope shall be sealed to the finished surface.	Recessed light fixtures installed in the building thermal envelope shall be air tight and IC rated.	
Plumbing and wiring		Batt insulation shall be cut neatly to fit around wiring and plumbing in exterior walls, or insulation that on installation readily conforms to available space shall extend behind piping and wiring.	
Shower/tub on exterior wall	The air barrier installed at exterior walls adjacent to showers and tubs shall separate them from the showers and tubs.	Exterior walls adjacent to showers and tubs shall be insulated.	
Electrical/phone box on exterior walls	The air barrier shall be installed behind electrical or communication boxes or air-sealed boxes shall be installed.		
HVAC register boots	HVAC supply and return register boots that penetrate building thermal envelope shall be sealed to the sub-floor, wall covering or ceiling penetrated by the boot.		
Concealed sprinklers	When required to be sealed, concealed fire sprinklers shall only be sealed in a manner that is recommended by the manufacturer. Caulking or other adhesive sealants shall not be used to fill voids voids between fire sprinkler cover plates and walls or ceilings.		

1724 SW Herlong St-Blanc...

Date: 3/13/23 By: R.G

Sanford, FL Phone: 407-450-0295

Project Information

For:

Stephanie Blanchard 1724 SW Herlong St, Fort White, FL 32038, FL 32038

Notes:

Design Information

Weather: Gainesville Regional, FL, US

Winter Design Conditions

Summer Design Conditions

Outside db Inside db	33 °F 70 °F	Outside db Inside db	92 °F 74 °F
Design TD	37 °F	Design TD Daily range	18 °F M
		Relative humidity Moisture difference	50 % 46 gr/lb

Heating Summary

Sensible Cooling Equipment Load Sizing

Structure Ducts Central vent (0 cfm) (none)	20613 0 0	Btuh Btuh Btuh	Structure Ducts Central vent (0 cfm) (none)	14398 Btuh 0 Btuh 0 Btuh
Humidification	0	Btuh Btuh	Blower	0 Btuh
Piping Equipment load	20613	Btuh	Use manufacturer's data Rate/swing multiplier	n 0.97
	Infiltration		Equipment sensible load	13995 Btuh

Method	Simplified
Construction quality	Average
Firenlaces ' '	δ 0

Heating 925

12949

0.45

Latent Cooling	Equipment Load Sizing
	4044 Dt I

0	Structure	1944	Btuh
	Ducts	0	Btuh
	Central vent (0 cfm)	0	Btuh
Cooling 925 12949	(none) Equipment latent load	1944	Btuh
0.23	Equipment Total Load (Sen+Lat)	15939	Btuh
50	Req. total capacity at 0.75 SHR	1.6	ton

Generic

Heating Equipment Summary

Cooling Equipment Summary

i rade				i rade				
Model	SEER 18.0, HSPF 9.1			Cond	SEER 18.0, H	HSPF 9.1		
AHRI ref	,			Coil	,			
				AHRI ref				
Efficiency		9.1	HSPF	Efficiency		14.7 EER, 1	8 SEER	
Heating inpu	ut			Sensible co	olina	,	15750	Btuh
Heating outp	out	20896	Btuh @ 47°F	Latent cooli	ng J		5250	Btuh
Temperature	e rise	27	°F	Total coolin			21000	Btuh
Actual air flo	W	700	cfm	Actual air flo			700	cfm
Air flow facto	or	0.034	cfm/Btuh	Air flow fact	or		0.049	cfm/Btuh
Static pressu		0.50	in H2O	Static press	ure		0.50	in H2O
Space therm	nostat			Load sensib	ole heat ratio		0.88	

Make

Capacity balance point = 31 °F

Generic

Backup:

Area (ft2) Volume (ft3)

Make

Air changes/hour Equiv. AVF (cfm)

Input = 6 kW, Output = 18944 Btuh, 100 AFUE

Calculations approved by ACCA to meet all requirements of Manual J 8th Ed.



Job: 1724 SW Herlong St-Blanchar...

3/13/23 Date: Ву: R.G

1 2 3 4 5	Expose Room	ed wall height dimensions					14.0 924.9	160. ft	e House 0 ft			24. ft	ATH 3 ft hea < 12.3 f	
	Ту	Construction number	U-value (Btuh/ft²-°F)	Or	H1 (Btul		Area (ft²) Load or perimeter (ft) (Btuh)			Area (ft²) or perimeter (ft)		Load (Btuh)		
					Heat	Cool	Gross	N/P/S	Heat	Cool	Gross	N/P/S	Heat	Cool
6	W W G G D	12C-0sw 11N0 12C-0sw 12C-0sw 4A4-2ov 4A4-2ov 11N0 12C-0sw 4A4-2ov 16B-30md 22A-tpm	0.091 0.350 0.091 0.400 0.400 0.350 0.091 0.400 0.032 1.180	ne se sw sw sw sw nw	3.35 12.88 3.35 14.72 14.72 12.88 3.35 14.72 1.18 43.42	2.34 10.74 2.34 2.34 24.95 24.95 10.74 2.34 24.12 1.73 0.00	837 37 284 837 6 18 38 284 15 925 925	799 37 284 775 0 0 38 269 0 925 160	481 949 2594 88 265 488 899 221 1089	401 663 1812 150 449 407 628 362	19 84 0 0 0 0 84	19 84 0 0 0 0 84 0 74	240 281 0 0	357 201 196 0 0 0 196 0 127 0
6	c) AED	excursion								304				-1
	Envelo	pe loss/gain							16699	8649			2454	1078
12		filtration oom ventilation							3914 0	989 0			593 0	150 0
13	Interna	I gains:	Occupants (Appliances/	@ other	230		2			460 4300	0			0 100
<u></u>	Subtota	al (lines 6 to 13)							20613	14398			3048	1328
14 15	Less ex Less tra Redistr Subtota Duct lo	ibution al					0%	0%	0 0 0 20613 0	0 0 0 14398 0	-0%	0%	0 0 -3048 0 0	0 0 -1328 0 0
		oom load uired (dim)							20613 700	14398 700			0	0 0



Job: 1724 SW Herlong St-Blanchar...

3/13/23 Date: Ву: R.G

Sario	u, FL PIK	one: 407-450-0295												
1	Room Expose								CHEN .5 ft		•		ROOM 5 ft	
3	Room	ed wall height dimensions						ft		at/cool	14.0	ft 1.0 >	hea	t/cool
4 5	Room	area	1				153.2	ft²	. 10.0 1		230.4	ft²	230.4	
	Ту	Construction number					Area (or perim	(ft²) neter (ft)	Load (Btuh)		Area (ft²) or perimeter (ft)		Load (Btuh)	
Ш					Heat	Cool	Gross	N/P/S	Heat	Cool	Gross	N/P/S	Heat	Cool
6		12C-0sw 11N0 12C-0sw 12C-0sw 4A4-2ov 4N4-2ov 11N0 12C-0sw	0.091 0.350 0.091 0.400 0.400 0.350 0.091	ne se sw sw sw sw	3.35 12.88 3.35 3.35 14.72 14.72 12.88 3.35	2.34 10.74 2.34 2.34 24.95 24.95 10.74 2.34	0 151 0 9 0	0 0 142 0 0 0	0 0 474 0 132 0 0	0 0 331 0 225 0	189 0 9	19 0 161 0 19 0	1016 240 0 540 0 132 240	201 0 377 0 225 201
	L_D 11N0 0.350 sw 12.88 10.74 12C-0sw 0.091 nw 3.35 2.34 1.72 24.12 C 16B-30md 0.032 - 1.18 1.73					24.12 1.73 0.00	153	0 153 22	180	0 266 0	0 230 230	0 230 37	0 271 1585	0 400 0
6	<u> </u>	excursion								71				70
	-	pe loss/gain							2224	1244			4026	2182
12	b) R	filtration oom ventilation							526 0	133			893 0	226
13	Interna		Occupants (Appliances/		230		0	-		0 1700	0			0 1400
\square		al (lines 6 to 13)						-	2750	3077			4919	3808
14 15	Less ex Less tra Redistr Subtota Duct lo	ibution al					-0%	0%	0 0 -2750 0 0	0 0 -3077 0 0	-0%	0%	0 0 6877 11795 0	0 0 5454 9262 0
		oom load uired (dim)							0	0			11795 401	9262 450



Job: 1724 SW Herlong St-Blanchar...

3/13/23 Date: Ву: R.G

1	Santo	ord, FL Phor	ne: 407-450-0295													
Second control contr	1 2	Room n Exposed	d wall					14.0	9.	5 ft	at/ooal	14.0	41.	3 ft	t/cool	
Part	3 4 5	Room n Room d Room a	limensions						10.3				14.3	nea < 13.5 f	t (2001	
Compared Compared		Ту		U-value (Btuh/ft²-°F)	Or			Area (or perim	ft²) neter (ft)		ad Area tuh) or peri		ft²) neter (ft)			
1						Heat	Cool	Gross	N/P/S	Heat	Cool	Gross	N/P/S	Heat	Cool	
Envelope loss/gain		W G G D G C	11N0 12C-Osw 4A4-2ov 4A4-2ov 11N0 12C-Osw 4A4-2ov 16B-30md	0.350 0.091 0.400 0.400 0.350 0.091 0.400 0.032	ne se sw sw sw sw nw nw	12.88 3.35 3.35 14.72 14.72 12.88 3.35 14.72 1.18	10.74 2.34 2.34 24.95 24.95 10.74 2.34 24.12 1.73	0 133 0 0 19 0 0 97	0 114 0 0 19 0 0 97	0 381 0 0 248 0 0 115	0 0 266 0 0 207 0 0 169	0 0 189 0 0 200 15 192	0 0 189 0 0 0 185 0	0 0 633 0 0 0 618 221 227	442 0 0 442 0 0 0 0 431 362 334 0	
12 a) Infiltration	6	c) AED 6	excursion		-		-			-	-1				118	
b) Room ventilation 0 0 0 0 0 13 14 15 15 15 15 15 15 15		Envelop	pe loss/gain					•		1156	641	-		4122	2128	
Appliances/other 200 20 20 20 20 20 20 20 20 20 20 20 20	12														255 0	
Less external load Less transfer Redistribution 14 Subtotal 15 Duct loads Less transfer 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0	13	Internal	gains:			230		0				2			460 200	
Less transfer 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0 0		Subtotal	I (lines 6 to 13)							1388	900			5131	3043	
Total room load		Less trar Redistrit Subtotal	nsfer bution I					-0%	0%	0 -1388 0	0 -900 0	-0%	0%	0 3687 8818	0 0 2093 5136 0	
															5136 250	



Job: 1724 SW Herlong St-Blanchar...

3/13/23 Date: Ву: R.G

Santo	ora, FL Ph	one: 407-450-0295												
1	Room								RY/PANTRY					
2 3	Expose Room	height					14.0	ft	0 ft hea	at/cool				
4 5	Room Room	dimensions					178.1	14.3 x	(12.5 f	t				
٦	Ty	Construction	U-value	Or	H1	ГМ		ft²)	Loa	d	Area		Loa	nd
	''	number	(Btuh/ft²-°F)	0.	(Btul	n/ft²)	or perim	neter (ft)	(Btu		or perin	neter		
					Heat	Cool	Gross	N/P/S	Heat	Cool	Gross	N/P/S	Heat	Cool
	W	12C-0sw 11N0	0.091 0.350	ne ne	3.35 12.88	2.34 10.74	4 0	4 0	12 0	8 0 467				
:	l W	12C-0sw	0.091	se	3.35	2.34	200	200	668	467				
11		12C-0sw 4A4-2ov	0.091 0.400		3.35 14.72	2.34 24.95	6	169 0 0	566 88	150				
	<u> </u> D	4A4-2ov 11N0	0.400 0.350	SW	14.72 12.88	24.95 10.74	0 0	0	0 0	395 150 0 0 0				
	₩ L_G	11N0 12C-0sw 4A4-2ov	0.091 0.400	nw	3.35 14.72	2.34 24.12	0	0 0 0	0	0				
	С	16B-30md	0.032	-	1.18	1.73	178	178	0 210	309				
	F	22A-tpm	1.180	-	43.42	0.00	178	27	1172	0				
Ì														
Ì														
_	٥١٨٢٥	L over troion					-			47				
6		excursion					-	-	0740	47		-	-	
-		pe loss/gain							2716	1376		-	ļ	-
12		filtration oom ventilation							660 0	167 0				
13	Interna	I gains:	Occupants (Appliances/	(1) Other	230		0			0 700				
	Subtota	al (lines 6 to 13)							3377	2243				
		dernal load							0	0	-			
	Less tra Redistr	ansfer							0 -3377	0 -2243				İ
14	Subtota	al					001	001	0	0				
15	Duct lo						-0%	0%	0	0			-	-
		oom load uired (cfm)							0	0				
Ь	1	- \/										L	1	



Manual S Compliance Report Entire House

Energy By Design

Sanford, FL Phone: 407-450-0295

Date: 3/13/23 By:

1724 SW Herlong St-Blanc... Job: R.G

Project Information

For: Stephanie Blanchard

1724 SW Herlong St, Fort White, FL 32038, FL 32038

Cooling Equipment

Design Conditions

Indoor RH:

Outdoor design DB:	92.2°F	Sensible gain:	14398	Btuh	Entering coil DB:	74.0°F
Outdoor design WB:	75.8°F	Latent gain:	1944	Btuh	Entering coil WB:	61.7°F
Indoor design DB:	74.0°F	Total gain:	16342	Btuh	_	

700

cfm

Estimated airflow:

Manufacturer's Performance Data at Actual Design Conditions

Equipment type: **Split ASHP**

Manufacturer: Generic Model: SEER 18.0, HSPF 9.1

Actual airflow: 700 cfm

Sensible capacity: 109% of load 15750 Btuh 270% of load Latent capacity: 5250 Btuh

50%

Total capacity: 21000 Btuh 129% of load SHR: 75%

Heating Equipment

Design Conditions

Outdoor design DB: 33.2°F Heat loss: 20613 **Btuh** Entering coil DB: 70.0°F Indoor design DB: 70.0°F

Manufacturer's Performance Data at Actual Design Conditions

Split ASHP Equipment type:

Manufacturer: Generic Model: SEER 18.0, HSPF 9.1

700 Actual airflow: cfm

31 °F 101% of load Output capacity: 20896 Btuh Capacity balance: Supplemental heat required: 0 Economic balance: -99 °F Btuh

Backup equipment type: Elec strip

Manufacturer: Model:

Actual airflow: 700 cfm

Output capacity: 5.6 kW 92% of load Temp. rise: 53 °F

Meets all requirements of ACCA Manual S.

2023-Mar-24 19:16:59

Page 1



Residential Plans Examiner Review Form for HVAC System Design (Loads, Equipment, Ducts)

Form RPER 1 15 Mar 09

Header Information


Contractor:			REQUIRED ATTA		ATTACHED
Mechanical license:		or M	ual J1 Form (and supportin J1AE Form* (and supportin I performance data (heatin	g worksheets):	Yes
Building plan #:			ual D Friction Rate Worksh	eet:	Yes No Yes No
Home address (Street or Lot#, Block,	Subdivision):	1724 SW Herlong St, En			
HVAC LOAD CALCULATION	ON (IRC M140	1.3)			
Design Conditions		Building Co	onstruction Informa	<u>tion</u>	
Winter Design Conditions Outdoor temperature: Indoor temperature: Total heat loss: Summer Design Conditions Outdoor temperature: Indoor temperature: Grains difference: Sensible heat gain:	33 70 20613 92 74 46 gr/lb @ 50% 14813	Btuh Number of Conditione Number of F F F Windows RH Eave overl Btuh Internal sh	West, South, Northeast, Northwest, So bedrooms: d floor area: f occupants: nang depth: ade:	Ooor faces North outheast, Southwest 1 925 ft² 2 0.5 ft none	Roof Eave
Latent heat gain: Total heat gain:	2000 16813			0	Depth Window
HVAC EQUIPMENT SELE Heating Equipment Data	ECTION (IRC N	M1401.3) <u>Cooling Equipment</u>	<u>Data</u>	Blower Data	
Equipment type: Furnace, Heat pump, Boiler, etc. Model: SEI Heating output capacity: Heat pumps - capacity at winter design outdoor. Aux. heating output capacity:	Split ASHP Generic ER 18.0, HSPF 9.1 0 Btuh cor conditions 18944 Btuh	Equipment type: Air Conditioner, Heat pump, of Model: Total cooling capacity: Sensible cooling capacity Latent cooling capacity	Gene SEER 18.0, HSPF 9. 0 Btu sity: 0 Btu	Cooling cfm: cric Static pressure: Fan's rated external airflow h	700 700 0.50 in H2O static pressure for design
HVAC DUCT DISTRIBUTI	ON SYSTEM I	DESIGN (IRC M1601.	1)		
Design airflow: Equipment design ESP: Total device pressure losses: Available static pressure (ASP):	700 cfm 0.50 in H2O -0.2 in H2O 0.34 in H2O	Longest supply duct: Longest return duct: Total effective length (TEL): Friction rate: Friction Rate = ASP ÷ (TEI	0 ft Tru 0 ft 0 in/100ft Bra	ct Materials Used nk duct: nch duct:	Round flex vinyl
I declare the load calculation, equipunderstand the claims made on the	oment, equipment s ese forms will be si	selection and duct design wer ubject to review and verification	e rigorously performed bas on.	sed on the building plan l	sted above. I
Contractor's printed name:					
Contractor's signature:				Date:	

Reserved for County, Town Municipality or Authority having jurisdiction use.

^{*}Home qualifies for MJ1AE Form based on Abridged Edition Checklist





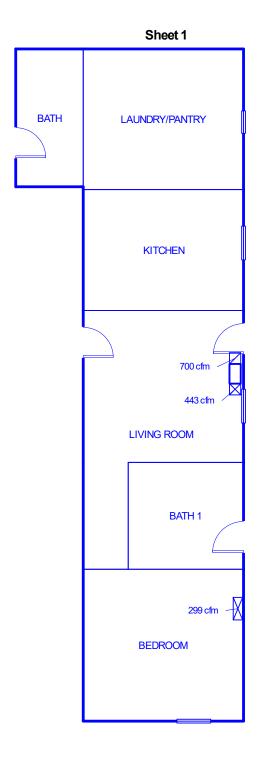

24K DUCTLESS MINI SPLIT SYSTEM. THE HEADS IN BED AND LIVING SPACES PROVIDE CFM IN CASE A MULTI HEAD UNIT IS DESIRED.

Job #: 1724 SW Herlong St-Blanchard-N Performed by R.G for:

Performed by R.G for: Stephanie Blanchard 1724 SW Herlong St Fort White, FL 32038, FL 32038 **Energy By Design**

Sanford, FL Phone: 407-450-0295 Scale: 1:102

Page 1 Right-Suite® Universal 2022 22.0.07 RSU27320 2023-Mar-24 19:16:02 ...24 SW Herlong St-Blanchard-N.rup
