

Manufacturer Data Report

HUD LABEL # FIA 326101 & FIA 326102
 M.H. ID # GD-IC-FL-1986-07859AB
 DATE MANUFACTURED 5-15-86
 MODEL # 5228-3-2 YEAR 19 86
 MFR. NAME GUERDON INDUSTRIES, INC.
 ADDRESS P.O. BOX 1100
LAKE CITY, FL 32056
 City State Zip

State of Florida
 Department of Highway Safety & Motor Vehicles
 Division of Motor Vehicles


No. Kirkman Building, 2900 Apalachee Parkway, (Room A) Tallahassee, FL 32301

DESTINATION (State) FLA ☐ Single ☒ Double ☐ Triple
 SIZE 14 X 52 14 X 52
 Unit A Unit B Unit C
☐ EXCLUDE HITCH ☒ INCLUDE HITCH

NEW DIMENSION HOMES

DEALER'S NAME
 ADDRESS 1708 280 BY PASS
PHENIX CITY, ALA. 36867
 City State Zip
 DAPIA NAME HILBORN, WERNER, CARTER, & ASS.
 ADDRESS 1627 S. MYRILE AVE.
CLEARWATER, FL 33516
 City State Zip

STRUCTURAL DESIGN BASIS CERTIFICATE

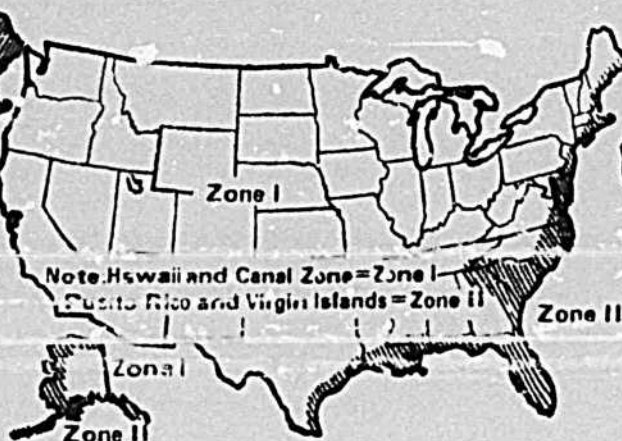

Roof Load ☐ North 40 PSF ☒ South 20 PSF ☐ Zone I 15 PSF Horizontal & 9 PSF Uplift ☒ Zone II (Hurricane) 25 PSF Horizontal & 15 PSF Uplift
☐ Middle 30 PSF ☐ Other ☐ Other

HEATING AND COOLING DESIGN BASIS CERTIFICATE



Design Winter Climate Zone

This mobile home has been thermally insulated to conform with the requirements of the Federal Mobile Home Construction and Safety Standards for all locations within climatic

☒ ZONE I ☐ ZONE II ☐ ZONE III

ALT #2	Equipment	Manufacturer	Model Designation	Equipment	Manufacturer	Model Designation
	Air Conditioning (N/A BTU/hr.)			Clothes Washer		
	Comfort Heating (54,400 BTU/hr.)	INERTHERM	MCH-068A	Clothes Dryer		
	Cooking Range	MAGIC CHEF	U31FA-7	Dishwasher	GEN. ELECT.	GSD500D-03AW
	Built-In Oven			Food Waste		
	Counter-Top Cooking Unit			Water Heater	STATE	SCI30LHSIK
	Refrigerator	GEN. ELECT.	TBF16SCB	Smoke Detector	PRODE	201

The heating equipment has the capacity to maintain an average 70° F temperature in this home at outdoor temperatures of 0° F. To maximize furnace operating economy, and to conserve energy, it is recommended that this home be installed where the outdoor winter design temperature (97 1/2° F) is not higher than 21° F. The above information has been calculated assuming a maximum wind velocity of 15 MPH at standard atmospheric pressure. The supply air distribution system installed in this home is sized ☐ Not designed for A/C ☒ A/C Ready ☐ A/C Installed

Manufacturer shall provide the minimum BTU requirements for heating and cooling or the "U" factors as designated below.

Walls (without windows & doors)	"U" = .1273	Floors	"U" = .0915	Air ducts installed outside the home	"U" = .2304
Ceilings & roofs of light color	"U" = .1273	Air ducts in floor	"U" = .1541	Heat transfer area to outside of home from air ducts	
Ceilings & roofs of dark color	"U" = .0940	Air ducts in ceiling	"U" = 0	Located: Inside Home Sq Ft 98 Outside Home Sq Ft 37	

This mobile home is designed to comply with the Federal Mobile Home Construction and Safety Standards in force at the time of manufacturer.

SIGNED Margaret A. Mathis MARGARET A. MATHIS
 Authorized Representative of Manufacturer Type or Print Name

5-15-86
 Date

JUN 16 1986

FOR TALLAHASSEE CENTRAL OFFICE USE ONLY

RED TAG # _____ DISTRICT _____
 COMPLAINTS NAME _____
 ADDRESS _____ City _____ State _____ Zip _____
 DISTRICT _____
