

DHSMV-V-MH8
(1-81)

HUD LABEL # 217294+217295

M.H. ID OR SERIAL # FLFL2(AB)D1933-

DATE ASSIGNED OR NFRD 5-10-83 5649

MAKE OF MODEL Barrington YEAR: 1983

MFR. NAME Fleetwood Homes of Florida, Inc

ADDRESS P O Box 37

Haines City, FL 33844

City / State / Zip

MANUFACTURER DATA REPORT

STATE OF FLORIDA

DIVISION OF MOTOR VEHICLES

DEPARTMENT OF HIGHWAY SAFETY AND MOTOR VEHICLES

ROOM 167, NEIL KIRKMAN BLDG., 2900 APALACHEE PKWY
TALLAHASSEE, FLORIDA 32301

DESTINATION (STATE) Florida

() SINGLE (X) DOUBLE () TRIPLE

12x52 12x52

SIZE: UNIT A UNIT B UNIT C

XX EXCLUDING HITCH () INCLUDING HITCH

DEALER'S
NAME Westgate M. Manor

ADDRESS 4431 NW 13th Street
Gainesville, FL 32601

City / State / Zip


DAFIA NAME RADCO

ADDRESS P O Box 5506

Carson, California 90749

City / State / Zip

STRUCTURAL DESIGN BASIS CERTIFICATE

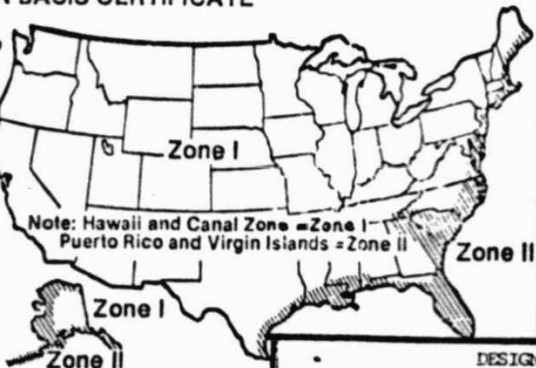

DESIGN WINTER CLIMATE ZONE

This mobile home has been thermally insulated to conform with the requirements of the Federal Mobile Home Construction and Safety Standards for all locations within climatic ☒ ZONE I ☐ ZONE II ☐ ZONE III

The heating equipment has the capacity to maintain an average 70°F temperature in this home at outdoor temperatures of NA °F.

To maximize furnace operating economy, and to conserve energy, it is recommended that this home be installed where the outdoor winter design temperature (97°F) is not higher than NA °F.

The above information has been calculated assuming a maximum wind velocity of 15 MPH at standard atmospheric pressure.

The supply air distribution system installed in this home is size () Not Designed For A/C (XX) A/C Ready () A/C Installed

MANUFACTURER SHALL PROVIDE THE MINIMUM BTU REQUIREMENTS FOR HEATING AND COOLING OR THE "U" FACTORS AS DESIGNATED BELOW.

Walls (without windows & doors)....."U"=0974
Ceilings & Roofs of Light Color....."U"=0748
Ceilings & Roofs of Dark Color....."U"=0748
Floors....."U"=0736
Air Ducts in Floor....."U"=2500
Air Ducts in Ceiling....."U"=2500
Air Ducts Installed Outside the Home....."U"=NA
Heat Transfer Area to Outside of Home from Air Ducts Located: Inside Home..Sq.Ft.84.0 Outside Home..Sq.Ft.0-

ROOF LOAD

☐ North 40 PSF
☐ Middle 30 PSF
☒ South 20 PSF
☐ Other

WIND LOAD

☒ Zone I 15 Psf Horizontal & 9 Psf Uplift
☒ Zone II (Hurricane)-25 Psf Horizontal & 15 Psf Uplift
☐ Zone III Other

EQUIPMENT

	MANUFACTURER	MODEL DESIGNATION
Air Conditioning (79,800 BTU/hr.)	Not supplied with home	
Comfort Heating (48,500 BTU/hr.)	Not supplied with home	
Cooking Range	Whirlpool	RJE 3100
Built-In Oven	NA	
Counter-Top Cooking Unit	NA	
Refrigerator	Whirlpool	EHT 181 JK
Water Heater	Grund	GPX-30P6
Clothes Washer	Not supplied with home	
Clothes Dryer	Not supplied with home	
Dishwasher	Not supplied with home	
Food Waste	Not supplied with home	
Smoke Detector	Firex	FXW-1A

THIS MOBILE HOME IS DESIGNED TO COMPLY WITH THE FEDERAL MOBILE HOME CONSTRUCTION AND SAFETY STANDARDS IN FORCE AT THE TIME OF MANUFACTURER.

SIGNED: Russell Geer

DATE 5-10-83

MAY 16 1983

FOR TALLAHASSEE CENTRAL OFFICE USE ONLY**
DISTRICT:

COMPLAINANT'S
NAME

COMPLAINANT'S
ADDRESS

City / State / Zip
