


District No. 1 - Kevin Parnell
District No. 2 - Rocky Ford
District No. 3 - Robby Hollingsworth
District No. 4 - Everett Phillips
District No. 5 - Tim Murphy

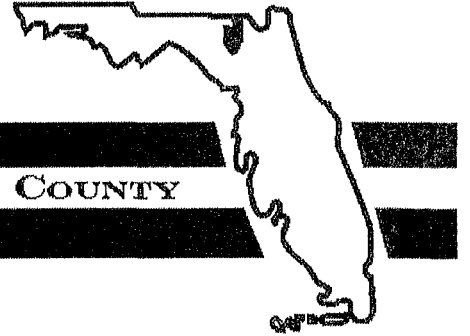

BOARD OF COUNTY COMMISSIONERS • COLUMBIA COUNTY

M E M O R A N D U M

DATE: July 27, 2026

TO: Board of County Commissioners

FROM: Erica Jones, Purchasing Officer

RE: Agenda item for August 6, 2026
P26-02-J Courthouse Landscape Renovation

On July 16, 2026 two (2) submittals were received in response to P26-02-J. The submittals were determined to be qualified meeting all of the required specifications.

Staff is recommending the Board to award P26-02-J to **Able Built LLC** and to approve the Construction Agreement.

BOARD MEETS FIRST THURSDAY AT 9:30 A.M. AND THIRD THURSDAY AT 5:30 P.M.

P.O. BOX 1529 LAKE CITY, FLORIDA 32056-1529 PHONE (386) 755-4100

CONSTRUCTION AGREEMENT

COLUMBIA COUNTY, a political subdivision of the State of Florida, by and through its Board of County Commissioners, situated at 135 NE Hernando Avenue, Suite 203, Lake City, Florida 32056- 1529 (the "County"), hereby enters into this Construction Agreement on this 6th day of August, 2026 with Able Built LLC (the "Contractor") of 126 SW Stafford Court, Lake City, FL 32024 (address) a contractor licensed to perform all work in the State of Florida in connection with the County's Project No. P26-02-J (the "Project"), as said work is set forth in the Plans and Specifications and other Contract Documents hereafter specified (the "Work"). The designee for the Project and the Work, as referenced in this Agreement, shall be

Jonathan Mick

The County and the Contractor, for the consideration herein set forth, agree as follows:

Section 1. Contract Documents

The Contract Documents consist of this Agreement, the Exhibits described in Section 4 hereof, the Legal Advertisement, the Instructions to Bidders, the Proposal and any duly executed and issued addenda, Change Orders, Work Directive Changes, Field Orders, Work Authorizations and amendments relating thereto. All of the foregoing Contract Documents are incorporated by reference and made a part of this Agreement (all of said documents including the Agreement sometimes being referred to herein as the "Contract Documents" and sometimes as the "Agreement"). A copy of the Contract Documents shall be maintained by Contractor at the Project site at all times during the performance of the Work.

Section 2. Scope of Work

The Contractor agrees to furnish and pay for all management, supervision, financing, labor, materials, tools, fuel, supplies, utilities, equipment and services of every kind and type necessary to diligently, timely, and fully perform and complete in a good and workmanlike manner the Work required by this Agreement.

Section 3. Contract Amount

In consideration of the faithful performance by the Contractor of the covenants in this Agreement to the full satisfaction and acceptance of the County, the County agrees to pay, or cause to be paid, to Contractor the following amount (herein "Contract Amount"), in accordance with the terms of this Agreement: \$ 146,000.00 (one hundred forty six thousand dollars).

[INSERT SCHEDULE OF UNIT PRICES AS APPLICABLE]

Section 4. Exhibits Incorporated

The following documents are expressly agreed to be incorporated by reference and made a part of this Agreement:

- A. Legal Advertisement
- B. Invitation to Bid
- C. Bid Proposal with required forms
- D. Performance Bond
- E. Public Payment Bond
- F. Insurance Requirements, including certificates of insurance
- G. Form of Release and Affidavit
- H. Change Order Form
- I. Notice of Award
- J. Notice to Proceed Form
- K. Application for Payment Form
- L. Special Conditions, if any
- M. **Project Plans**
- N. _____
- O. _____
- P. _____

Section 5. Bonds

A. The Contractor shall provide Performance and Payment Bonds, in the form prescribed in the Exhibits to the Agreement, in the amount of 100% of the Contract Amount, the costs of which are to be paid by Contractor. The Performance and Payment Bonds shall be underwritten by a surety authorized to do business in the State of Florida and otherwise acceptable to the County; provided, however, the surety shall be rated as "A-" or better as to general policy holders rating and Class V or higher rating as to financial size category and the amount required shall not exceed 5% of the reported policy holder's surplus, all as reported in the most current Best Key Rating Guide, published by A.M. Best Company, Inc. of 75 Fulton Street, New York, New York 10038.

B. If the surety for any bond furnished by Contractor is declared bankrupt, becomes insolvent, its right to do business is terminated in the State of Florida, or it ceases to meet the requirements imposed by the Contract Documents, the Contractor shall, within five (5) calendar days thereafter, substitute another bond and surety, both of which shall be subject to the County's approval.

Section 6. Contract Time and Liquidated Damages

A. Time is of the essence in the performance of the Work under this Agreement. The "Commencement Date" shall be established in the Notice to Proceed to be issued by the County. The Contractor shall commence the Work within five (5) calendar days from the Commencement Date. No Work shall be performed at the Project site prior to the Commencement Date. Any Work performed by the Contractor prior to the Commencement

Date shall be at the sole risk of the Contractor. The Work shall be substantially completed within 60 calendar days from the Commencement Date. The date of substantial completion of the Work (or designated portions thereof) is the date certified by the County when construction is sufficiently complete, in accordance with the Contract Documents, so the County can occupy or utilize the Work (or designated portions thereof) for the use for which it is intended. The Work shall be fully completed and ready for final acceptance by the County within 30 calendar days from the Commencement Date (herein "Contract Time").

B. The County and the Contractor recognize that, since time is of the essence for this Agreement, the County will suffer financial loss if the Work is not substantially completed within the time specified above, as said time may be adjusted as provided for herein. Should the Contractor fail to substantially complete the Work within the time period noted above, the County shall be entitled to assess, as liquidated damages, but not as a penalty, \$500 for each calendar day thereafter until substantial completion is achieved. The Project shall be deemed to be substantially completed on the date the County issues a Substantial Completion Certificate pursuant to the terms hereof. The Contractor hereby expressly waives and relinquishes any right which it may have to seek to characterize the above noted liquidated damages as a penalty, which the parties agree represents a fair and reasonable estimate of the County's actual damages at the time of contracting if the Contractor fails to substantially complete the Work in a timely manner.

C. When any period of time is referenced by days herein, it shall be computed to exclude the first day and include the last day of such period. If the last day of any such period falls on a Saturday or Sunday or on a day made a legal holiday by the law of the applicable jurisdiction, such day shall be omitted from the computation, and the last day shall become the next succeeding day which is not a Saturday, Sunday or legal holiday.

D. Contracts for more than the simplified acquisition threshold, which is the inflation adjusted amount determined by the Civilian Agency Acquisition Council and the Defense Acquisition Regulations Council (Councils) as authorized by 41 U.S.C. 1908, must address administrative, contractual, or legal remedies in instances where contractors violate or breach contract terms, and provide for such sanctions and penalties as appropriate.

Section 7. Intent of Contract Documents and Contractor Representations

A. It is the intent of the Contract Documents to describe a functionally complete project (or portion thereof) to be constructed in accordance with the Contract Documents. Any work, materials or equipment that may reasonably be inferred from the Contract Documents as being required to produce the intended result shall be supplied whether or not specifically called for. When words which have a well-known technical or trade meaning are used to describe work, materials or equipment, such words shall be interpreted in accordance with that meaning. Reference to standard specifications, manuals or codes of any technical society, organization or association or to the laws or regulations of any governmental authority having jurisdiction over the Project, whether such reference be specific or by implication, shall mean the latest standard specification, manual, code,

law or regulation in effect at the time the Work is performed, except as may be otherwise specifically stated herein.

B. If before or during the performance of the Work, Contractor discovers a conflict, error or discrepancy in the Contract Documents, Contractor immediately shall report same to the County in writing and before proceeding with the Work affected thereby shall obtain a written interpretation or clarification from the County. Contractor shall take field measurements and verify field conditions and shall carefully compare such field measurements and conditions and other information known to Contractor with the Contract Documents before commencing any portion of the Work.

C. Drawings are intended to show general arrangements, design and extent of Work and are not intended to serve as shop drawings. Specifications are separated into divisions for convenience of reference only and shall not be interpreted as establishing divisions for the Work, trades, subcontracts, or extent of any part of the Work. In the event of a discrepancy between or among the drawings, specifications or other Contract Document provisions, Contractor shall be required to comply with the provision which is the more restrictive or stringent requirement upon the Contractor, as determined by the County.

D. In order to induce Owner to enter into this Agreement Contractor makes the following representations:

- D.1 Contractor has examined and carefully studied the Contract Documents (including those listed in Section 4) and the other related data identified in the Project Documents including "technical data."
- D.2 Contractor has visited the site and become familiar with and is satisfied as to the general, local, and site conditions that may affect cost, progress, performance or furnishing of the Work.
- D.3 Contractor is familiar with and is satisfied as to all federal, state, and local Laws and Regulations that may affect cost, progress, performance and furnishing of the Work.
- D.4 Contractor has carefully studied all reports of explorations and tests of subsurface conditions at or contiguous to site and all drawings of physical conditions in or relating to existing surface or subsurface structures at or contiguous to the site. Contractor acknowledges that Owner and County do not assume responsibility for the accuracy or completeness of information and data shown or indicated in the Contract Documents with respect to Underground Facilities at or contiguous to the site. Contractor has obtained and carefully studied (or assumes responsibility for having done so) all such additional supplementary examinations, investigations, explorations, tests, studies, and data concerning conditions (surface, subsurface, and Underground Facilities) at or contiguous to the site or otherwise which may affect cost, progress, performance, or furnishing of the Work or which relate

to any aspect of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor and safety precautions, and programs incident thereto. Contractor does not consider that any additional examinations, investigations, explorations, tests, studies, or data are necessary for the performance and furnishing of the Work at the Contract Price, within the Contract Times and in accordance with the other terms and conditions of the Contract Documents.

- D.5 Contractor is aware of the general nature of work to be performed by Owner and others at the site that relates to the Work as indicated in the Contract Documents.
- D.6. Contractor has correlated the information known to Contractor, information and observation obtained from visits to the site, reports, and drawings identified in the Contract Documents and all additional examinations, investigations, explorations, tests, studies, and data with the Contract Documents.
- D.7. Contractor has given the County written notice of all conflicts, errors, ambiguities or discrepancies that Contractor has discovered in the Contract Documents and the written resolution thereof by the County is acceptable to Contractor, and the Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.

Section 8. Investigation and Utilities

A. Contractor shall have the sole responsibility of satisfying itself concerning the nature and location of the Work and the general and local conditions, and particularly, but without limitation, with respect to the following: those affecting transportation, access, disposal, handling and storage of materials; availability and quality of labor; water and electric power; availability and condition of roads; work area; living facilities; climatic conditions and seasons; physical conditions at the work-site and the project area as a whole; topography and ground surface conditions; nature and quantity of the surface materials to be encountered; subsurface conditions; equipment and facilities needed preliminary to and during performance of the Work; and all other costs associated with such performance. The failure of Contractor to acquaint itself with any applicable conditions shall not relieve Contractor from any of its responsibilities to perform under the Contract Documents, nor shall it be considered the basis for any claim for additional time or compensation.

B. Contractor shall locate all existing roadways, railways, drainage facilities and utility services above, upon, or under the Project site, said roadways, railways, drainage facilities and utilities being referred to in this Sub-Section 8.B. as the "Utilities". Contractor shall contact the owners of all Utilities to determine the necessity for relocating or temporarily interrupting any Utilities during the construction of the Project. Contractor shall schedule and coordinate its Work

around any such relocation or temporary service interruption. Contractor shall be responsible for properly shoring, supporting and protecting all Utilities at all times during the course of the Work.

Section 9. Schedule

A. The Contractor, within ten (10) calendar days after receipt of a Notice of Award, shall prepare and submit to the County, for their review and approval, a progress schedule for the Project (herein "Progress Schedule"). The Progress Schedule shall relate to all Work required by the Contract Documents and shall: show the various activities of work in sufficient detail to demonstrate a reasonable and workable plan to complete the Project within the Contract Time; show the order and interdependence of activities and the sequence for accomplishing the Work and describe all activities in sufficient detail so that the County can readily identify the work and measure the progress on of each activity; show each activity with a beginning work date, a duration, and a monetary value; include activities for procurement fabrication, and delivery of materials, plant, and equipment, and review time for shop drawings and submittals; include milestone activities when milestones are required by the Contract Documents; and in a Project with more than one phase, adequately identify each phase and its completion date, and not allow activities to span more than one phase. The Contractor shall also submit a working plan with the Progress Schedule, consisting of a concise written description of the construction plan.

B. The County will return inadequate schedules to the Contractor for corrections and Contractor shall resubmit a corrected schedule within five (5) calendar days from the date of the County's return transmittal. The County will use the accepted Project Schedule as the baseline against which to measure the progress. However, by acceptance of the Project Schedule, the County does not endorse or otherwise certify the validity or accuracy of the activity durations or sequencing of activities.

C. The Progress Schedule shall be updated by the Contractor if there is a significant change in the planned order or duration of an activity or upon the request of the County, which shall not be requested more than [INSERT TIMES] a month. All updates to the Progress Schedule shall be subject to the County's review and approval. The County's review and approval of submitted the Progress Schedule and any required or requested updates shall be a condition precedent to the County's obligation to pay the Contractor.

Section 10. Progress Payments

A. Prior to submitting its first Application for Payment, Contractor shall submit to the County, for their review and approval, a schedule of values based upon the Contract Price, listing the major elements of the Work and the dollar value for each element. After its approval by the County, this schedule of values shall be used as the basis for the Contractor's monthly Applications for Payment. This schedule shall be updated and submitted each month to the County along with a completed and notarized copy of the Application for Payment form.

B. Prior to submitting its first Application for Payment, Contractor shall submit to the

County a complete list of all its proposed subcontractors and materialmen. The first Application for Payment shall be submitted no earlier than thirty (30) days after the Commencement Date.

C. If payment is requested on the basis of materials and equipment not incorporated into the Project, but delivered and suitably stored at the site or at another location agreed to by the County in writing, the Application for Payment shall also be accompanied by a bill of sale, invoice or other documentation warranting that the County has received the materials and equipment free and clear of all liens, charges, security interests and encumbrances, together with evidence that the materials and equipment are covered by appropriate property insurance and other arrangements to protect the County's interest therein, all of which shall be subject to the County's satisfaction.

D. Contractor shall submit its monthly Application for Payment to the County on or before the 25th day of each month for work performed during the previous month. Invoices received after the 25th day of each month shall be considered for payment as part of the next month's application. Within ten (10) calendar days after receipt of each Application for Payment, the County shall either:

- D.1 indicate his approval of the requested payment;
- D.2 indicate his approval of only a portion of the requested payment, stating in writing his reasons therefore; or
- D.3 return the Application for Payment to the Contractor indicating, in writing, the reason for refusing to approve payment.

In the event of a total denial and return of the Application for Payment by the County, the Contractor may make the necessary corrections and resubmit the Application for Payment. The County shall, within thirty (30) calendar days after County approval of an Application for Payment, pay the Contractor the amounts so approved. Provided, however, in no event shall the County be obligated to pay any amount greater than that portion of the Application for Payment approved by the County.

E. The County shall retain five percent (5%) of the gross amount of each monthly payment request or five percent (5%) of the portion thereof approved by the County for payment, whichever is less. Such sums shall be accumulated and released to Contractor with final payment.

F. Monthly payments to Contractor shall in no way imply approval or acceptance of Contractor's work.

G. Each Application for Payment shall be accompanied by a Release and Affidavit, in the form attached to this Agreement, showing that all materials, labor, equipment and other bills associated with that portion of the Work for which payment is being requested have been paid in full. The County shall not be required to make payment until and unless these affidavits are furnished by the Contractor.

H. The County reserves the right to issue joint checks to Contractor and its material suppliers, subcontractors, labor unions, equipment suppliers, etc., if, in the County's sole judgment, it is necessary to do so to ensure payment to the above named parties or if above named parties have filed a notice of nonpayment, lien or intent to lien, stop notice, etc.

Section 11. Payments Withheld

A. The County may decline to approve any Application for Payment, or portions thereof, because of subsequently discovered evidence or subsequent inspections. The County may nullify the whole or any part of any approval for payment previously issued and the County may withhold any payments otherwise due Contractor under this Agreement or any other agreement between the County and Contractor, to such extent as may be necessary in the County's opinion to protect it from loss because of:

- A.1 Defective Work not remedied;
- A.2 Third party claims filed or reasonable evidence indicating probable filing of such claims;
- A.3 Failure of Contractor to make payment properly to subcontractors or for labor, materials or equipment;
- A.4 Reasonable doubt that the Work can be completed for the unpaid balance of the Contract Amount;
- A.5 Reasonable indication that the Work will not be completed within the Contract Time;
- A.6 Unsatisfactory prosecution of the Work by the Contractor;
- A.7 Failure to provide accurate and current "As-Builts"; or
- A.8 Any other material breach of the Contract Documents.

B. If these conditions in Subsection 11.A are not remedied or removed, the County may, after three (3) days written notice, rectify the same at Contractor's expense. The County also may offset against any sums due Contractor the amount of any liquidated or unliquidated obligations of Contractor to the County, whether relating to or arising out of this Agreement or any other agreement between Contractor and the County.

Section 12. Final Payment

A. The County shall make final payment to Contractor within thirty (30) calendar days after the Work is finally inspected and accepted by the County in accordance with Section 25.B. herein, provided that Contractor first, and as an explicit condition precedent to the accrual of

Contractor's right to final payment, shall have furnished the County with a properly executed and notarized copy of the Release and Affidavit, as well as, a duly executed copy of the Surety's consent to final payment and such other documentation that may be required by the Contract Documents and the County.

B. Contractor's acceptance of final payment shall constitute a full waiver of any and all claims by Contractor against the County arising out of this Agreement or otherwise relating to the Project, except those previously made in writing and identified by parties as unsettled at the time of the final Application for Payment. Neither the acceptance of the Work nor payment by the County shall be deemed to be a waiver of the County's right to enforce any obligations of Contractor hereunder or to the recovery of damages for defective Work not discovered by the County at the time of final inspection.

Section 13. Submittals and Substitutions

A. Contractor shall carefully examine the Contract Documents for all requirements for approval of materials to be submitted such as a schedule of values, safety manual, shop drawings, data, test results, schedules and samples. Contractor shall submit all such materials at its own expense and in such form as required by the Contract Documents in sufficient time to prevent any delay in the delivery of such materials and the installation thereof.

B. Whenever materials or equipment are specified or described in the Contract Documents by using the name of a proprietary item or the name of a particular supplier, the naming of the item is intended to establish the type, function and quality required. Unless the name is followed by words indicating that no substitution is permitted, materials or equipment of other suppliers may be accepted by the County if sufficient information is submitted by Contractor to allow the County to determine that the material or equipment proposed is equivalent or better than to that named. Requests for review of substitute items of material and equipment will not be accepted by the County from anyone other than Contractor and all such requests must be submitted by Contractor to the County within thirty (30) calendar days after Notice of Award is received by Contractor.

C. If Contractor wishes to furnish or use a substitute item of material or equipment, Contractor shall make application to the County for acceptance thereof, certifying that the proposed substitute shall perform adequately the functions and achieve the results called for by the general design, be similar and of equal substance to that specified and be suited to the same use as that specified. The application shall state that the evaluation and acceptance of the proposed substitute will not prejudice Contractor's achievement of substantial completion on time, whether or not acceptance of the substitute for use in the Work will require a change in any of the Contract Documents (or in the provisions of any other direct contract with the County for the Project) to adapt the design to the proposed substitute and whether or not incorporation or use of the substitute in

connection with the Work is subject to payment of any license fee or royalty. All variations of the proposed substitute from that specified will be identified in the application and available maintenance, repair and replacement service shall be indicated. The application also shall contain an itemized estimate of all costs that will result, directly or indirectly, from acceptance of such substitute, including costs for redesign and claims of other contractors affected by the resulting change, all of which shall be considered by the County in evaluating the proposed substitute. The County may require Contractor to furnish at Contractor's expense additional data about the proposed substitute.

D. If a specific means, method, technique, sequence or procedure of construction is indicated in or required by the Contract Documents, Contractor may furnish or utilize a substitute means, method, sequence, technique or procedure of construction acceptable to the County, if Contractor submits sufficient information to allow the County to determine that the substitute proposed is equivalent to that indicated or required by the Contract Documents. The procedures for submission to and review by the County shall be the same as those provided herein for substitute materials and equipment.

E. The County shall be allowed a reasonable time within which to evaluate each proposed substitute. The County shall be the sole judge of acceptability, and no substitute will be ordered, installed or utilized without the County's prior written acceptance which shall be evidenced by either a Change Order or an approved Shop Drawing. The County may require Contractor to furnish at Contractor's expense a special performance guarantee or other surety with respect to any substitute.

Section 14. Daily Reports, As-Built and Meetings

A. Unless waived in writing by the County, Contractor shall complete, maintain, and submit to County on a N/A basis a daily log of the Contractor's work in a format approved by the County. The daily log shall document all activities of Contractor at the Project site including, but not limited to, the following:

- A1. Weather conditions showing the high and low temperatures during work hours, the amount of precipitation received on the Project site, and any other weather conditions which adversely affect the Work;
- A2. Any Conditions which adversely affect the Work;
- A3. The hours of operation by Contractor's and subcontractor's personnel;
- A4. The number of Contractor's and subcontractor's personnel present and working at the Project site, by subcontract and trade;

- A5. All equipment present at the Project site, description of equipment use and designation of time equipment was used (specifically indicating any down time);
- A.6. Description of Work being performed at the Project site;
- A.7. Any unusual or special occurrences at the Project site;
- A.8. Materials received at the Project site;
- A.9. A list of all visitors to the Project site; and
- A.10. Any problems that might impact either the cost or quality of the Work or the time of performance.

The daily log shall not constitute nor take the place of any notice required to be given by Contractor to the County pursuant to the Contract Documents.

B. Contractor shall maintain in a safe place at the Project site one record copy of the Contract Documents, including, but not limited to, all drawings, specifications, addenda, amendments, Change Orders, Work Directive Changes and Field Orders, as well as all written interpretations and clarifications issued by the County, in good order and annotated to show all changes made during construction. The annotated drawings shall be continuously updated by the Contractor throughout the prosecution of the Work to accurately reflect all field changes that are made to adapt the Work to field conditions, changes resulting from Change Orders, Work Directive Changes and Field Orders, and all concealed and buried installations of piping, conduit and utility services. All buried and concealed items, both inside and outside the Project site, shall be accurately located on the annotated drawings as to depth and in relationship to not less than two (2) permanent features (e.g. interior or exterior wall faces). The annotated drawings shall be clean and all changes, corrections and dimensions shall be given in a neat and legible manner in a contrasting color. The "As-Built" record documents, together with all approved samples and a counterpart of all approved shop drawings shall be available to County for reference. Current and accurate "As-Built" record documents shall be submitted with each Application for Payment. Failure to provide current and accurate "As-Built" record drawings shall be reason for rejecting the Application for Payment. Upon completion of the Work and as a condition precedent to Contractor's entitlement to final payment, these "As-Built" record documents, samples and shop drawings shall be delivered to the County by Contractor for the County.

C. Contractor shall keep all records and supporting documentation which concern or relate to the Work hereunder for a minimum of five (5) years from the date of termination of this Agreement or the date the Project is completed, whichever is later. The County, or any duly authorized agents or representatives of the County, shall have the right to audit, inspect and copy all such records and documentation as often as they deem necessary during the period of this Agreement

and during the five (5) year period noted above; provided, however, such activity shall be conducted only during normal business hours.

D. In addition to other requirements provided herein, Contractor shall:

D1. Keep and maintain public records that ordinarily and necessarily would be required by the County in order to perform the Work.

D2. Provide the public with access to public records on the same terms and conditions that the County would provide the records and at a cost that does not exceed the cost provided in this chapter or as otherwise provided by law.

D3. Ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law.

D4. Meet all requirements for retaining public records and transfer, at no cost, to the County all public records in possession of the Contractor upon termination of the Contract and destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. All records stored electronically must be provided to the County in a format that is compatible with the information technology systems of the County.

D5. If the Contractor does not comply with a public records request, the County may terminate this Contract in accordance with Section 23 hereof.

Section 15. Independent Contractor

Contractor is an independent contractor and shall, at its sole cost and expenses and without increase in the contract price, comply with all laws, rules, ordinances, and regulations of all governing bodies having jurisdiction over the Work. Contractor shall be responsible for securing timely inspections and approvals of its work from all such authorities and as required by the Contract Documents. Contractor shall obtain and pay for all necessary permits and licenses, including business licenses; pay all fees, manufacturer's taxes, sales taxes, use taxes, processing taxes, and all federal and state taxes, insurance and contributions for social security and unemployment or disability insurance, which are measured by wages, salaries, or other remunerations paid to Contractor's employees, whether levied under existing or subsequently enacted laws, rules, or regulations. Contractor shall maintain proof that it has complied with all aspects of the foregoing provision and shall make such proof available for review by the County at County's request.

Section 16. Contractor Performance, Extensions, and No Damages for Delay of Work

A. Contractor shall diligently pursue the completion of the Work and coordinate the Work being done on the Project by its subcontractors and materialmen, as well as coordinating its Work with all work of others at the Project Site, so that its Work or the work of others shall not be delayed or impaired by any act or omission by Contractor. Contractor shall be solely responsible for

all construction means, methods, techniques, sequences, and procedures, as well as coordination of all portions of the Work under the Contract Documents.

B. Should Contractor be obstructed or delayed in the prosecution of or completion of the Work as a result of unforeseeable causes beyond the control of Contractor, and not due to its fault or neglect, including but not restricted to acts of God or of the public enemy, acts of government, fires, floods, epidemics, quarantine regulation, strikes or lockouts, Contractor shall notify the County in writing within forty-eight (48) hours after the commencement of such delay, stating the cause or causes thereof, or be deemed to have waived any right which Contractor may have had to request a time extension.

C. No interruption, interference, inefficiency, suspension or delay in the commencement or progress of the Work from any cause whatever, including those for which the County may be responsible, in whole or in part, shall relieve Contractor of his duty to perform or give rise to any right to damages or additional compensation from the County. Contractor expressly acknowledges and agrees that it shall receive no damages for delay. Contractor's sole remedy, if any, against the County will be the right to seek an extension to the Contract Time; provided, however, the granting of any such time extension shall not be a condition precedent to the aforementioned "No Damage For Delay" provision. This paragraph shall expressly apply to claims for early completion, as well as to claims based on late completion.

Section 17. Changes in the Work

A. The County shall have the right at any time during the progress of the Work to increase or decrease the Work. Promptly after being notified of a change, Contractor shall submit an itemized estimate of any cost or time increases or savings it foresees as a result of the change. Except in an emergency endangering life or property, or as expressly set forth herein, no addition or changes to the Work shall be made except upon written order of the County, and the County shall not be liable to the Contractor for any increased compensation without such written order. No officer, employee or agent of the County is authorized to direct any extra or changed work orally.

B. A Change Order, in the form attached to this Agreement, shall be issued and executed promptly after an agreement is reached between Contractor and the County concerning the requested changes. Contractor shall promptly perform changes authorized by duly executed Change Orders. The Contract Amount and Contract Time shall be adjusted in the Change Order in the manner as the County and Contractor shall mutually agree.

C. If the County and Contractor are unable to agree on a Change Order for the requested change, Contractor shall, nevertheless, promptly perform the change as directed by the County in a written Work Directive Change. In that event, the Contract Amount and Contract Time shall be adjusted as directed by the County. If Contractor disagrees with the County's adjustment determination, Contractor must make a claim pursuant to Section 18 of this Agreement or else be deemed to have waived any claim on this matter it might otherwise have had.

D. In the event a requested change results in an increase to the Contract Amount, the amount of the increase shall be limited to the Contractor's reasonable direct labor and material costs and reasonable actual equipment costs as a result of the change (including allowance for labor burden costs) plus a maximum ten percent (10%) markup for all overhead and profit. In the event such change Work is performed by a Subcontractor, a maximum ten percent (10%) markup for all overhead and profit for all Subcontractors' and sub-subcontractors' direct labor and material costs and actual equipment costs shall be permitted, with a maximum five percent (5%) markup thereon by the Contractor for all of its overhead and profit, for a total maximum markup of fifteen percent (15%). All compensation due Contractor and any Subcontractor or sub-subcontractor for field and home office overhead is included in the markups noted above.

E. The County shall have the right to conduct an audit of Contractor's books and records to verify the accuracy of the Contractor's claim with respect to Contractor's costs associated with any Change Order.

F. The County shall have authority to order minor changes in the Work not involving an adjustment to the Contract Amount or an extension to the Contract Time exceeding his/her authority and not inconsistent with the intent of the Contract Documents. Minor changes approved by the County, whether changes to Work and or Contract Time, cumulatively may not exceed ten percent (10%) of the Work and or Original Contract Time. Such changes may be effected by Field Order or by other written order. Such changes shall be binding on the Contractor.

Section 18. Claims and Disputes

A. A Claim is a demand or assertion by one of the parties seeking an adjustment or interpretation of the terms of the Contract Documents, payment of money, extension of time or other relief with respect to the terms of the Contract Documents. The term "Claim" also includes other disputes and matters in question between the County and Contractor arising out of or relating to the Contract Documents. The responsibility to substantiate a Claim shall rest with the party making the Claim.

B. Claims by the Contractor shall be made in writing to the County within forty-eight (48) hours after the first day of the event giving rise to such Claim or else the Contractor shall be deemed to have waived the Claim. Written supporting data shall be submitted to the County within fifteen (15) calendar days after the occurrence of the event, unless the County grants additional time in writing, or else the Contractor shall be deemed to have waived the Claim. All claims shall be priced in accordance with the provisions of Subsection 17.D. County will render a formal decision on the claim in writing within fifteen (15) calendar days after receipt of the Contractor's Claim. County's written decision will be final and binding upon Contractor and unless Contractor submits a written notice to the County requesting non-binding voluntary mediation within fifteen (15) calendar days of the date of such decisions, then Contractor forever waives and relinquishes any rights to bring any future legal actions or court claims with respect to such Claim.

Non-binding Mediation shall be completed within sixty (60) days from the date of Contractor's timely submission of a written notice requesting non-binding voluntary mediation.

C. The Contractor shall proceed diligently with its performance as directed by the County, regardless of any pending Claim, action, suit or administrative proceeding, unless otherwise agreed to by the County in writing. The County shall continue to make payments in accordance with the Contract Documents during the pendency of any Claim.

Section 19. Indemnification and Insurance

A. To the fullest extent permitted by law, Contractor and its surety covenant and agree to indemnify and hold County harmless of and from any and all claims, losses, demands, causes of action and the like, including but not limited to, attorneys' fees and court costs which may be asserted against County by anyone other than Contractor, resulting from, to the extent of, or occurring in connection with the failure of Contractor or supplier of Contractor to perform all work required within the scope of this agreement in strict accordance with the contract documents.

B. To the full extent permitted by law, Contractor hereby agrees to defend and indemnify, protect and hold harmless County, its agents, employees, servants and sureties (individually the "Indemnified Party" and collectively the "Indemnified Parties") of and from any loss or damage and to reimburse the Indemnified Parties for any and all expenses, including legal fees, expert witness fees and other litigation costs to which the Indemnified Parties may be put because of:

- B.1. the liability for claims and liens for labor performed or materials used or furnished through or under Contractor for the project for which Contractor is liable due to any failure of Contractor to adhere to the terms of this agreement or any of the contract documents;
- B.2. liability to County resulting from Contractor's failure to comply with applicable licensing requirements;
- B.3. any personal injury, loss, damage or death to any person or persons (including employees, officers or agents of County, Contractor and lower tier subcontractors) and any property damage arising out of, result from, or in connection with the performance or non-performance of work required in this contract or by reason of any act, omission, fault or negligence whether active or passive of Contractor whether on the project or proceeding to or from the site, including, without limitation, any personal injury, loss, damage, death or property damage caused (or alleged to be caused) by any negligent or grossly negligent act, error or omission of any person or entity, including any Indemnified Party whether such Indemnified Party's or the person's or

entity's negligence be joint or concurrent however, Contractor shall not be required to indemnify an Indemnified Party for that party's sole negligence; or

- B.4. liability imposed upon County directly or indirectly by Contractor's failure or the failure of any of its employees to comply with any law, ordinance, rule, regulation or requirement, including, but not limited to, any Occupational Safety and Health Administration violations and any penalties, including enhancements, resulting in whole or in part by subcontractor's acts or omissions as well as the Immigration Reform and Control Act of 1986 and all rules and regulations adopted pursuant thereto.

C. To the fullest extent permitted by law, in addition to the express duty to indemnify County when there is any causal connection between Contractor's work and any injury, loss, damage, death or property damage, Contractor expressly undertakes a duty to defend County as a separate duty, independent of and broader than the duty to indemnify. The duty to defend agreed to by Contractor hereby expressly include all costs of litigation, attorney's fees, settlement costs and reasonable expenses in connection with the litigation, whether or not the claims made for loss, injury, damage or property damage are valid or groundless and regardless of whether the defense of County is maintained by the County or assumed by Contractor as long as the claims made could be causally connected to Contractor as reasonable determined by County (claims).

D. The County and Contractor agree the first \$100.00 of the Contract Amount paid by the County to Contractor shall be given as separate consideration for this indemnification and duty to defend, and any other indemnification of the County by Contractor provided for within the Contract Documents, the sufficiency of such separate consideration being acknowledged by Contractor by Contractor's execution of the Agreement. The Contractor's obligation under this provision shall not be limited in any way by the agreed upon contract price as shown in this contract or the Contractor's limit of, or lack of, sufficient insurance protection.

E. Contractor shall obtain and carry, at all times during its performance under the Contract Documents, insurance of the types and in the amounts set forth in the Insurance Requirements attached to this Agreement. All insurance policies shall be from responsible companies duly authorized to do business in the State of Florida and/or responsible risk retention group insurance companies which are registered with the State of Florida. Within fifteen (15) calendar days after Notice of Award is received by Contractor, Contractor shall provide the County with properly executed Certificates of Insurance to evidence Contractor's compliance with the insurance requirements of the Contract Documents. Said Certificates of Insurance shall be on forms approved by the County. The Certificates of Insurance shall be personally, manually signed by the authorized representatives of the insurance company/companies shown on the Certificates of Insurance, with proof that they are authorized representatives thereof. In addition, certified, true and exact copies of all insurance policies required hereunder shall be provided to the County, on a timely basis, when requested by the County.

F. The Certificates of Insurance and required insurance policies shall contain provisions that thirty (30) days prior written notice by registered or certified mail shall be given the County of any cancellation, intent not to renew, or reduction in the policies or coverages, except in the application of the aggregate limits provisions. In the event of a reduction in the aggregate limit of any policy, Contractor shall immediately take steps to have the aggregate limit reinstated to the full extent permitted under such policy.

G. All insurance coverages of the Contractor shall be primary to any insurance or self-insurance program carried by the County applicable to this Project. The acceptance by the County of any Certificate of Insurance does not constitute approval or agreement by the County that the insurance requirements have been satisfied or that the insurance policy shown on the Certificate of Insurance is in compliance with the requirements of the Contract Documents. No work shall commence at the Project site unless and until the required Certificates of Insurance are received by the County.

H. Contractor shall require each of its subcontractors to procure and maintain, until the completion of the subcontractor's work, insurance of the types and to the limits specified in the Insurance Requirements attached to this Agreement, unless such insurance requirements for the subcontractor is expressly waived in writing by the County. All liability insurance policies, other than professional liability, worker's compensation, employer's liability and business auto liability policies, obtained by Contractor to meet the requirements of the Contract Documents shall name the County and Engineer as additional insureds and shall contain severability of interest provisions. If any insurance provided pursuant to the Contract Documents expires prior to the completion of the Work, renewal Certificates of Insurance and, if requested by the County, certified, true copies of the renewal policies, shall be furnished by Contractor within thirty (30) days prior to the date of expiration.

I. Should at any time the Contractor not maintain the insurance coverages required herein, the County may terminate the Agreement or at its sole discretion shall be authorized to purchase such coverages and charge the Contractor for such coverages purchased. The County shall be under no obligation to purchase such insurance, nor shall it be responsible for the coverages purchased or the insurance company or companies used. The decision of the County to purchase such insurance coverages shall in no way be construed to be a waiver of any of its rights under the Contract Documents.

J. Contractor shall submit to the County a copy of all accident reports arising out of any injuries to its employees or those of any firm or individual to whom it may have subcontracted a portion of the Work, or any personal injuries or property damages arising or alleged to have arisen on account of any work by Contractor under the Contract Documents.

Section 20. Compliance with Laws

Contractor agrees to comply, at its own expense, with all federal, state and local laws, codes, statutes, ordinances, rules, regulations and requirements applicable to the Project, including but not

limited to those dealing with taxation, worker's compensation, equal employment and safety. If Contractor observes that the Contract Documents are at variance therewith, it shall promptly notify the County in writing.

Equal Employment Opportunity. Except as otherwise provided under 41 CFR Part 60, all contracts that meet the definition of "federally assisted construction contract" in 41 CFR Part 60-1.3 must include the equal opportunity clause provided under 41 CFR 60-1.4(b), in accordance with Executive Order 11246, "Equal Employment Opportunity" (30 FR 12319, 12935, 3 CFR Part, 1964-1965 Comp., p. 339), as amended by Executive Order 11375, "Amending Executive Order 11246 Relating to Equal Employment Opportunity," and implementing regulations at 41 CFR part 60, "Office of Federal Contract Compliance Programs, Equal Employment Opportunity, Department of Labor."

Davis-Bacon Act, as amended (40 U.S.C. 3141-3148). When required by Federal program legislation, all prime construction contracts in excess of \$2,000 awarded by non-Federal entities must include a provision for compliance with the Davis-Bacon Act (40 U.S.C. 3141-3144, and 3146-3148) as supplemented by Department of Labor regulations (29 CFR Part 5, "Labor Standards Provisions Applicable to Contracts Covering Federally Financed and Assisted Construction"). In accordance with the statute, contractors must be required to pay wages to laborers and mechanics at a rate not less than the prevailing wages specified in a wage determination made by the Secretary of Labor. In addition, contractors must be required to pay wages not less than once a week. The non-Federal entity must place a copy of the current prevailing wage determination issued by the Department of Labor in each solicitation. The decision to award a contract or subcontract must be conditioned upon the acceptance of the wage determination. The non-Federal entity must report all suspected or reported violations to the Federal awarding agency. The contracts must also include a provision for compliance with the Copeland "Anti-Kickback" Act (40 U.S.C. 3145), as supplemented by Department of Labor regulations (29 CFR Part 3, "Contractors and Subcontractors on Public Building or Public Work Financed in Whole or in Part by Loans or Grants from the United States"). The Act provides that each contractor or subrecipient must be prohibited from inducing, by any means, any person employed in the construction, completion, or repair of public work, to give up any part of the compensation to which he or she is otherwise entitled. The non-Federal entity must report all suspected or reported violations to the Federal awarding agency.

Section 21. Cleanup and Protections

A. Contractor agrees to keep the Project site clean at all times of debris, rubbish and waste materials arising out of the Work. At the completion of the Work, Contractor shall remove all debris, rubbish and waste materials from and about the Project site, as well as all tools, appliances, construction equipment and machinery and surplus materials, and shall leave the Project site clean and ready for occupancy by the County.

B. Any existing surface or subsurface improvements, including, but not limited to, pavements, curbs, sidewalks, pipes, utilities, footings, structures, trees and shrubbery, not indicated in the Contract Documents to be removed or altered, shall be protected by Contractor from damage during the prosecution of the Work. Any such improvements so damaged shall be restored by Contractor to the condition equal to that existing at the time of Contractor's commencement of the

Work.

Section 22. Assignment

Contractor shall not assign this Agreement or any part thereof, without the prior consent in writing of the County. If Contractor does, with approval, assign this Agreement or any part thereof, it shall require that its assignee be bound to it and to assume toward Contractor all of the obligations and responsibilities that Contractor has assumed toward the County.

Section 23. Permits, Licenses and Taxes

A. Pursuant to Section 218.80, F.S., the County will pay for all County permits and fees, including license fees, permit fees, impact fees or inspection fees applicable to the work. Contractor is not responsible for paying for permits issued by the County wherein the work is to be performed, but is responsible for acquiring all permits. The County may require the Contractor to deliver internal budget transfer documents to applicable County agencies when the Contractor is acquiring permits.

B. All permits, fees and licenses necessary for the prosecution of the Work which are not issued by the County shall be acquired and paid for by the Contractor.

C. Contractor shall pay any and all sales, use, or other taxes, assessments and other similar charges when due, as required by any local, state or federal law, as it pertains to the services provided herein. Contractor further agrees that it shall protect, reimburse, and indemnify the County from and assume all liability for its tax obligations under the terms of this Agreement.

Section 24. Termination for Default

A. Contractor shall be considered in material default of the Agreement and such default shall be considered cause for the County to terminate the Agreement, in whole or in part, as further set forth in this Section, if Contractor: (1) fails to begin the Work under the Contract Documents within the time specified herein; or (2) fails to properly and timely perform the Work as directed by the County or as provided for in the approved Progress Schedule; or (3) performs the Work unsuitably or neglects or refuses to remove materials or to correct or replace such Work as may be rejected as unacceptable or unsuitable; or (4) discontinues the prosecution of the Work; or (5) fails to resume Work which has been suspended within a reasonable time after being notified to do so; or (6) becomes insolvent or is declared bankrupt, or commits any act of bankruptcy; or (7) allows any final judgment to stand against it unsatisfied for more than ten (10) days; or (8) makes an assignment for the benefit of creditors; or (9) fails to obey any applicable codes, laws, ordinances, rules or regulations with respect to the Work; or (10) materially breaches any other provision of the Contract Documents.

B. The County shall notify Contractor in writing of Contractor's default(s). If the County determines that Contractor has not remedied and cured the default(s) within seven (7) calendar days

following receipt by Contractor of said written notice, then the County, at its option, without releasing or waiving its rights and remedies against the Contractor's sureties and without prejudice to any other right or remedy it may be entitled to hereunder or by law, may terminate Contractor's right to proceed under the Agreement, in whole or in part, and take possession of all or any portion of the Work and any materials, tools, equipment, and appliances of Contractor, take assignments of any of Contractor's subcontracts and purchase orders, and complete all or any portion of Contractor's Work by whatever means, method or agency which the County, in its sole discretion, may choose.

C. If the County deems any of the foregoing remedies necessary, Contractor agrees that it shall not be entitled to receive any further payments hereunder until after the Project is completed. All monies expended and all of the costs, losses, damages and extra expenses, including all management, administrative and other overhead and other direct and indirect expenses (including Engineer and attorneys' fees) or damages incurred by the County incident to such completion, shall be deducted from the Contract Amount, and if such expenditures exceed the unpaid balance of the Contract Amount, Contractor agrees to pay promptly to the County on demand the full amount of such excess, including costs of collection, attorney's fees (including appeals) and interest thereon at the maximum legal rate of interest until paid. If the unpaid balance of the Contract Amount exceeds all such costs, expenditures and damages incurred by the County to complete the Work, such excess shall be paid to the Contractor. The amount to be paid to the Contractor or the County, as the case may be, shall be approved by the County, upon application, and this obligation for payment shall survive termination of the Agreement.

D. The liability of Contractor hereunder shall extend to and include the full amount of any and all sums paid, expenses and losses incurred, damages sustained, and obligations assumed by the County in good faith under the belief that such payments or assumptions were necessary or required, in completing the Work and providing labor, materials, equipment, supplies, and other items therefore or re-letting the Work, and in settlement, discharge or compromise of any claims, demands, suits, and judgments pertaining to or arising out of the Work hereunder.

E. If, after notice of termination of Contractor's right to proceed pursuant to this Section, it is determined for any reason that Contractor was not in default, or that its default was excusable, or that the County is not entitled to the remedies against Contractor provided herein, then Contractor's remedies against the County shall be the same as and limited to those afforded Contractor under Section 24 below.

Section 24. Termination for Convenience and Right of Suspension

A. The County shall have the right to terminate this Agreement without cause upon seven (7) calendar days' written notice to Contractor. In the event of such termination for convenience, Contractor's recovery against the County shall be limited to that portion of the Contract Amount earned through the date of termination, together with any retainage withheld and reasonable termination expenses incurred, but Contractor shall not be entitled to any other or further recovery against the County, including, but not limited to, damages or any anticipated profit on portions of the Work not performed.

B. The County shall have the right to suspend all or any portions of the Work upon giving Contractor not less than two (2) calendar days' prior written notice of such suspension. If all or any portion of the Work is so suspended, Contractor's sole and exclusive remedy shall be to seek an extension of time to its schedule in accordance with the procedures set forth in the Contract Documents. In no event shall the Contractor be entitled to any additional compensation or damages. Provided, however, if the ordered suspension exceeds six (6) months, the Contractor shall have the right to terminate the Agreement with respect to that portion of the Work which is subject to the ordered suspension.

C. All contracts in excess of \$10,000 must address termination for cause and for convenience by the non-Federal entity including the manner by which it will be effected and the basis for settlement.

Section 25. Completion

A. When the entire Work (or any portion thereof designated in writing by the County) is ready for its intended use, Contractor shall notify the County in writing that the entire Work (or such designated portion) is substantially complete and request that County issue a Certificate of Substantial Completion (or Certificate of Partial Substantial Completion). Within a reasonable time thereafter, the Contractor and County shall make an inspection of the Work (or designated portion thereof) to determine the status of completion. If the County does not consider the Work (or designated portion) substantially complete, County shall notify Contractor in writing giving the reasons therefor. If the County considers the Work (or designated portion) substantially complete, County shall prepare and deliver to Contractor a Certificate of Substantial Completion (or Certificate of Partial Substantial Completion) which shall fix the date of Substantial Completion for the entire Work (or designated portion thereof) and include a tentative punchlist of items to be completed or corrected by Contractor before final payment. The County shall have the right to exclude Contractor from the Work and Project site (or designated portion thereof) after the date of Substantial Completion, but the County shall allow Contractor reasonable access to complete or correct items on the tentative punchlist.

B. Upon receipt of written certification by Contractor that the Work is completed in accordance with the Contract Documents and is ready for final inspection and acceptance and upon receipt of a final Application for Payment, County will make such inspection and, if he finds the Work acceptable and fully performed under the Contract Documents, he shall promptly issue a final Certificate for Payment, recommending that, on the basis of his observations and inspections, and the Contractor's certification that the Work has been completed in accordance with the terms and conditions of the Contract Documents, that the entire balance found to be due Contractor is due and payable. Neither the final payment nor the retainage shall become due and payable until Contractor submits: (1) the Release and Affidavit in the form attached, (2) consent of surety to final payment, and (3) if required by the County, other data establishing payment or satisfaction of all obligations, such as receipts, releases and waivers of liens, arising out of the Contract Documents, to the extent and in such form as may be designated by the County. The County reserves the right to inspect the

Work and make an independent determination as to the Work's acceptability, even though the County may have issued his recommendations. Unless and until the County is completely satisfied, neither the final payment nor the retainage shall become due and payable.

Section 26. Warranty

Contractor shall obtain and assign to the County all express warranties given to Contractor or any subcontractors by any materialmen supplying materials, equipment or fixtures to be incorporated into the Project. Contractor warrants to the County that any materials and equipment furnished under the Contract Documents shall be new unless otherwise specified, and that all Work shall be of good quality, free from all defects and in conformance with the Contract Documents. Contractor further warrants to the County that all materials and equipment furnished under the Contract Documents shall be applied, installed, connected, erected, used, cleaned and conditioned in accordance with the instructions of the applicable manufacturers, fabricators, suppliers or processors except as otherwise provided for in the Contract Documents. If, within one (1) year after final completion, any Work is found to be defective or not in conformance with the Contract Documents, Contractor shall correct it promptly after receipt of written notice from the County. Contractor shall also be responsible for and pay for replacement or repair of adjacent materials or Work which may be damaged as a result of such replacement or repair. These warranties are in addition to those implied warranties to which the County is entitled as a matter of law.

Section 27. Tests and Inspections.

A. The County, their respective representatives, agents and employees, and governmental agencies with jurisdiction over the Project shall have access at all times to the Work, whether the Work is being performed on or off of the Project site, for their observation, inspection and testing. Contractor shall provide proper, safe conditions for such access. Contractor shall provide the County with timely notice of readiness of the Work for all required inspections, tests or approvals.

B. If the Contract Documents or any codes, laws, ordinances, rules or regulations of any public authority having jurisdiction over the Project requires any portion of the Work to be specifically inspected, tested or approved, Contractor shall assume full responsibility therefore, pay all costs in connection therewith and furnish County the required certificates of inspection, testing or approval. All inspections, tests or approvals shall be performed in a manner and by organizations acceptable to the County.

C. If any Work that is to be inspected, tested or approved is covered without written concurrence from the County, such work must, if requested by County, be uncovered for observation. Such uncovering shall be at Contractor's expense unless Contractor has given County timely notice of Contractor's intention to cover the same and County has not acted with reasonable promptness to respond to such notice. If any Work is covered contrary to written directions from County, such Work must, if requested by County, be uncovered for County's observation and be replaced at Contractor's sole expense.

D. The County shall charge to Contractor and may deduct from any payments due Contractor all engineering and inspection expenses incurred by the County in connection with any overtime work. Such overtime work consisting of any work during the construction period beyond the regular eight (8) hour day and for any work performed on Saturday, Sunday or holidays.

E. Neither observations nor other actions by the County nor inspections, tests or approvals by others shall relieve Contractor from Contractor's obligations to perform the Work in accordance with the Contract Documents.

Section 28. Defective Work

A. Work not conforming to the requirements of the Contract Documents shall be deemed defective Work. If required by the County, Contractor shall, as directed, either correct all defective Work, whether or not fabricated, installed or completed, or if the defective Work has been rejected by the County, remove it from the site and replace it with conforming Work. Contractor shall bear all direct, indirect and consequential costs of such correction or removal (including, but not limited to fees and charges of engineers, architects, attorneys and other professionals) made necessary thereby, and shall hold the County harmless for same.

B. If any portion of the Work is defective, or Contractor fails to supply sufficient skilled workers with suitable materials or equipment, or fails to finish or perform the Work in such a way that the completed Work will conform to the Contract Documents, the County may order Contractor to stop the Work, or any portion thereof, until the cause for such stop in the work has been eliminated; however, this right of the County to stop the Work shall not give rise to any duty on the part of the County to exercise this right for the benefit of Contractor or any other party.

C. If Contractor fails, within a reasonable time after the written notice from the County, to correct defective Work or to remove and replace rejected defective Work as required by the County, or if Contractor fails to perform the Work in accordance with the Contract Documents, or if Contractor fails to comply with any of the provisions of the Contract Documents, the County may, after seven (7) days written notice to Contractor, correct and remedy any such deficiency.

Section 29. Supervision and Superintendents

Contractor shall plan, organize, supervise, schedule, monitor, direct and control the Work competently and efficiently, devoting such attention thereto and applying such skills and expertise as may be necessary to perform the Work in accordance with the Contract Documents. Contractor shall be responsible to see that the finished Work complies accurately with the Contract Documents. Contractor shall keep on the Work at all times during its progress a competent resident superintendent, who shall not be replaced without prior written notice to the County and Engineer except under extraordinary circumstances. The superintendent shall be Contractor's representative at the Project site and shall have authority to act on behalf of Contractor. All communications given to the superintendent shall be as binding as if given to the Contractor.

Section 30. Protection of Work

Contractor shall fully protect the Work from loss or damage and shall bear the cost of any such loss or damage until final payment has been made. If Contractor or any one for whom Contractor is legally liable is responsible for any loss or damage to the Work, or other work or materials of the County or the County's separate contractors, Contractor shall be charged with the same, and any monies necessary to replace such loss or damage shall be deducted from any amounts due Contractor.

Section 31. Emergencies

In the event of an emergency affecting the safety or protection of persons or the Work or property at the Project site or adjacent thereto, Contractor, without special instruction or authorization from the County is obligated to act to prevent threatened damage, injury or loss. Contractor shall give County written notice within forty-eight (48) hours after the occurrence of the emergency, if Contractor believes that any significant changes in the Work or variations from the Contract Documents have been caused thereby. If the County determines that a change in the Contract Documents is required because of the action taken in response to an emergency, a Change Order shall be issued to document the consequences of the changes or variations. If Contractor fails to provide the forty-eight (48) hour written notice noted above, the Contractor shall be deemed to have waived any right it otherwise may have had to seek an adjustment to the Contract Amount or an extension to the Contract Time.

Section 32. Use of Premises

Contractor shall confine all construction equipment, the storage of materials and equipment and the operations of workers to the Project site and land and areas identified in and permitted by the Contract Documents and other lands and areas permitted by law, rights of way, permits and easements, and shall not unreasonably encumber the Project site with construction equipment or other material or equipment. Contractor shall assume full responsibility for any damage to any such land or area, or to the owner or occupant thereof, or any land or areas contiguous thereto, resulting from the performance of the Work.

Section 33. Safety

A. Contractor shall be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the Work. Contractor shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury or loss to:

- A.1. All employees on the Work and other persons and/or organizations who may be affected thereby;
- A.2. All the Work and materials and equipment to be incorporated therein,

whether in storage on or off the Project site; and

- A.3. Other property on Project site or adjacent thereto, including trees, shrubs, walks, pavements, roadways, structures, utilities and any underground structures or improvements not designated for removal, relocation or replacement in the Contract Documents.

B. Contractor shall comply with all applicable codes, laws, ordinances, rules and regulations of any public body having jurisdiction for the safety of persons or property or to protect them from damage, injury or loss. Contractor shall erect and maintain all necessary safeguards for such safety and protection. Contractor shall notify owners of adjacent property and of underground structures and improvements and utility owners when prosecution of the Work may affect them, and shall cooperate with them in the protection, removal, relocation or replacement of their property. Contractor's duties and responsibilities for the safety and protection of the Work shall continue until such time as the Work is completed and final acceptance of same by the County has occurred.

C. Contractor shall designate a responsible representative at the Project site whose duty shall be the prevention of accidents. This person shall be Contractor's superintendent unless otherwise designated in writing by Contractor to the County.

Section 34. Project Meetings

Prior to the commencement of Work, the Contractor shall attend a preconstruction conference with the Engineer and others as appropriate to discuss the Progress Schedule, procedures for handling shop drawings and other submittals, and for processing Applications for Payment, and to establish a working understanding among the parties as to the Work. During the prosecution of the Work, the Contractor shall attend any and all meetings convened by the County with respect to the Project, when directed to do so by the County. Contractor shall have its subcontractors and suppliers attend all such meetings (including the preconstruction conference) as may be directed by the County.

Section 35. Notices

A. All notices required or made pursuant to this Agreement by the Contractor to the County or Engineer shall be in writing and delivered by hand or by United States Postal Service Department, first class mail, postage pre-paid, return receipt requested, or by Federal Express, addressed to the following:

County

David Kraus, Columbia County Administrator
135 NE Hernando Avenue, Suite 203
Lake City, Florida 32056-1529

With courtesy copies also provided to:

Joel F. Foreman, County Attorney Columbia County, Florida
207 S. Marion Avenue Lake City, Florida 32025

Kevin Kirby, Public Works Director Columbia County, Florida
Post Office Box 969
Lake City, Florida 32056-0969

B. All notices required or made pursuant to this Agreement by the County to Contractor shall be made in writing and shall be delivered by hand or by United States Postal Service Department, first class mail, postage pre-paid, return receipt requested, or by Federal Express, addressed to the following:

Corporate Name of Contractor: Able Built
Address (including city, state and zip): 126 SW Stafford Ct Lake city 32024

Name of person with their title and attention the notice should be sent:

Brent Williams

Telephone and Fax numbers: 386-365-4226

Email Address: brent@ablebuiltfl.com

C. Either party may change its above noted address by giving written notice to the other party in accordance with the requirements of this Section.

Section 36. Modification

No modification or change to the Agreement shall be valid or binding upon the parties unless in writing and executed by the party or parties intended to be bound by it.

Section 37. Successors and Assigns

Subject to other provisions hereof, the Agreement shall be binding upon and shall inure to the benefit of the successors and assigns of the parties to the Agreement.

Section 38. Governing Law

The Agreement shall be interpreted under and its performance governed by the laws of the

State of Florida.

Section 39. Venue

The state courts in and for Columbia County, Florida shall be the proper and sole venue for any legal action on any and all claims, disputes or other matters in controversy arising out of or relating to this Agreement, whether stated as contractual, tort, equitable, statutory or any other claims or causes of action.

Section 40. No Waiver

The failure of the County to enforce at any time or for any period of time any one or more of the provisions of the Agreement shall not be construed to be and shall not be a waiver of any such provision or provisions or of its right thereafter to enforce each and every such provision.

Section 41. Remedies Cumulative

No right or remedy in this Agreement is intended to be exclusive of any other right or remedy, but every such right or remedy shall be cumulative and shall be in addition to and not a limitation of any duties, obligations, rights and remedies otherwise imposed or available by law.

Section 42. Entire Agreement

Each of the parties hereto agrees and represents that the Agreement comprises the full and entire agreement between the parties affecting the Work contemplated, and no other agreement or understanding of any nature concerning the same has been entered into or will be recognized, and that all negotiations, acts, work performed, or payments made prior to the execution hereof shall be deemed merged in, integrated and superseded by the Agreement.

Section 43. Severability

Should any provision of the Agreement be determined by a court to be unenforceable, such a determination shall not affect the validity or enforceability of any other section or part thereof.

Section 44. Third Party Beneficiaries

It is specifically agreed between the parties executing this Agreement that it is not intended by any of the provisions of any part of the Agreement to create in the public or any member thereof, a third party beneficiary under this Agreement, or to authorize anyone not a party to this Agreement to maintain a suit for personal injuries or property damage pursuant to the terms or provisions of this Agreement.

Section 45. Public Records

IF THE CONTRACTOR HAS QUESTIONS REGARDING THE APPLICATION OF CHAPTER 119, FLORIDA STATUTES, TO THE CONTRACTOR'S DUTY TO PROVIDE PUBLIC RECORDS RELATING TO THIS CONTRACT, CONTACT THE CUSTODIAN OF PUBLIC RECORDS at bccadmin@columbiacountyfla.com or call (386) 758-1326 or P.O. Box 1529 Lake City, FL 32056.

Contractor must comply with the public records laws, Florida Statute chapter 119, specifically Contractor must:

- A. Keep and maintain public records required by the County to perform the service.
- B. Upon request from the County's custodian of public records, provide the County with a copy of the requested records or allow the records to be inspected or copied within a reasonable time at a cost that does not exceed the cost provided in chapter 119 Florida Statutes or as otherwise provided by law.
- C. Ensure that public records that are exempt or confidential and exempt from public records disclosure requirements are not disclosed except as authorized by law for the duration of the contract term and following completion of the contract if the contractor does not transfer the records to the County.
- D. Upon completion of the contract, transfer, at no cost, to the County all public records in possession of the contractor or keep and maintain public records required by the County to perform the service. If the contractor transfers all public records to the public agency upon completion of the contract, the contractor shall destroy any duplicate public records that are exempt or confidential and exempt from public records disclosure requirements. If the contractor keeps and maintains public records upon completion of the contract, the contractor shall meet all applicable requirements for retaining the public records. All records stored electronically must be provided to the public agency, upon the request from the public agency's custodian of public records, in a format that is compatible with the information technology systems of the public agency.

IN WITNESS WHEREOF, the parties have executed this Agreement on the date(s) indicated above.

CONTRACTOR: Able Built LLC
(Company Name)

ATTEST:

By: Brent Williams (Signature) Brent Williams (Printed)
Its: Owner (Title)
Date: 8.11.26

Witness:

Its: Brent Williams
President/Corporate Secretary/Witness
[Corporate Seal]

Date: 8.17.26

[Signature]
2nd Witness (if not incorporated)

OWNER: Board of County Commissioners of Columbia County, Florida

(SEAL)

Clerk:



By:


Chairman

Date:

8/6/2026

Approved as to Form and Content:

County Attorney



Joel Foreman

CERTIFICATE OF LIABILITY INSURANCE

DATE (MM/DD/YYYY)

8/14/2026

THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.

IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).

PRODUCER W.L. Hunter Insurance Agency LLC PO Box 1827 Lake City FL 32056		CONTACT NAME: PHONE (A/C, No, Ext): E-MAIL ADDRESS: wl@wlhunter.com FAX (A/C, No):	
INSURED Able Built LLC 126 SW Stafford Ct Lake City FL 32024		INSURER(S) AFFORDING COVERAGE INSURER A: Southern Owners Ins Co INSURER B: Progressive Express Ins Co INSURER C: FCBI INSURER D: INSURER E: INSURER F:	
		NAIC # 10190 10193	

COVERAGES

CERTIFICATE NUMBER:

REVISION NUMBER:

THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. *LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS. LIMITS SHOWN ARE INCLUSIVE OF AMOUNTS REQUESTED BY THE CERTIFICATE HOLDER AND MAY NOT REFLECT POLICY LIMIT AMOUNTS IN EXCESS OF THOSE REQUESTED. *Not Applicable in WY

INSR LTR	TYPE OF INSURANCE	ADDL SUBR INSR	WVD	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
A	☒ COMMERCIAL GENERAL LIABILITY			78611614	08/14/2026	08/14/2027	EACH OCCURRENCE \$ 1,000,000
	☐ CLAIMS-MADE ☒ OCCUR						DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 300,000
							MED EXP (Any one person) \$ 10,000
							PERSONAL & ADV INJURY \$ 1,000,000
	GEN'L AGGREGATE LIMIT APPLIES PER:						GENERAL AGGREGATE \$ 2,000,000
	☒ POLICY ☐ PRO-JECT ☐ LOC						PRODUCTS - COMP/OP AGG \$ 2,000,000
	OTHER:						\$
B	AUTOMOBILE LIABILITY			878479646	08/14/2026	08/14/2027	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000
	☐ ANY AUTO						BODILY INJURY (Per person) \$
	☐ OWNED AUTOS ONLY ☒ SCHEDULED AUTOS						BODILY INJURY (Per accident) \$
	☐ HIRED AUTOS ONLY ☐ NON-OWNED AUTOS ONLY						PROPERTY DAMAGE (Per accident) \$
							\$
	UMBRELLA LIAB						EACH OCCURRENCE \$
	EXCESS LIAB						AGGREGATE \$
	☐ OCCUR ☐ CLAIMS-MADE						\$
	DED RETENTION \$						\$
C	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY			106	8/12/2026	8/12/2027	PER STATUTE ☒ OTH-ER
	ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH)	Y/N	N/A				E.L. EACH ACCIDENT \$ 1,000,000
	If yes, describe under DESCRIPTION OF OPERATIONS below						E.L. DISEASE - EA EMPLOYEE \$ 1,000,000
							E.L. DISEASE - POLICY LIMIT \$ 1,000,000

DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required)

CERTIFICATE HOLDER

CANCELLATION

Columbia Co Building Dept 135 NE Hernando Ave Lake City FL 32055	SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS. AUTHORIZED REPRESENTATIVE Travis Hunter
--	--

Auto-Owners INSURANCE

LIFE • HOME • CAR • BUSINESS

BOND NUMBER: 66478560

LABOR & MATERIAL PAYMENT BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, ABLE BUILT LLC of 126 SW STAFFORD CT LAKE CITY, FL 32024-1142, as Principal, and the Auto-Owners Insurance Company, a corporation organized under the laws of the State of Michigan, and having its principal office in the city of Lansing, Michigan, as Surety, are held and firmly bound unto COLUMBIA COUNTY BOARD OF COUNTY COMMI, 135 NE HERNANDO AVE STE 203 RM 203, LAKE CITY FL 32055-4004, as Oblige, in the penal sum of one hundred forty six thousand and xx/100 Dollars (\$146,000.00), lawful money of the United States of America, for which payment, well and truly to be made, we jointly and severally bind ourselves, our successors, administrators and assigns, firmly by these presents.

WHEREAS, the aforesaid Principal has entered into a certain written contract with the aforesaid Oblige dated 16th day of July, 2026 for furnishing all labor and materials for COLUMBIA COUNTY COURT HOUSE SHRUBS, CONSTRUCTION OF A PERGOLA, REPLACE TOP SOIL, MULCH AND IRRIGATION which contract is hereby referred to and made a part hereof.

NOW, THEREFORE, THE CONDITION OF THIS OBLIGATION IS SUCH, that if the aforesaid Principal shall pay or cause to be paid all indebtedness which may arise from him to any subcontractor or to any person, firm or corporation performing labor or furnishing materials or supplies furnished in the performance of said contract then this obligation shall be void, otherwise to remain in full force and effect.

THIS BOND is further conditioned that the liability of the Surety shall not be affected by any extensions of time and notice of any such extensions of time is hereby waived by the Surety.

NON-ASSESSABLE. This bond is non-assessable and the premiums designed herein and in the endorsements attached hereto are the only premiums for which the Principal or Oblige shall be liable.

PARTICIPATING. The Principal or Oblige shall be entitled to an equitable participation in the funds of the Company in excess of the amounts required to pay expenses and all the losses or claims or other policy obligations incurred, together with the reserve and surplus funds required or permitted by law; such distribution shall be made by the Company only in accordance with the decision of the Directorate acting under the insurance laws and under the charger of the Company.

SIGNED, SEALED and DATED this 14TH day of AUGUST, 2026.

ABLE BUILT LLC

Principal

By



Auto-Owners Insurance Company

Surety

By

Teresa E. Gibson

Attorney-in-Fact

BOND NUMBER: 66478560

PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS:

That we, ABLE BUILT LLC of 126 SW STAFFORD CT LAKE CITY, FL 32024-1142 as Principal(s), hereinafter called Principal, and Auto-Owners Insurance Company, a Michigan corporation, of Lansing, Michigan, as Surety, hereinafter called Surety, are held and firmly bound unto COLUMBIA COUNTY BOARD OF COUNTY COMMI, 135 NE HERNANDO AVE STE 203 RM 203, LAKE CITY FL 32055-4004 as Obligee, hereinafter called Obligee, in the penal sum of one hundred forty six thousand and xx/100 Dollars (\$146,000.00), lawful money of the United States of America, for the payment whereof, well and truly to be made, we bind ourselves, our heirs, executors, administrators, successors and assigns, jointly and severally, firmly by these presents.

WHEREAS, the Principal has entered into a contract with the Obligee, dated the 16th day of July, 2026 for COLUMBIA COUNTY COURT HOUSE SHRUBS, CONSTRUCTION OF A PERGOLA, REPLACE TOP SOIL, MULCH AND IRRIGATION which contract and the plans and specifications are by reference made a part hereof.

NOW, THEREFORE, THE CONDITION OF THIS OBLIGATION IS SUCH, that if the above bounden Principal shall well and truly keep, do and perform each and every, all and singular, the matters and things in said contract set forth and specified to be by said Principal kept, done and performed, at the times and in the manner in said contract specified, or shall pay over, make good and reimburse to the above named Obligee, all loss and damage which said Obligee may sustain by reason of failure or default on the part of said Principal so to do, then this obligation shall be null and void; otherwise shall remain in full force and effect.

AND PROVIDED, that any alterations which may be made in the terms of the contract, or in the work to be done under it, or the giving by the Obligee of any extension of time for the performance of the contract, or an other forbearance on the part of either executors, administrators, successors, or assigns from their liability hereunder, notice to the Surety of any such alterations, extension of time or of forbearance being hereby waived.

SIGNED AND SEALED this 14TH day of AUGUST, 2026.

ABLE BUILT LLC

Principal

By



Auto-Owners Insurance Company

Surety

By

Teresa E. Gibson

Attorney-in-Fact

DATE AND ATTACH TO ORIGINAL BOND
AUTO-OWNERS INSURANCE COMPANY

LANSING, MICHIGAN
POWER OF ATTORNEY

NO. 66478560

KNOW ALL MEN BY THESE PRESENTS: That the AUTO-OWNERS INSURANCE COMPANY AT LANSING, MICHIGAN, a Michigan Corporation, having its principal office at Lansing, County of Eaton, State of Michigan, adopted the following Resolution by the directors of the Company on January 27, 1971, to wit.

"RESOLVED, That the President or any Vice President or Secretary or Assistant Secretary of the Company shall have the power and authority to appoint Attorneys-in-fact, and to authorize them to execute on behalf of the Company, and attach the seal of the Company thereto, bonds and undertakings, recognizances, contracts of indemnity, and other writings obligatory in the nature thereof. Signatures of officers and seal of Company imprinted on such powers of attorney by facsimile shall have same force and effect as if manually affixed. Said officers may at any time remove and revoke the authority of any such appointee."

Does hereby constitute and appoint Teresa E. Gibson

its true and lawful attorney(s)-in-fact, to execute, seal and deliver for and on its behalf as surety, any and all bonds and undertakings, recognizances, contracts of indemnity and other writings obligatory in the nature thereof, and the execution of such instrument(s) shall be as binding upon the AUTO-OWNERS INSURANCE COMPANY AT LANSING, MICHIGAN as fully and amply, to all intents and purposes, as if the same had been duly executed and acknowledged by its regularly elected officers at its principal office.

IN WITNESS WHEREOF, the AUTO-OWNERS INSURANCE COMPANY AT LANSING, MICHIGAN, has caused this to be signed by its authorized officer this 22nd day of December, 2023

Brandi Holly

Brandi Holly Senior Vice President

STATE OF MICHIGAN } ss.
COUNTY OF EATON }

On this 22nd day of December, 2023, before me personally came Brandi Holly, to me known, who being duly sworn, did depose and say that they are Brandi Holly, Senior Vice President of AUTO-OWNERS INSURANCE COMPANY, the corporation described in and which executed the above instrument, that they know the seal of said corporation, that the seal affixed to said instrument is such Corporate Seal, and that they received said instrument on behalf of the corporation by authority of their office pursuant to a Resolution of the Board of Directors of said corporation.

My commission expires January 26th, 2029.

Jeffrey P. Many
Jeffrey P. Many

Notary Public



STATE OF MICHIGAN } ss.
COUNTY OF EATON }

I, the undersigned First Vice President, Secretary and General Counsel of AUTO-OWNERS INSURANCE COMPANY, do hereby certify that the authority to issue a power of attorney as outlined in the above board of directors resolution remains in full force and effect as written and has not been revoked and the resolution as set forth is now in force.

Signed and sealed at Lansing, Michigan. Dated this 14th day of August, 2026.

William F. Woodbury
William F. Woodbury, First Vice President, Secretary and General Counsel





Bond Number 66478560

ACKNOWLEDGEMENT BY SURETY


STATE OF MICHIGAN

County of Eaton

On this 14TH day of AUGUST, 2026, before me personally appeared Teresa E. Gibson, known to me to be the Attorney-in-Fact of Auto-Owners Insurance Company, the corporation that executed the within instrument, and acknowledged to me that such corporation executed the same.

IN WITNESS WHEREOF, I have hereunto set my hand and affixed my official seal, at my office in the aforesaid County, the day and year in this certificate first above written.




Jeffrey P. Many

Notary Public in the State of Michigan
County of Ingham

JEFFREY P MANY
NOTARY PUBLIC-STATE OF MICHIGAN
COUNTY INGHAM
My Commission Expires Jan 26, 2029
Acting In the County of _____
